

Panel Production Sheets

Job #Philis
Standard

Philis
Level 2

Date: 02/20/19
Page: 1
Bundle 1

Panel #2 (120.9 Bf)

Start Of Panel: 0"

Studs: 2X6 x 7' 8-5/8" (#2 SPF & BTR) [8] 1' 4" o.c.



(1) Top and (1) Bottom Plates: 2X6 x 11' 0" (#2 SPF & BTR)

*** Panel Diagonal 13' 7" ***

Insert	Start	End
* L premium(2X6) Up	4' 1-3/4"	4' 8-3/4"
L CRNR(2X6) Down *	10' 5"	@ End

Bottom Plate Lap: Flush

Start	Type	End
4' 0" x 8' 0"	7/16" OSB	
4' 0" x 8' 0"	7/16" OSB	
3' 0" x 8' 0"	7/16" OSB	Flush

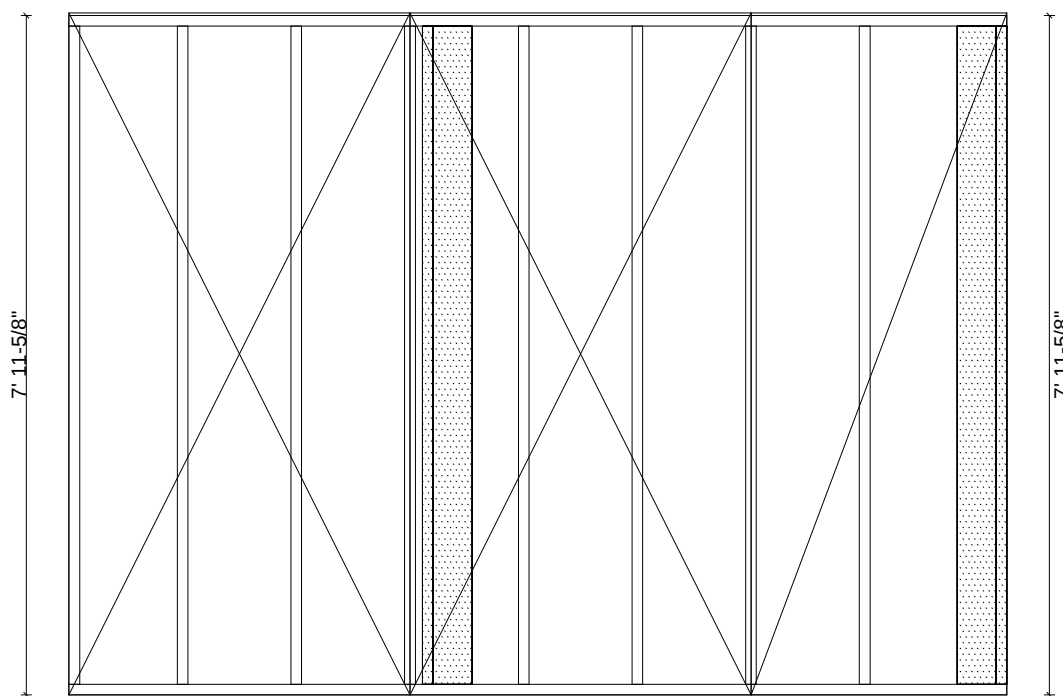

Panel Production Sheets

Job #Philis
Standard

Philis
Level 2

Date: 02/20/19
Page: 2
Bundle 1

Panel #1 (81.8 Bf)

Start Of Panel: 0"



Studs: 2X6 x 7' 8-5/8" (#2 SPF & BTR) [6] 1' 4" o.c.

(1) Top and (1) Bottom Plates: 2X6 x 8' 0" (#2 SPF & BTR)

*** Panel Diagonal 11' 3-1/2" ***

Insert	Start	End
* L CRNR(2X6) Down	@ Start	7"

Bottom Plate Lap: Flush	Start	Type	End
Flush	4' 0" x 8' 0"	7/16" OSB	
	4' 0" x 8' 0"	7/16" OSB	Flush

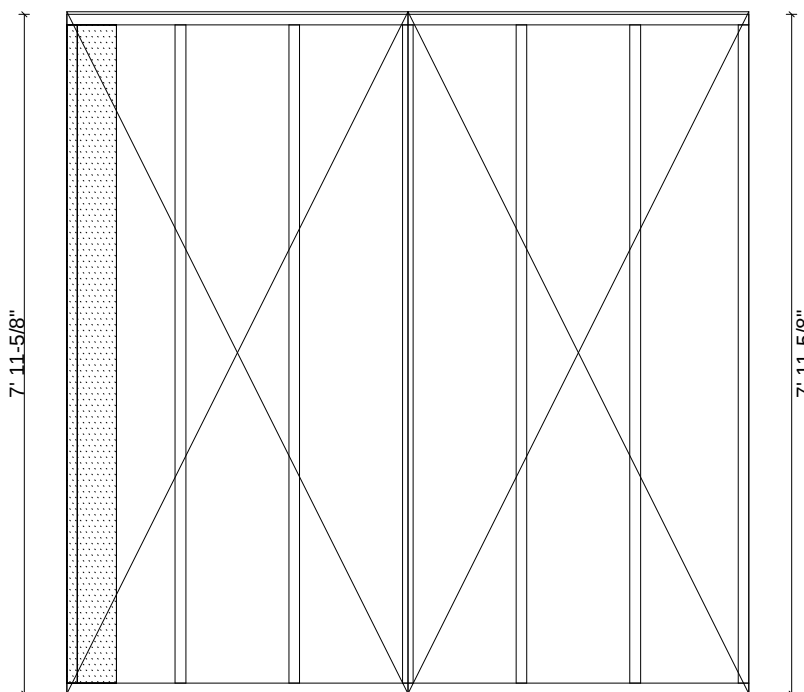

Panel Production Sheets

Job #Philis
Standard

Philis
Level 2

Date: 02/20/19
Page: 3
Bundle 1

Panel #4 (27.2 Bf)

Start Of Panel: 0"

Studs: 2X6 x 7' 8-5/8" (#2 SPF & BTR) [1] 1' 4" o.c.

(1) Top and (1) Bottom Plates: 2X6 x 1' 4" (#2 SPF & BTR)



*** Panel Diagonal 8' 0-15/16" ***

Insert	Start	End

* L CRNR(2X6) Down	@ Start	7"

Bottom Plate Lap: Flush			End
Start	Type		

Flush	1' 4" x 8' 0"	7/16" OSB	Flush



Panel Production Sheets

Job #Philis
Standard

Philis
Level 2

Date: 02/20/19
Page: 4
Bundle 1

Panel #3 (105.1 Bf)

Start Of Panel: 5-15/16"

Studs: 2X6 Sloped (#2 SPF & BTR) [2] 1' 4" o.c.

Top Plates: 2X6 (#2 SPF & BTR)

(1) 3' 10-11/16"

Start Rake Cut: 22.6 Deg /

End Rake Cut: 22.6 Deg /

TS: 3' 10-1/16"

(1) 3' 10-11/16"

Start Rake Cut: 112.6 Deg \

End Rake Cut: 112.6 Deg \

TS: 3' 10-1/16"

Bottom: (1) 2X6 x 7' 1" (#2 SPF & BTR)

Insert	Start	End
60x54-LB	1' 6-7/16"	6' 6-7/16"

Bottom Plate Lap: Flush

Start	Type	End
-------	------	-----

Extend 5-15/16"

7/16" OSB	A: * 7' 9"	B: 3"
	C: * 8' 0"	D: N.A.
	E: 7-1/8"	F: 11-5/16"
	G: 1' 6-7/16"	H: N.A.

7/16" OSB	A: N.A.	B: 4-11/16"
	C: * 4-11/16"	D: N.A.
	E: 11-5/16"	F: N.A.
	G: 11-5/16"	H: N.A.

7/16" OSB	A: * 1' 1-9/16"	B: 1' 0-1/2"
	C: * 2' 2-1/16"	D: N.A.
	E: 2' 6"	F: N.A.
	G: 2' 6"	H: N.A.

7/16" OSB	A: * 2' 2-1/16"	B: N.A.
	C: * 1' 1-9/16"	D: 1' 0-1/2"
	E: 2' 6"	F: N.A.
	G: 2' 6"	H: N.A.

Date: 02/20/19
Page: 5
Bundle 1

Panel Production Sheets

Job #Philis
Standard

Philis
Level 2

Date: 02/20/19
Page: 6
Bundle 1

Panel #5 (76.0 Bf)

Start Of Panel: 0"

Studs: 2X6 Sloped (#2 SPF & BTR) [5] 1' 4" o.c.

Top Plates: 2X6 (#2 SPF & BTR)

(1) 6' 6-5/8"

Start Rake Cut: 112.6 Deg \

End Rake Cut: 112.6 Deg \

TS: 6' 6"

Bottom: (1) 2X6 x 6' 0" (#2 SPF & BTR)

Insert	Start	End
* L CRNR(2X6) Up	@ Start	7"

Bottom Plate Lap: Flush

Start	Type	End
-------	------	-----

6-3/16" Open

3' 5-13/16" x 8' 0" 7/16" OSB

7/16" OSB	A: * 2' 2-15/16"	B: N.A.
	C: * 9-1/2"	D: 1' 5-7/16"
	E: 3' 5-13/16"	F: N.A.
	G: 3' 5-13/16"	H: N.A.

2' 0" x 8' 0" 7/16" OSB

7/16" OSB	A: * 9-1/2"	B: N.A.
	C: N.A.	D: 9-1/2"
	E: 1' 10-13/16"	F: N.A.
	G: N.A.	H: N.A.

Hold 1-3/16"

Quan.	Left Edge	Right Edge	Pitch (/12)	Angle	Top Plate Location	Bot. Plate Location
(1)	* 9' 8"	9' 7-3/8"	-5.00	-22.6	1' 4-1/2"	1' 3-1/4"
(1)	* 9' 1-3/8"	9' 0-3/4"	-5.00	-22.6	2' 9-7/8"	2' 7-1/4"
(1)	* 8' 6-11/16"	8' 6-1/16"	-5.00	-22.6	4' 3-3/16"	3' 11-1/4"
(1)	* 8' 0"	7' 11-3/8"	-5.00	-22.6	5' 8-1/2"	5' 3-1/4"
(1)	* 7' 9"	7' 8-3/8"	-5.00	-22.6	6' 4-3/8"	5' 10-1/2"

Panel #5 Continued Next Page


Panel Production Sheets

Job #Philis
Standard

Philis
Level 2

Date: 02/20/19
Page: 7
Bundle 1

Panel #5 (Continued)

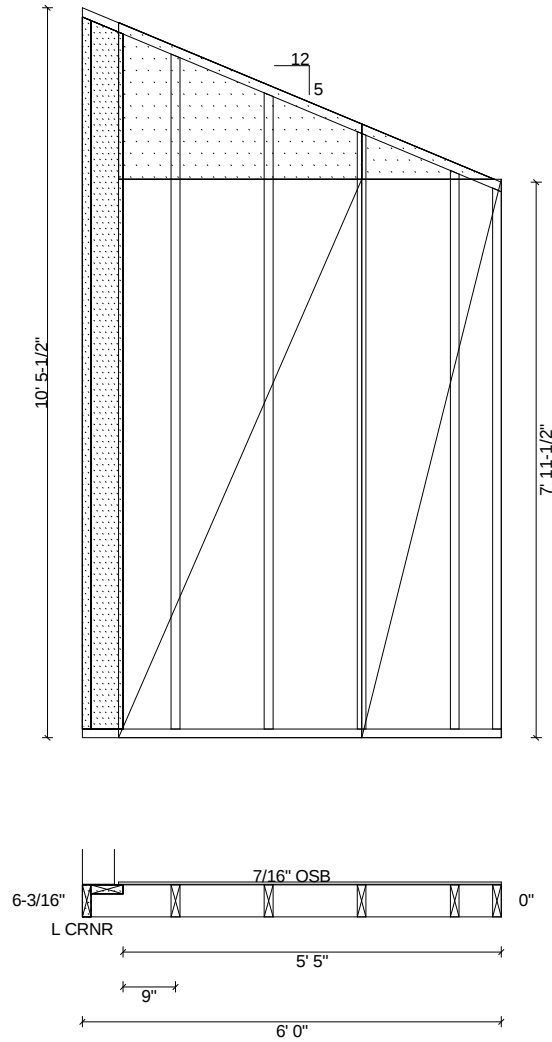

Panel Production Sheets

Job #Philis
Standard

Philis
Level 2

Date: 02/20/19
Page: 8
Bundle 1

Panel #6 (84.4 Bf)

Start Of Panel: 0"

Studs: 2X6 x 7' 8-5/8" (#2 SPF & BTR) [4] 1' 4" o.c.



(1) Top and (1) Bottom Plates: 2X6 x 5' 3" (#2 SPF & BTR)

*** Panel Diagonal 9' 6-1/2" ***

Insert	Start	End
SS	5-1/2"	8-1/2"
C premium(2X6) *	4' 8"	@ End

Bottom Plate Lap: Flush

Start	Type	End
Flush	2' 8" x 8' 0" 7/16" OSB	
	2' 0-13/16" x 8' 0" 7/16" OSB	
	6-3/16" Open	

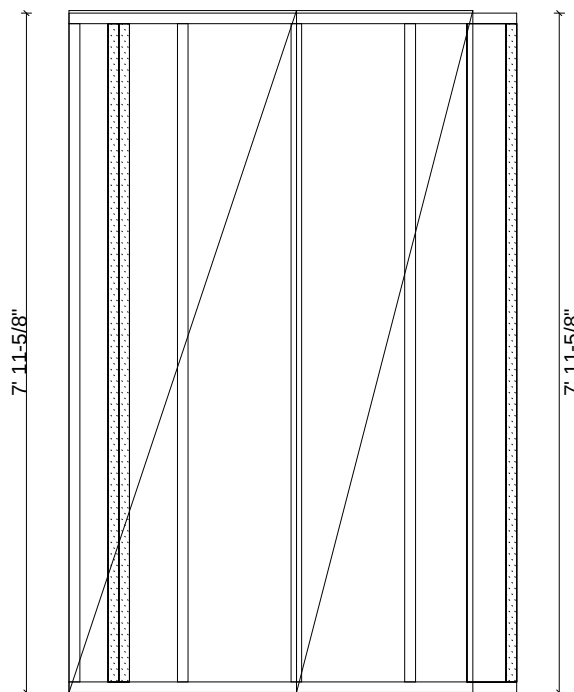

Panel Production Sheets

Job #Philis
Standard

Philis
Level 2

Date: 02/20/19
Page: 9
Bundle 1

Panel #7 (65.1 Bf)

Start Of Panel: 0"

Studs: 2X6 x 7' 8-5/8" (#2 SPF & BTR) [6] 1' 4" o.c.


(1) Top and (1) Bottom Plates: 2X6 x 6' 1-1/2" (#2 SPF & BTR)

*** Panel Diagonal 10' 0-5/8" ***

Bottom Plate Lap: Flush
Start Type

End

Flush 4' 0" x 8' 0" 7/16" OSB
2' 7-7/16" x 8' 0" 7/16" OSB Extend 5-15/16"

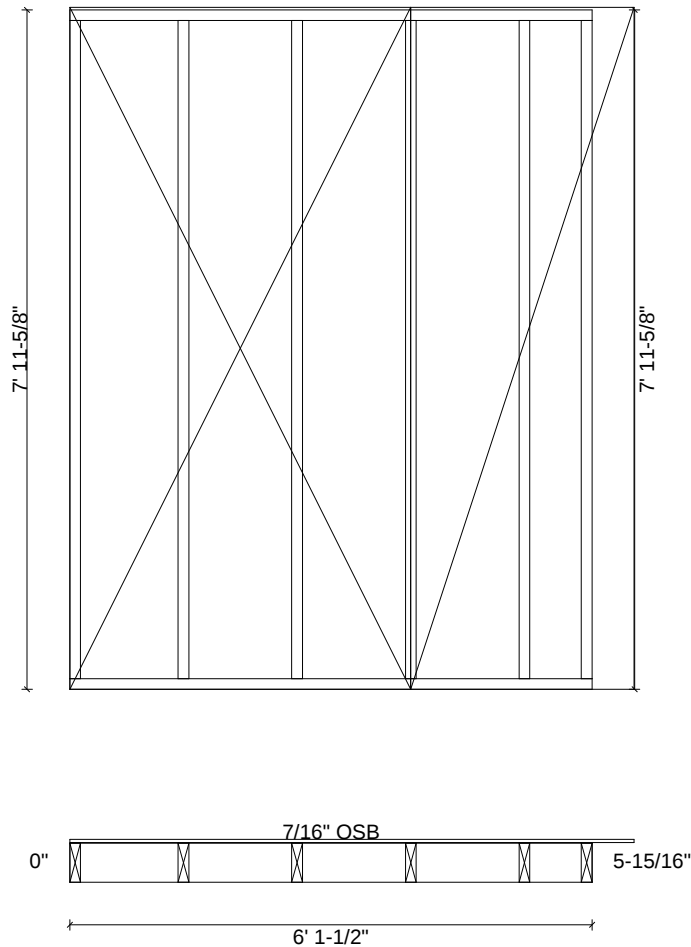

Panel Production Sheets

Job #Philis
Standard

Philis
Level 2

Date: 02/20/19
Page: 10
Bundle 1

Panel #10 (178.2 Bf)

Start Of Panel: 0"

Studs: 2X6 x 7' 8-5/8" (#2 SPF & BTR) [3] 1' 4" o.c.

(1) Top and (1) Bottom Plates: 2X6 x 9' 6-1/2" (#2 SPF & BTR)

The stud located at 9' 4" is omitted.

*** Panel Diagonal 12' 5-3/16" ***

Insert	Start	End

* L CRNR(2X6) Down	@ Start	7"
24x24-LB	1' 4"	3' 4"
30x48-LB	4' 10"	7' 4"

Bottom Plate Lap: Flush

Start	Type	End

Flush	1' 4" x 8' 0" 7/16" OSB	
	2' 0" x 8-1/2" 7/16" OSB	
	2' 0" x 4' 0" / 1' 3-1/8" 7/16" OSB	
	1' 6" x 8' 0" 7/16" OSB	
	2' 6" x 8-1/2" 7/16" OSB	
	2' 6" x 3' 3-1/8" 7/16" OSB	
	2' 8-7/16" x 8' 0" 7/16" OSB	Extend 5-15/16"

Panel #10 Continued Next Page



Panel Production Sheets

Job #Philis
Standard

Philis
Level 2

Date: 02/20/19
Page: 11
Bundle 1

Panel #10 (Continued)

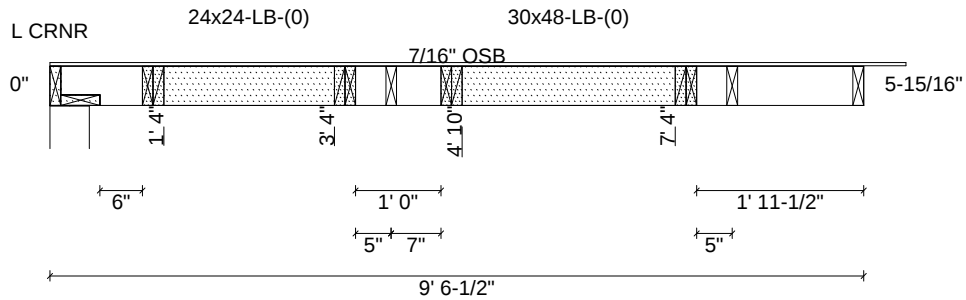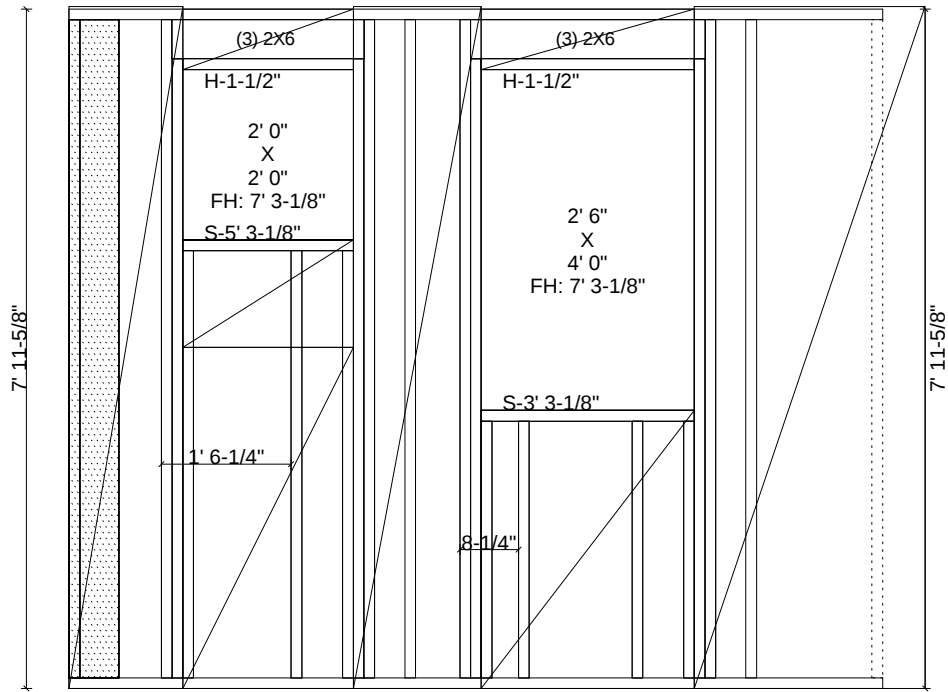

Panel Production Sheets

Job #Philis
Standard

Philis
Level 2

Date: 02/20/19
Page: 12
Bundle 1

Panel #9 (25.2 Bf)

Start Of Panel: 0"

Studs: 2X6 x 7' 8-5/8" (#2 SPF & BTR) [1] 1' 4" o.c.

(1) Top and (1) Bottom Plates: 2X6 x 1' 0" (#2 SPF & BTR)



*** Panel Diagonal 8' 0-3/8" ***

Insert	Start	End

* L CRNR(2X6) Up	@ Start	7"

Bottom Plate Lap: Flush		
Start	Type	End

6-3/16" Open		
11-3/4" x 8' 0"	7/16" OSB	Extend 5-15/16"



Panel Production Sheets

Job #Philis
Standard

Philis
Level 2

Date: 02/20/19
Page: 13
Bundle 1

Panel #12 (93.4 Bf)

Start Of Panel: 0"

Studs: 2X6 x 7' 8-5/8" (#2 SPF & BTR) [5] 1' 4" o.c.

(1) Top and (1) Bottom Plates: 2X6 x 8' 1-1/2" (#2 SPF & BTR)

*** Panel Diagonal 11' 4-9/16" ***

Insert	Start	End
* L CRNR(2X6) Up	@ Start	7"
L CRNR(2X6) Down *	7' 6-1/2"	@ End

Bottom Plate Lap: Flush

Start	Type	End
-------	------	-----



6-3/16" Open

3' 5-13/16" x 8' 0" 7/16" OSB

2' 8" x 8' 0" 7/16" OSB

1' 5-1/2" x 8' 0" 7/16" OSB

Flush

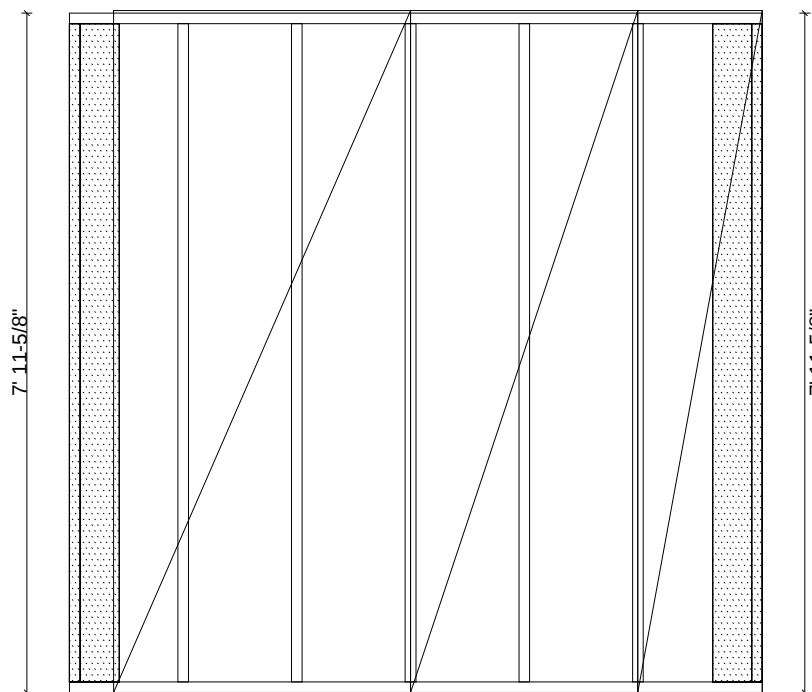

Panel Production Sheets

Job #Philis
Standard

Philis
Level 2

Date: 02/20/19
Page: 14
Bundle 1

Panel #8 (48.1 Bf)

Start Of Panel: 0"



Studs: 2X6 x 7' 8-5/8" (#2 SPF & BTR) [3] 1' 4" o.c.

(1) Top and (1) Bottom Plates: 2X6 x 3' 4" (#2 SPF & BTR)

*** Panel Diagonal 8' 7-5/8" ***

Insert	Start	End
* L CRNR(2X6) Down	@ Start	7"

Bottom Plate Lap: Flush	Type	End
Flush	3' 4" x 8' 0" 7/16" OSB	Flush

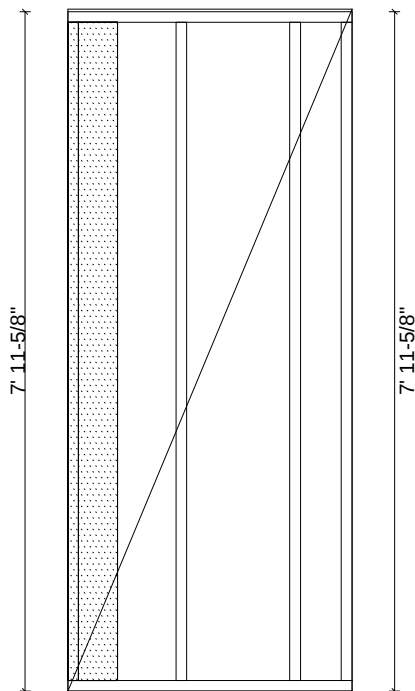

Panel Production Sheets

Job #Philis
Standard

Philis
Level 2

Date: 02/20/19
Page: 15
Bundle 1

Panel #11 (171.1 Bf)

Start Of Panel: 0"

Studs: 2X6 x 7' 8-5/8" (#2 SPF & BTR) [10] 1' 4" o.c.



(1) Top and (1) Bottom Plates: 2X6 x 16' 0" (#2 SPF & BTR)

*** Panel Diagonal 17' 10-1/2" ***

Insert	Start	End
* L CRNR(2X6) Down	@ Start	7"
* L premium(2X6) Down	7' 7-1/4"	8' 2-1/4"
SS	15' 8-15/16"	15' 11-15/16"

Bottom Plate Lap: Flush

Start	Type	End
Flush	4' 0" x 8' 0" 7/16" OSB	
	4' 0" x 8' 0" 7/16" OSB	
	4' 0" x 8' 0" 7/16" OSB	
	4' 0" x 8' 0" 7/16" OSB	Flush

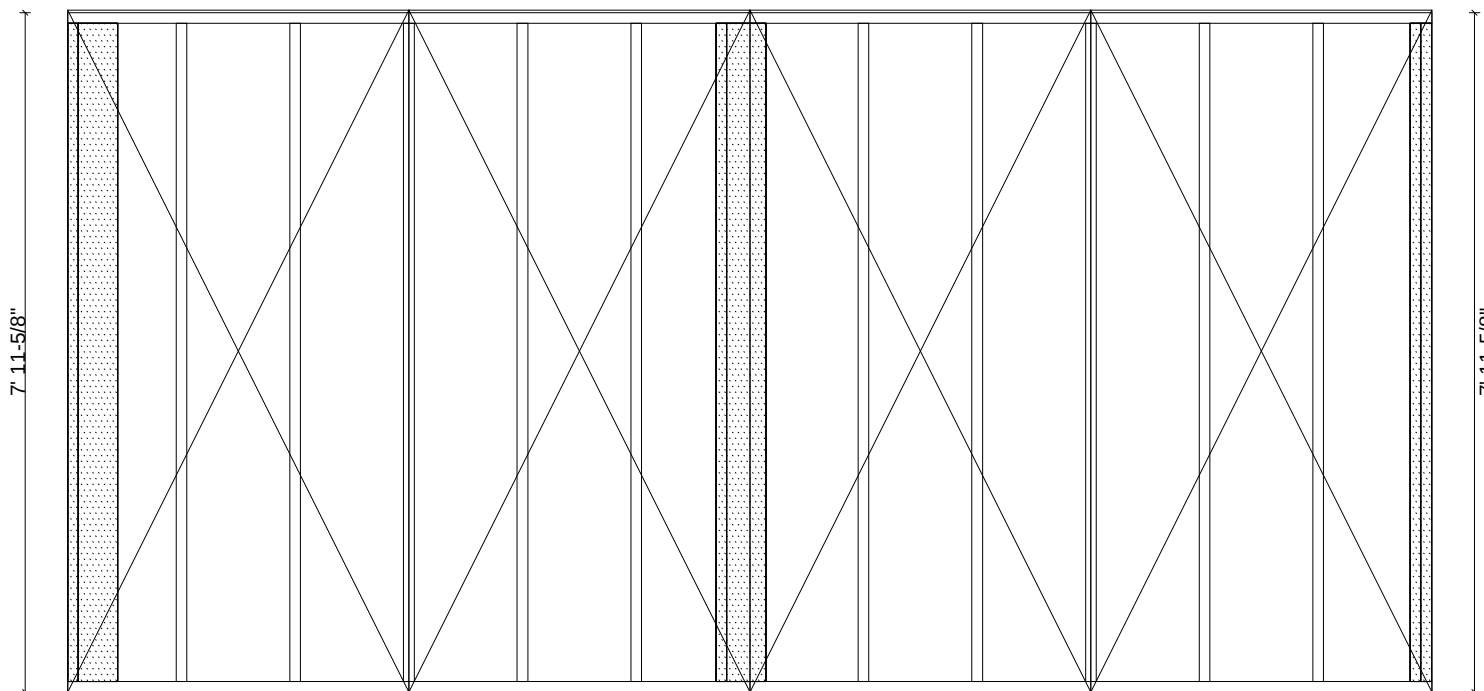

Panel Production Sheets

Job #Philis
Standard

Philis
Level 2

Date: 02/20/19
Page: 16
Bundle 1

Panel #13 (257.5 Bf)

Start Of Panel: 5-15/16"

Studs: 2X6 Sloped (#2 SPF & BTR) [2] 1' 4" o.c.

Top Plates: 2X6 (#2 SPF & BTR)

(1) 7' 1-11/16"

Start Rake Cut: 22.6 Deg /

End Rake Cut: 22.6 Deg /

TS: 7' 1-1/16"

(1) 7' 1-11/16"

Start Rake Cut: 112.6 Deg \

End Rake Cut: 112.6 Deg \

TS: 7' 1-1/16"

Bottom: (1) 2X6 x 13' 1" (#2 SPF & BTR)

The stud located at 12' 10-1/16" is omitted.

The stud located at 11' 6-1/16" is omitted.

The stud located at 10-1/16" is omitted.

Insert	Start	End
Loose Stud	1' 9-1/4"	1' 10-3/4"
30x30-LB	2' 10-15/16"	5' 4-15/16"
30x48-LB	5' 9-7/16"	8' 3-7/16"
30x30-LB	8' 7-15/16"	11' 1-15/16"
Loose Stud	12' 5-1/4"	12' 6-3/4"

Bottom Plate Lap: Flush

Start	Type	End
-------	------	-----

Extend 5-15/16"

7/16" OSB	A: * 7' 9"	B: 3"
	C: * 8' 0"	D: N.A.
	E: 7-1/8"	F: 2' 3-13/16"
	G: 2' 10-15/16"	H: N.A.

7/16" OSB	A: N.A.	B: 11-9/16"
	C: * 11-9/16"	D: N.A.
	E: 2' 3-13/16"	F: N.A.
	G: 2' 3-13/16"	H: N.A.

7/16" OSB	A: * 1' 8-7/16"	B: 1' 0-1/2"
	C: * 2' 8-15/16"	D: N.A.
	E: 2' 6"	F: N.A.
	G: 2' 6"	H: N.A.

Panel Production Sheets

Job #Philis
Standard

Philis
Level 2

Date: 02/20/19
Page: 17
Bundle 1

2' 6" x 4' 0" / 9-1/8" 7/16" OSB
4-1/2" x 8' 0" 7/16" OSB

Panel Production Sheets

Job #Philis
Standard

Philis
Level 2

Date: 02/20/19
Page: 18
Bundle 1

7/16" OSB	A: * 2' 0-1/16"	B: 1-7/8"
	C: * 2' 1-15/16"	D: N.A.
	E: 4-1/2"	F: N.A.
	G: 4-1/2"	H: N.A.

7/16" OSB	A: * 1' 4-13/16"	B: 6-1/4"
	C: * 1' 11-1/16"	D: N.A.
	E: 1' 3"	F: N.A.
	G: 1' 3"	H: N.A.

7/16" OSB	A: * 1' 11-1/16"	B: N.A.
	C: * 1' 4-13/16"	D: 6-1/4"
	E: 1' 3"	F: N.A.
	G: 1' 3"	H: N.A.

1' 3" x 4' 0" / 9-1/8"	7/16" OSB
1' 3" x 4' 0" / 9-1/8"	7/16" OSB
4-1/2" x 8' 0"	7/16" OSB

7/16" OSB	A: * 2' 1-15/16"	B: N.A.
	C: * 2' 0-1/16"	D: 1-7/8"
	E: 4-1/2"	F: N.A.
	G: 4-1/2"	H: N.A.

7/16" OSB	A: * 2' 8-15/16"	B: N.A.
	C: * 1' 8-7/16"	D: 1' 0-1/2"
	E: 2' 6"	F: N.A.
	G: 2' 6"	H: N.A.

2' 6" x 4' 0" / 9-1/8"	7/16" OSB
------------------------	-----------

7/16" OSB	A: * 8' 0"	B: N.A.
	C: * 7' 9"	D: 3"
	E: 2' 3-13/16"	F: 7-1/8"
	G: 2' 10-15/16"	H: N.A.

7/16" OSB	A: * 11-9/16"	B: N.A.
-----------	---------------	---------

Date: 02/20/19
Page: 19
Bundle 1

D: 11-9/16"
F: N.A.
H: N.A.

Quan.	Left Edge	Right Edge	Pitch (/12)	Angle	Top Plate Location	Bot. Plate Location
(1)	7' 8-3/8"	* 7' 9"	5.00	22.6	0"	0"
(1)	* 7' 9"	7' 8-3/8"	-5.00	-22.6	6' 11-7/16"	12' 11-1/2"



Panel Production Sheets

Job #Philis
Standard

Philis
Level 2

Date: 02/20/19
Page: 20
Bundle 1

Panel #18 (305.6 Bf)

Start Of Panel: 0"

Studs: 2X6 x 6' 4-5/8" (#2 SPF & BTR) [4] 1' 4" o.c.

(1) Top and (1) Bottom Plates: 2X6 x 17' 3-1/2" (#2 SPF & BTR)

*** Panel Diagonal 18' 6-5/16" ***

Insert	Start	End
-LB	3' 4-3/4"	11' 1-3/4"
-LB	11' 6-1/4"	16' 6-3/4"

Bottom Plate Lap: Flush

Start	Type	End
Flush	3' 4-3/4" x 6' 7-5/8" 7/16" OSB 2' 4" Open 4-1/2" x 2' 0" 7/16" OSB 2' 4" Open 4-1/2" x 2' 0" 7/16" OSB 7' 9" x 8-1/2" 7/16" OSB 7' 9" x 3' 11-1/8" 7/16" OSB 4-1/2" x 6' 7-5/8" 7/16" OSB 2' 4" Open 4-1/2" x 2' 0" 7/16" OSB 5' 0-1/2" x 8-1/2" 7/16" OSB 5' 0-1/2" x 3' 11-1/8" 7/16" OSB 8-3/4" x 6' 7-5/8" 7/16" OSB	Flush

Panel #18 Continued Next Page



Panel Production Sheets

Job #Philis
Standard

Philis
Level 2

Date: 02/20/19
Page: 21
Bundle 1

Panel #18 (Continued)

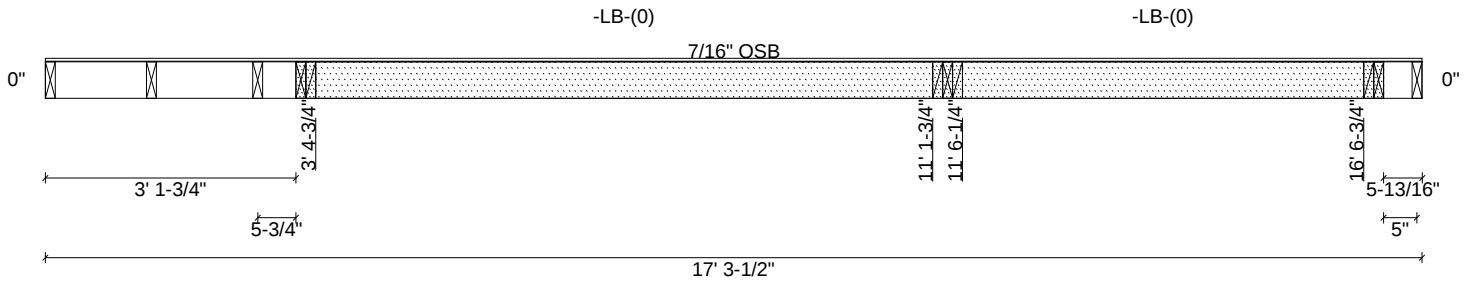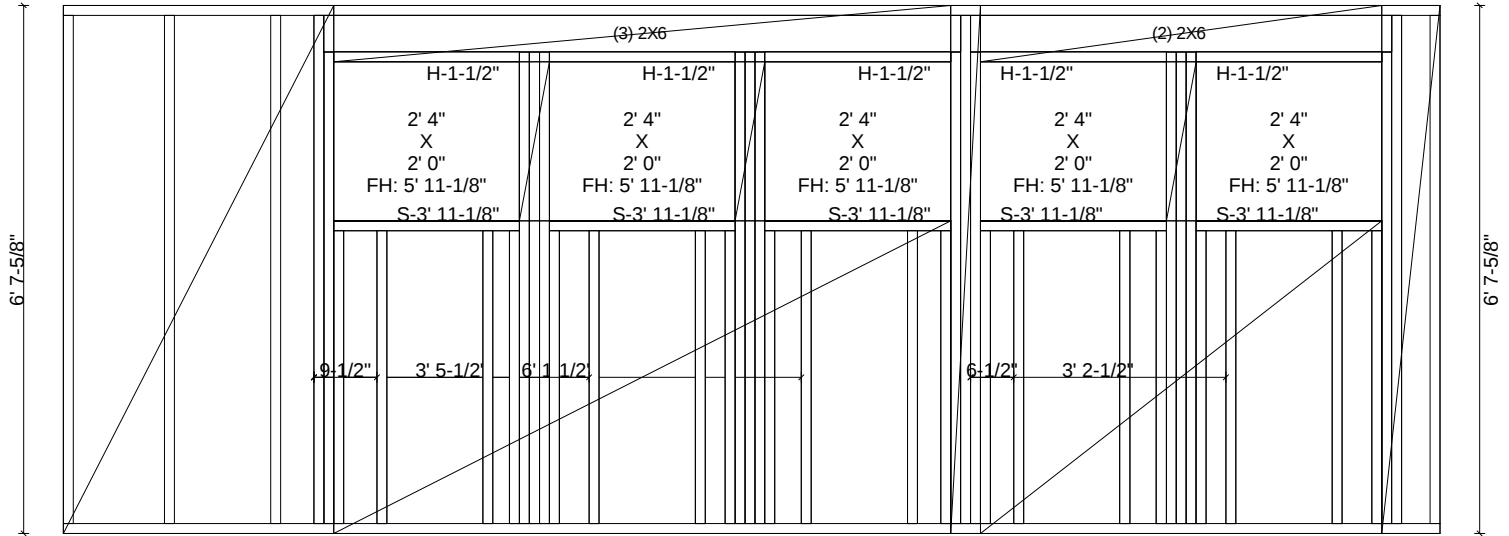

Panel Production Sheets

Job #Philis
Standard

Philis
Level 2

Date: 02/20/19
Page: 1
Bundle 2

Panel #14 (110.1 Bf)



Start Of Panel: 0"

Studs: 2X4 x 7' 8-5/8" (#2 SPF & BTR) [7] 1' 4" o.c.

(1) Top and (1) Bottom Plates: 2X4 x 12' 5" (#2 SPF & BTR)

*** Panel Diagonal 14' 9-1/16" ***

Insert	Start	End
2668/NB	2' 3-1/2"	4' 11-1/2"
* L2x4 Up	5' 2-1/2"	5' 7-1/2"
* L 2x8 Down	8' 11-3/8"	9' 8-1/8"

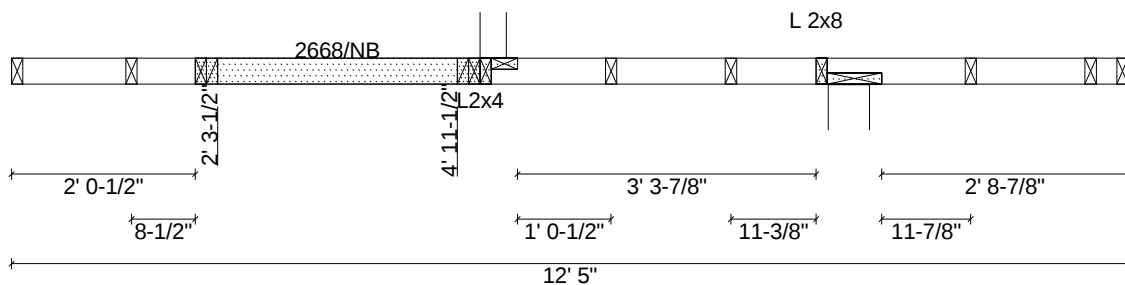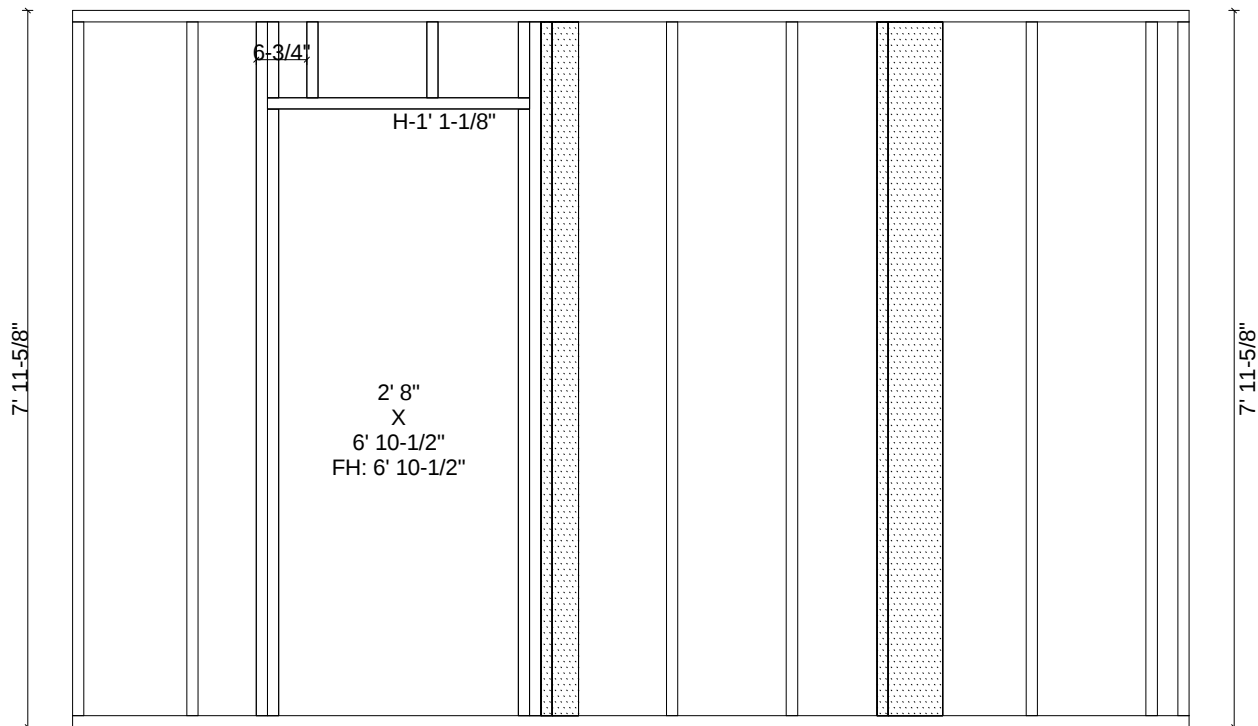

Panel Production Sheets

Job #Philis
Standard

Philis
Level 2

Date: 02/20/19
Page: 2
Bundle 2

Panel #15 (55.3 Bf)

Start Of Panel: 0"

Studs: 2X4 x 7' 8-5/8" (#2 SPF & BTR) [1] 1' 4" o.c.



(1) Top and (1) Bottom Plates: 2X4 x 5' 7-1/2" (#2 SPF & BTR)

The stud located at 5' 4" is omitted.

The stud located at 4' 0" is omitted.

*** Panel Diagonal 9' 9-1/16" ***

Insert	Start	End
2668/NB	3"	2' 11"
L2x4 Down *	3' 2"	3' 7"
Loose Stud	4' 3-1/4"	4' 4-3/4"

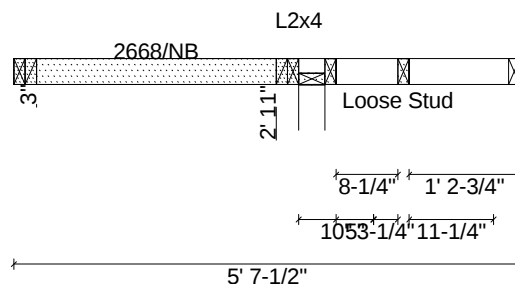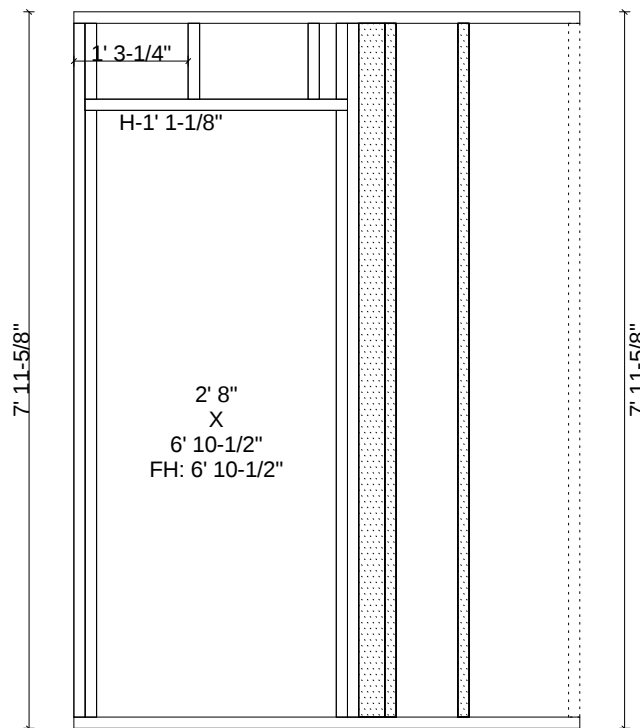

Panel Production Sheets

Job #Philis
Standard

Philis
Level 2

Date: 02/20/19
Page: 3
Bundle 2


Panel #16 (28.2 Bf)

Start Of Panel: 0"

Studs: 2X4 x 7' 8-5/8" (#2 SPF & BTR) [4] 1' 4" o.c.

(1) Top and (1) Bottom Plates: 2X4 x 3' 7" (#2 SPF & BTR)

*** Panel Diagonal 8' 8-7/8" ***

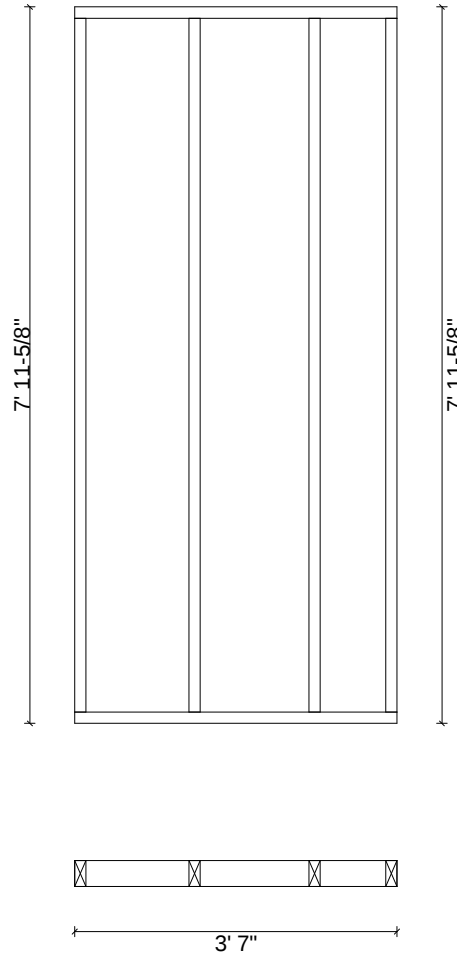

Panel Production Sheets

Job #Philis
Standard

Philis
Level 2

Date: 02/20/19
Page: 4
Bundle 2

Panel #17 (77.8 Bf)

Start Of Panel: 0"

Studs: 2X6 x 7' 8-5/8" (#2 SPF & BTR) [3] 1' 4" o.c.

(1) Top and (1) Bottom Plates: 2X6 x 6' 3-1/2" (#2 SPF & BTR)

*** Panel Diagonal 10' 1-13/16" ***

Insert	Start	End
2468/NB	3' 6-1/2"	6' 0-1/2"

