

Panel Production Sheets

Job #Philis
Standard

Philis
Level 1

Date: 02/20/19
Page: 1
Bundle 1

Panel #47 (140.2 Bf)


Start Of Panel: 0"

Studs: 2X6 x 8' 8-5/8" (#2 SPF & BTR) [11] 1' 4" o.c.

6.6 Deg / (1) Top and (1) Bottom Plates: 2X6 (#2 SPF & BTR)
(1) 14' 5-3/16" TE
14' 5-13/16" LP
14' 5-13/16" BE

The stud located at 1' 4" is omitted.

*** Panel Diagonal 17' 0-7/16" ***

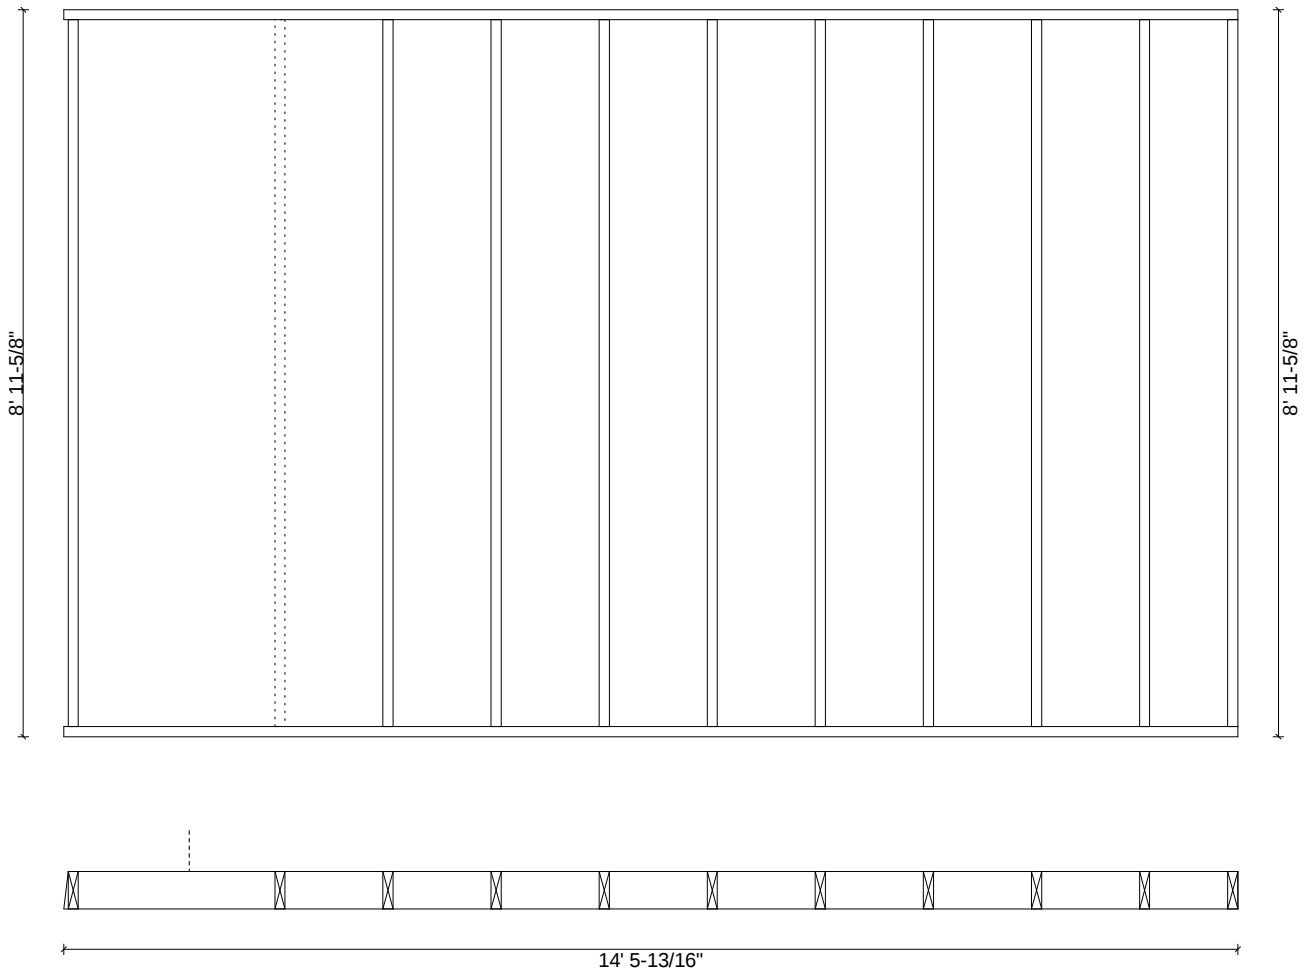

Panel Production Sheets

Job #Philis
Standard

Philis
Level 1

Date: 02/20/19
Page: 2
Bundle 1

Panel #46 (57.8 Bf)



Start Of Panel: 0"

Studs: 2X4 x 8' 8-5/8" (#2 SPF & BTR) [5] 1' 4" o.c.

22.9 Deg \ (1) Top and (1) Bottom Plates: 2X4 (#2 SPF & BTR)
(1) 7' 2-1/2" TE / 50.8 Deg
7' 2-1/2" LP
6' 8-3/4" BE

*** Panel Diagonal 11' 6-1/16" ***

Insert	Start	End
* L premium(2X6) Up	3' 10-3/16"	4' 5-3/16"

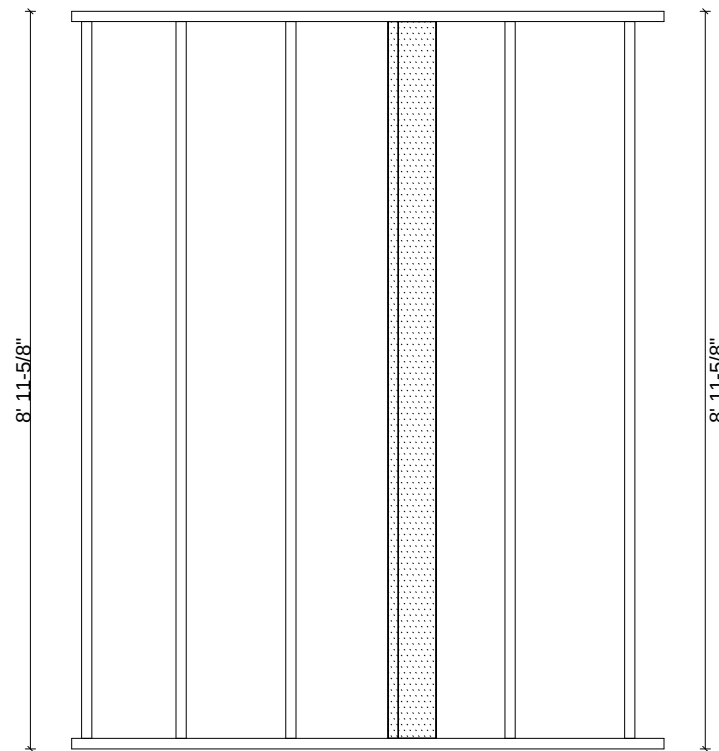

Panel Production Sheets

Job #Philis
Standard

Philis
Level 1

Date: 02/20/19
Page: 3
Bundle 1

Panel #45 (72.0 Bf)

Start Of Panel: 0"

Studs: 2X4 x 8' 8-5/8" (#2 SPF & BTR) [7] 1' 4" o.c.

(1) Top and (1) Bottom Plates: 2X4 (#2 SPF & BTR)



(1) 8' 5-3/4" TE / 22.9 Deg

8' 5-3/4" LP

8' 4-1/4" BE

*** Panel Diagonal 12' 4-1/8" ***

Insert	Start	End
* L premium(2X6) Down	3' 7-1/4"	4' 2-1/4"

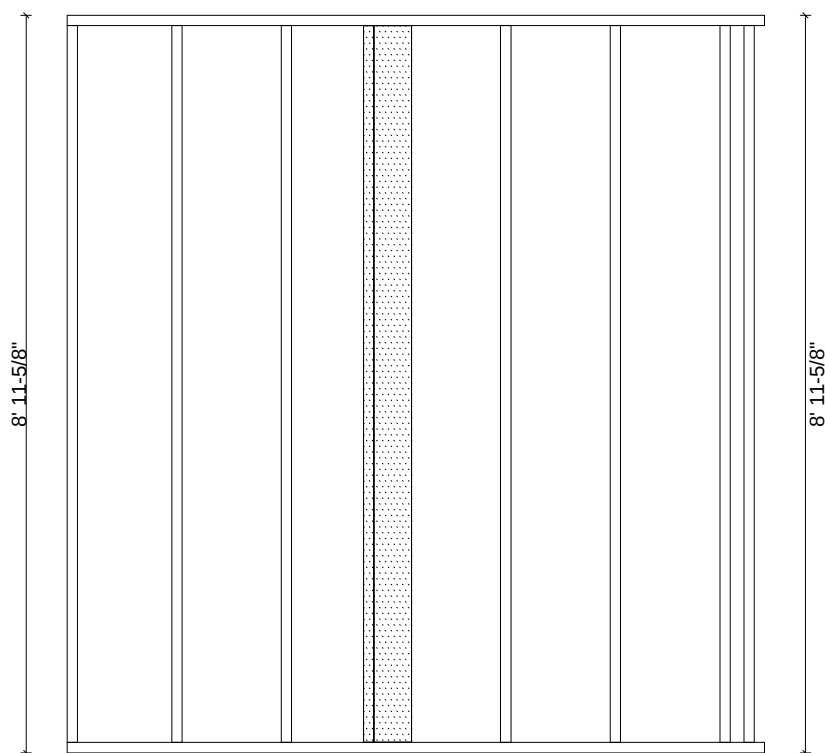

Panel Production Sheets

Job #Philis
Standard

Philis
Level 1

Date: 02/20/19
Page: 4
Bundle 1

Panel #43 (47.6 Bf)



Start Of Panel: 0"

Studs 2X4 x 8' 8-5/8" (#2 SPF & BTR) [0] 1' 4" o.c.

(1) Top and (1) Bottom Plates: 2X4 x 4' 0-1/2" (#2 SPF & BTR)

*** Panel Diagonal 9' 10-1/16" ***

Insert	Start	End
SS	@ Start	3"
*2-2068/NB	6-3/4"	3' 9-1/4"

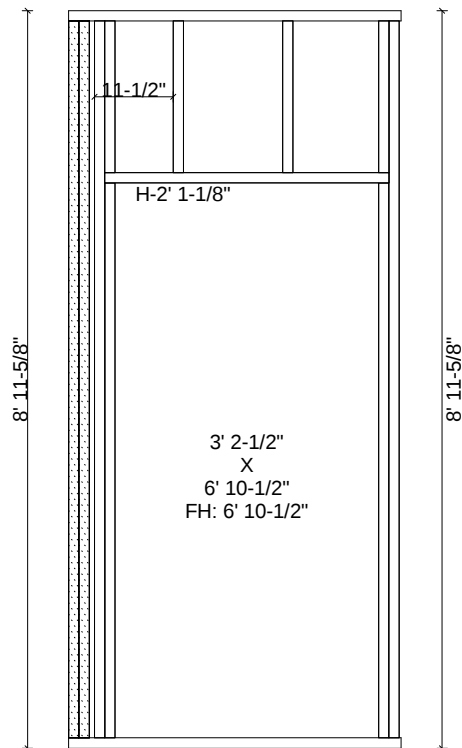

Panel Production Sheets

Job #Philis
Standard

Philis
Level 1

Date: 02/20/19
Page: 5
Bundle 1


Panel #42 (21.6 Bf)

Start Of Panel: 0"

Studs: 2X4 x 8' 8-5/8" (#2 SPF & BTR) [3] 1' 4" o.c.

(1) Top and (1) Bottom Plates: 2X4 x 1' 10-3/4" (#2 SPF & BTR)

*** Panel Diagonal 9' 2" ***

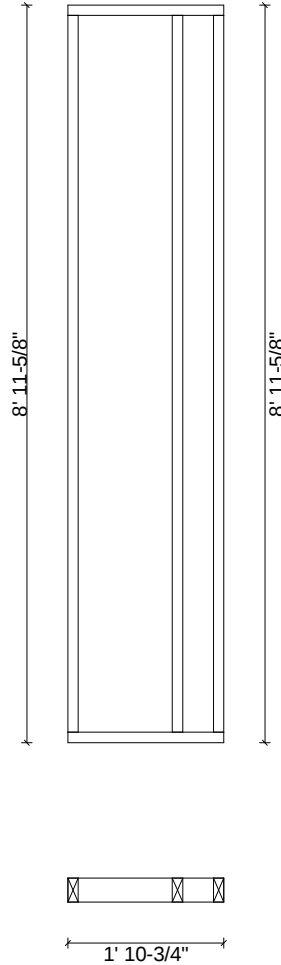

Panel Production Sheets

Job #Philis
Standard

Philis
Level 1

Date: 02/20/19
Page: 6
Bundle 1

Panel #58 (61.6 Bf)

Start Of Panel: 0"

Studs: 2X4 x 8' 8-5/8" (#2 SPF & BTR) [1] 1' 4" o.c.

(1) Top and (1) Bottom Plates: 2X4 (#2 SPF & BTR)



(1) 6' 3-3/8" TE / 0.8 Deg

6' 3-3/8" LP

6' 3-5/16" BE

*** Panel Diagonal 10' 11-3/8" ***

Insert	Start	End
* L2x4 Up	@ Start	5"
2-2668/NB	8-5/16"	5' 10-13/16"

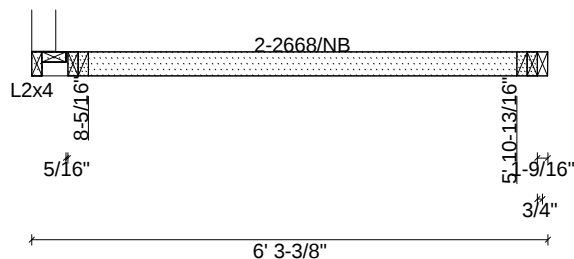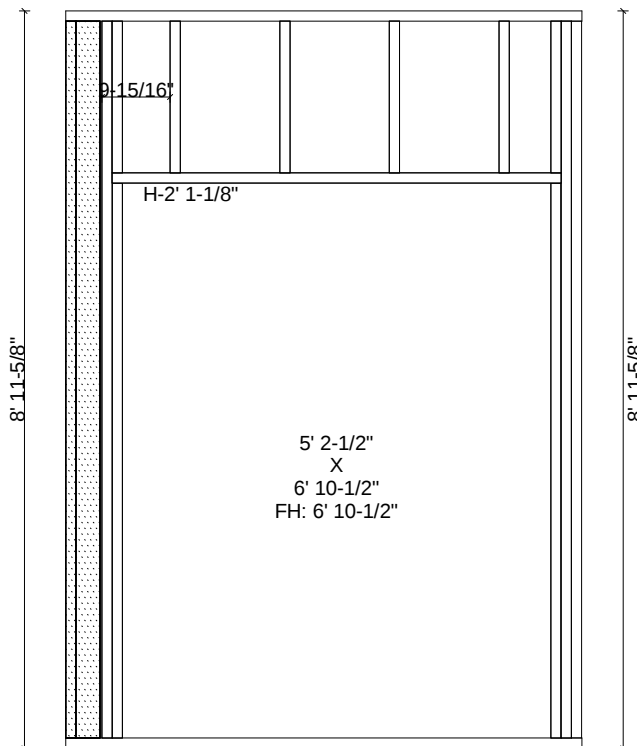

Panel Production Sheets

Job #Philis
Standard

Philis
Level 1

Date: 02/20/19
Page: 7
Bundle 1

Panel #55 (42.1 Bf)



Start Of Panel: 0"

Studs: 2X4 x 8' 8-5/8" (#2 SPF & BTR) [1] 1' 4" o.c.

22.5 Deg \ (1) Top and (1) Bottom Plates: 2X4 (#2 SPF & BTR)
(1) 4' 4" TE
4' 4" LP
4' 2-9/16" BE

*** Panel Diagonal 9' 11-1/2" ***

Insert	Start	End
2668/NB	1' 5"	4' 1"

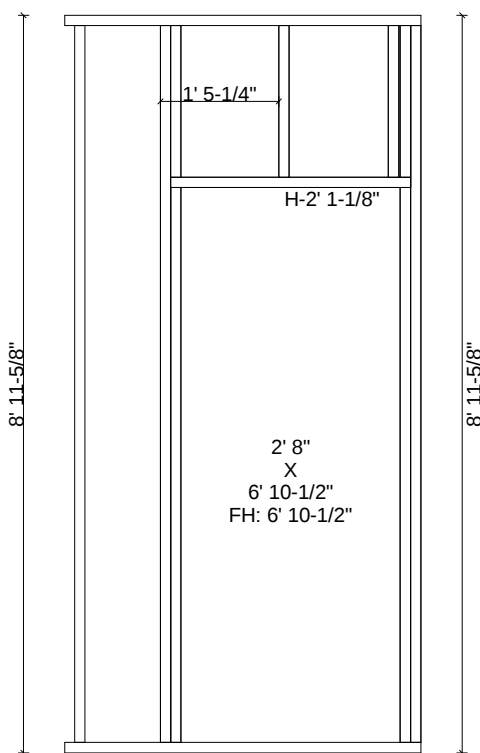

Panel Production Sheets

Job #Philis
Standard

Philis
Level 1

Date: 02/20/19
Page: 8
Bundle 1



Panel #54 (21.2 Bf)

Start Of Panel: 0"

Studs: 2X4 x 8' 8-5/8" (#2 SPF & BTR) [3] 1' 4" o.c.

22.4 Deg \ (1) Top and (1) Bottom Plates: 2X4 (#2 SPF & BTR)
(1) 1' 10-11/16" TE / 22.4 Deg
1' 10-11/16" LP
1' 7-13/16" BE

*** Panel Diagonal 9' 2" ***

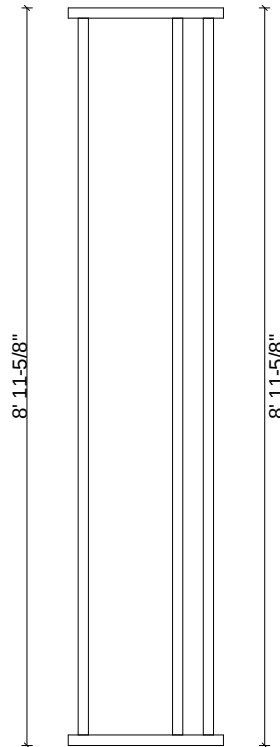

Panel Production Sheets

Job #Philis
Standard

Philis
Level 1

Date: 02/20/19
Page: 9
Bundle 1

Panel #53 (79.2 Bf)

Start Of Panel: 0"

Studs: 2X4 x 8' 8-5/8" (#2 SPF & BTR) [8] 1' 4" o.c.

(1) Top and (1) Bottom Plates: 2X4 (#2 SPF & BTR)



(1) 9' 0-1/2" TE / 22.5 Deg

9' 0-1/2" LP

8' 11-1/16" BE

*** Panel Diagonal 12' 8-13/16" ***

Insert	Start	End
* L premium(2X6) Down	6' 10-1/4"	7' 5-1/4"

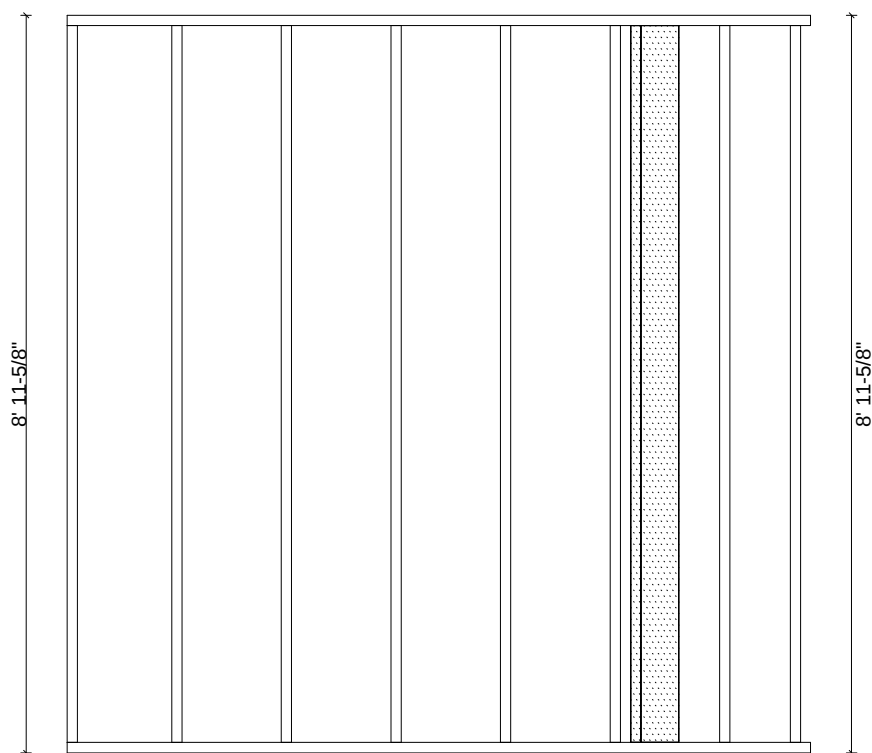

Panel Production Sheets

Job #Philis
Standard

Philis
Level 1

Date: 02/20/19
Page: 10
Bundle 1


Panel #66 (21.6 Bf)

Start Of Panel: 0"

Studs: 2X4 x 8' 8-5/8" (#2 SPF & BTR) [3] 1' 4" o.c.

(1) Top and (1) Bottom Plates: 2X4 x 2' 0" (#2 SPF & BTR)

*** Panel Diagonal 9' 2-1/4" ***

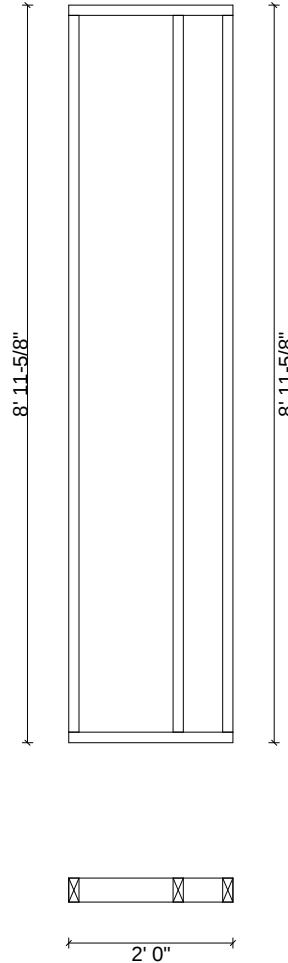

Panel Production Sheets

Job #Philis
Standard

Philis
Level 1

Date: 02/20/19
Page: 11
Bundle 1


Panel #61 (45.9 Bf)

Start Of Panel: 0"

Studs: 2X6 x 8' 8-5/8" (#2 SPF & BTR) [4] 1' 4" o.c.

(1) Top and (1) Bottom Plates: 2X6 x 3' 6-1/2" (#2 SPF & BTR)

*** Panel Diagonal 9' 7-11/16" ***

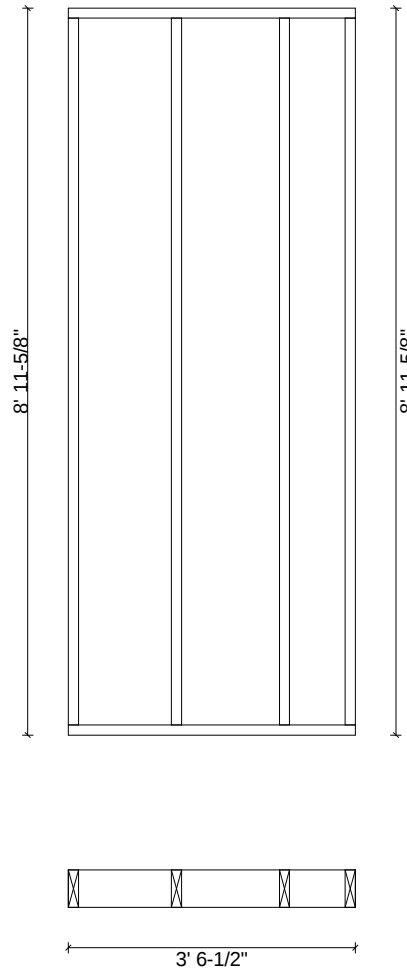

Panel Production Sheets

Job #Philis
Standard

Philis
Level 1

Date: 02/20/19
Page: 12
Bundle 1

Panel #44 (30.4 Bf)

Start Of Panel: 0"



Studs: 2X6 x 8' 8-5/8" (#2 SPF & BTR) [1] 1' 4" o.c.

(1) Top and (1) Bottom Plates: 2X6 x 2' 5-3/4" (#2 SPF & BTR)

The stud located at 3/4" is omitted.

*** Panel Diagonal 9' 3-11/16" ***

Insert	Start	End
-----	-----	-----
L CRNR(2X4) Down *	2' 0-3/4"	@ End

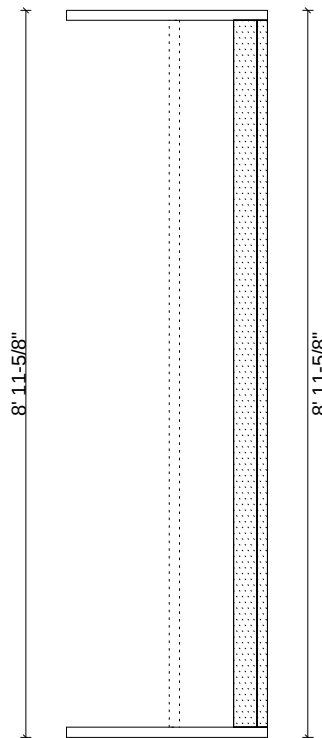

Panel Production Sheets

Job #Philis
Standard

Philis
Level 1

Date: 02/20/19
Page: 13
Bundle 1

Panel #40 (57.1 Bf)

Start Of Panel: 0"


Studs: 2X6 x 8' 8-5/8" (#2 SPF & BTR) [1] 1' 4" o.c.

(1) Top and (1) Bottom Plates: 2X6 x 2' 8" (#2 SPF & BTR)


*** Panel Diagonal 9' 4-1/4" ***

Insert	Start	End

* L CRNR(2X4) Down	@ Start	5"
SSS	2' 3-7/16"	2' 7-15/16"

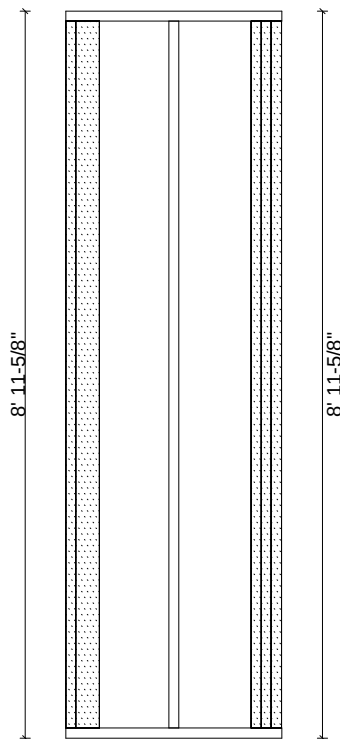

L CRNR



Panel Production Sheets

Job #Philis
Standard

Philis
Level 1

Date: 02/20/19
Page: 14
Bundle 1

Panel #57 (44.5 Bf)

Start Of Panel: 0"



Studs: 2X4 x 8' 8-5/8" (#2 SPF & BTR) [4] 1' 4" o.c.

22.4 Deg \ (1) Top and (1) Bottom Plates: 2X4 (#2 SPF & BTR)
(1) 3' 4-7/16" TE
3' 4-7/16" LP
3' 3" BE

*** Panel Diagonal 9' 6-15/16" ***

Insert	Start	End

* L premium(2X6) Down	1' 10-11/16"	2' 5-11/16"

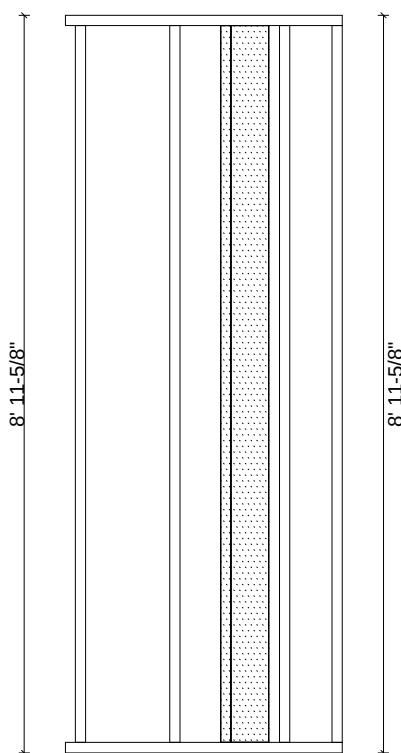

Panel Production Sheets

Job #Philis
Standard

Philis
Level 1

Date: 02/20/19
Page: 15
Bundle 1

Panel #59 (125.8 Bf)



Start Of Panel: 0"

Studs: 2X4 x 8' 8-5/8" (#2 SPF & BTR) [7] 1' 4" o.c.

(1) Top and (1) Bottom Plates: 2X4 x 14' 3" (#2 SPF & BTR)

*** Panel Diagonal 16' 10-1/16" ***

Insert	Start	End
* L premium(2X6) Up	6' 2-3/4"	6' 9-3/4"
* L premium(2X6) Down	10' 3-1/4"	10' 10-1/4"
2668/NB	11' 4"	14' 0"

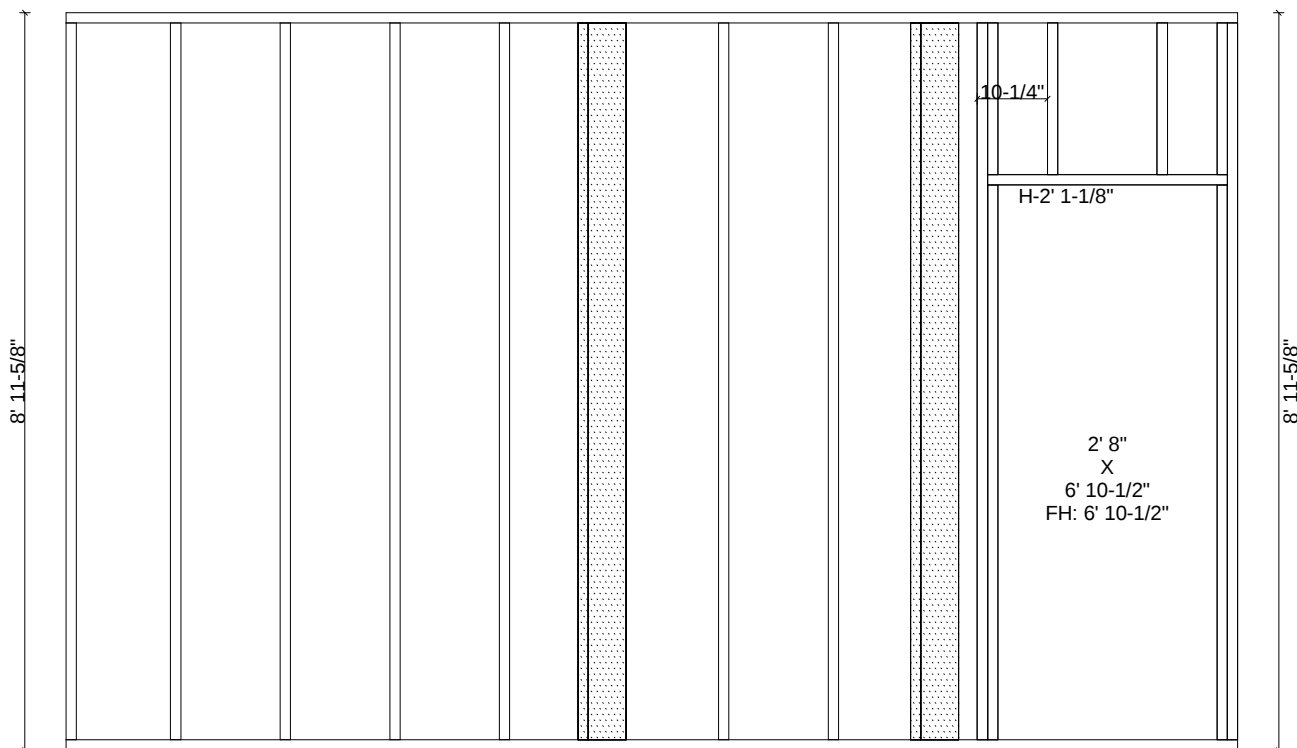

Panel Production Sheets

Job #Philis
Standard

Philis
Level 1

Date: 02/20/19
Page: 16
Bundle 1

Panel #60 (60.1 Bf)



Start Of Panel: 0"

Studs: 2X4 x 8' 8-5/8" (#2 SPF & BTR) [3] 1' 4" o.c.

(1) Top and (1) Bottom Plates: 2X4 x 7' 3-1/2" (#2 SPF & BTR)

*** Panel Diagonal 11' 6-11/16" ***

Insert	Start	End
2868/NB	4' 2-1/2"	7' 0-1/2"

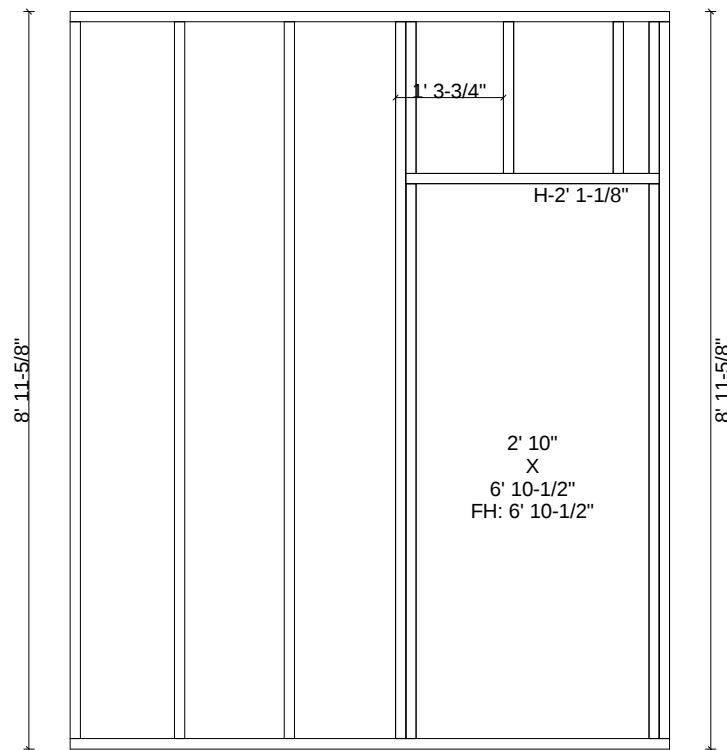

Panel Production Sheets

Job #Philis
Standard

Philis
Level 1

Date: 02/20/19
Page: 17
Bundle 1


Panel #65 (29.9 Bf)

Start Of Panel: 0"

Studs: 2X4 x 8' 8-5/8" (#2 SPF & BTR) [4] 1' 4" o.c.

(1) Top and (1) Bottom Plates: 2X4 x 3' 2" (#2 SPF & BTR)

*** Panel Diagonal 9' 6-1/8" ***

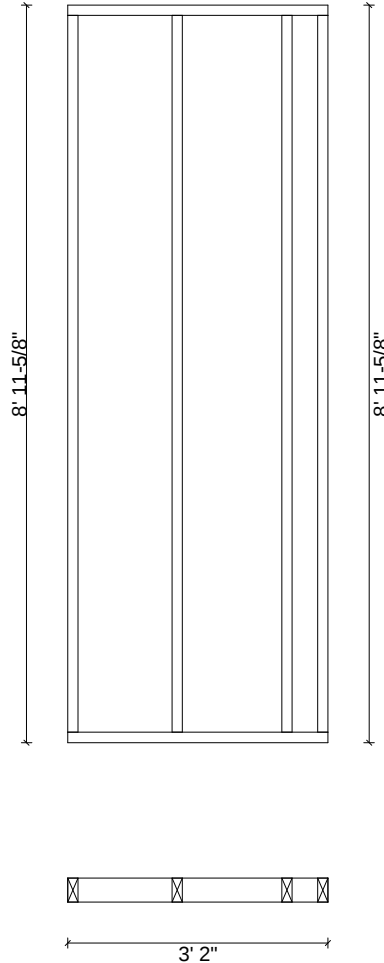

Panel Production Sheets

Job #Philis
Standard

Philis
Level 1

Date: 02/20/19
Page: 18
Bundle 1

Panel #64 (30.3 Bf)

Start Of Panel: 0"



Studs: 2X4 x 8' 8-5/8" (#2 SPF & BTR) [2] 1' 4" o.c.

22.5 Deg / (1) Top and (1) Bottom Plates: 2X4 (#2 SPF & BTR)
(1) 2' 3-15/16" TE
2' 5-3/8" LP
2' 5-3/8" BE

The stud located at 2' 4-9/16" is omitted.

*** Panel Diagonal 9' 3-9/16" ***

Insert	Start	End
-----	-----	-----
* L premium(2X6) Down	7-1/4"	1' 2-1/4"

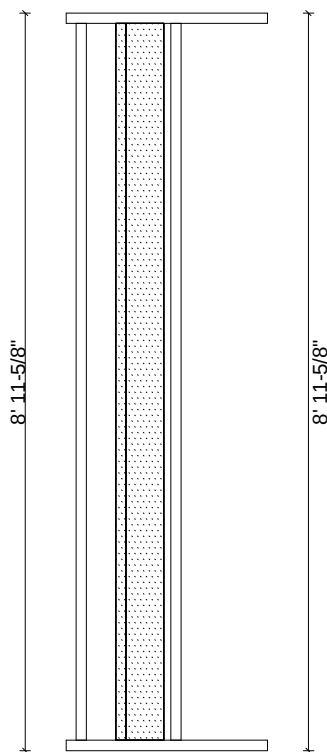

Panel Production Sheets

Job #Philis
Standard

Philis
Level 1

Date: 02/20/19
Page: 19
Bundle 1

Panel #63 (21.7 Bf)

Start Of Panel: 0"

Studs: 2X4 x 8' 8-5/8" (#2 SPF & BTR) [3] 1' 4" o.c.



(1) Top and (1) Bottom Plates: 2X4 (#2 SPF & BTR)

(1) 1' 11" TE \ 22.4 Deg

2' 0-7/16" LP

2' 0-7/16" BE

*** Panel Diagonal 9' 2-3/8" ***

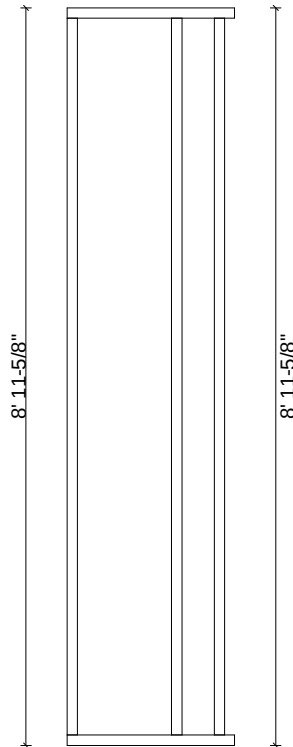

Panel Production Sheets

Job #Philis
Standard

Philis
Level 1

Date: 02/20/19
Page: 20
Bundle 1

Panel #62 (26.6 Bf)



Start Of Panel: 0"

Studs: 2X4 x 8' 8-5/8" (#2 SPF & BTR) [1] 1' 4" o.c.

(1) Top and (1) Bottom Plates: 2X4 x 1' 6-1/2" (#2 SPF & BTR)

*** Panel Diagonal 9' 1-3/16" ***

Insert	Start	End
C2x4(2X4) *	1' 1-7/16"	1' 6-7/16"



Panel Production Sheets

Job #Philis
Standard

Philis
Level 1

Date: 02/20/19
Page: 21
Bundle 1

Panel #48 (57.3 Bf)



Start Of Panel: 0"

Studs: 2X4 x 8' 8-5/8" (#2 SPF & BTR) [3] 1' 4" o.c.

(1) Top and (1) Bottom Plates: 2X4 x 5' 10-1/2" (#2 SPF & BTR)

*** Panel Diagonal 10' 8-5/8" ***

Insert	Start	End
2868/NB	3"	3' 1"

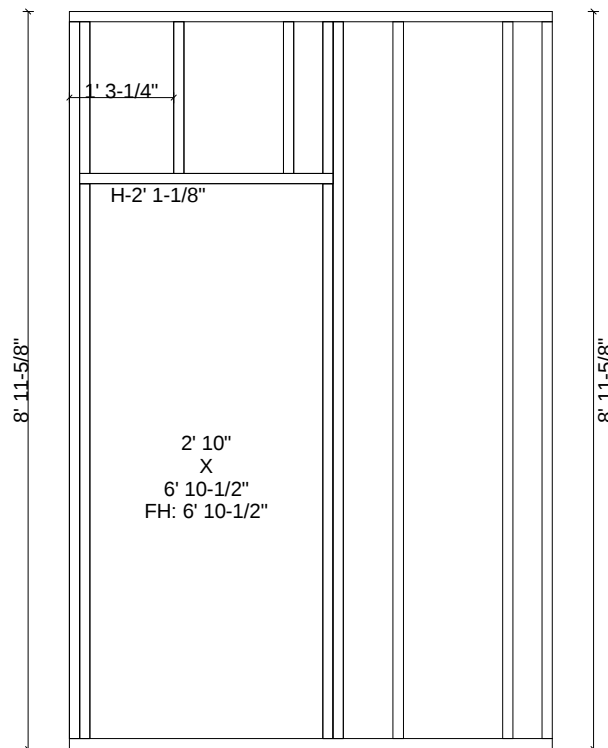

Panel Production Sheets

Job #Philis
Standard

Philis
Level 1

Date: 02/20/19
Page: 22
Bundle 1



Panel #49 (35.7 Bf)
Start Of Panel: 0"
Studs: 2X4 x 8' 8-5/8" (#2 SPF & BTR) [3] 1' 4" o.c.

(1) Top and (1) Bottom Plates: 2X4 x 3' 4" (#2 SPF & BTR)

*** Panel Diagonal 9' 6-13/16" ***

Insert	Start	End

* L CRNR(2X4) Down	@ Start	5"

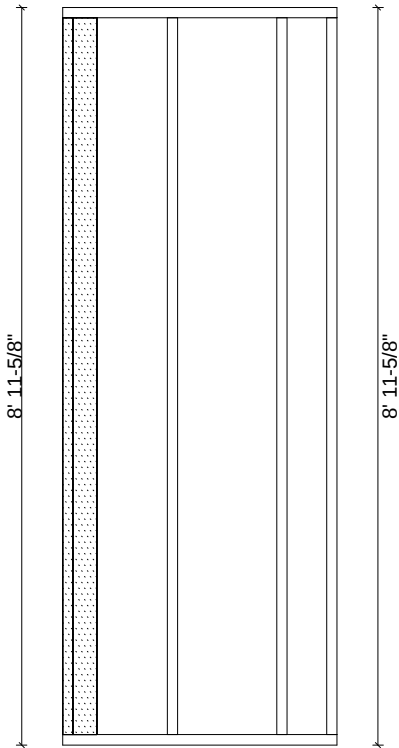

Panel Production Sheets

Job #Philis
Standard

Philis
Level 1

Date: 02/20/19
Page: 23
Bundle 1


Panel #52 (40.0 Bf)

Start Of Panel: 0"

Studs: 2X4 x 8' 8-5/8" (#2 SPF & BTR) [5] 1' 4" o.c.

(1) Top and (1) Bottom Plates: 2X4 x 5' 3" (#2 SPF & BTR)

*** Panel Diagonal 10' 4-11/16" ***

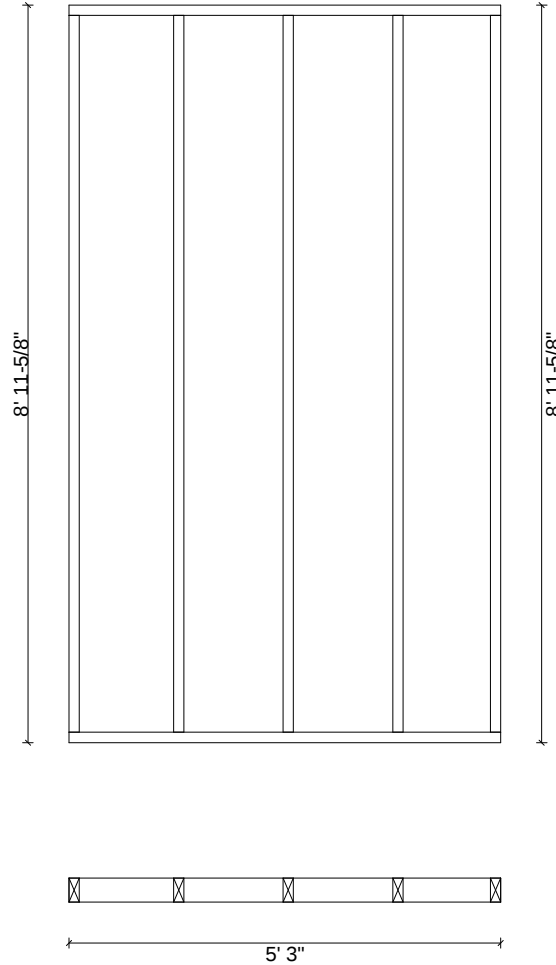

Panel Production Sheets

Job #Philis
Standard

Philis
Level 1

Date: 02/20/19
Page: 24
Bundle 1

Panel #56 (47.8 Bf)

Start Of Panel: 0"

Studs: 2X4 x 8' 8-5/8" (#2 SPF & BTR) [3] 1' 4" o.c.

(1) Top and (1) Bottom Plates: 2X4 (#2 SPF & BTR)



(1) 3' 8" TE / 22.5 Deg

3' 8" LP

3' 6-9/16" BE

*** Panel Diagonal 9' 8-1/4" ***

Insert	Start	End
* L CRNR(2X4) Down	@ Start	5"
* L CRNR(2X4) Up	2' 9-1/2"	3' 2-1/2"

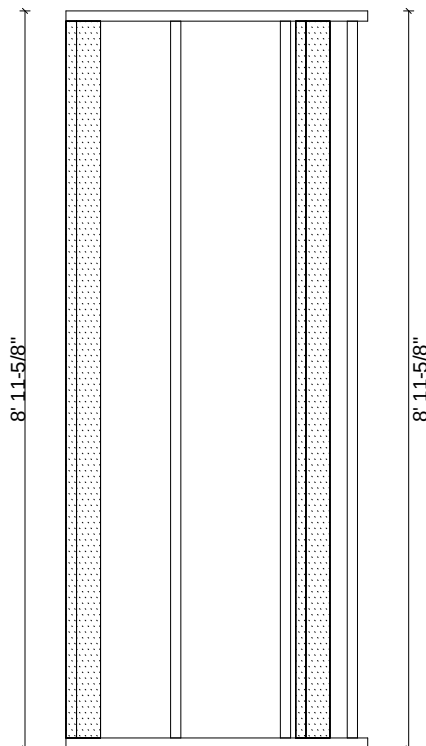

Panel Production Sheets

Job #Philis
Standard

Philis
Level 1

Date: 02/20/19
Page: 25
Bundle 1

Panel #50 (67.1 Bf)



Start Of Panel: 0"

Studs: 2X4 x 8' 8-5/8" (#2 SPF & BTR) [5] 1' 4" o.c.

(1) Top and (1) Bottom Plates: 2X4 x 6' 2" (#2 SPF & BTR)

*** Panel Diagonal 10' 10-5/8" ***

Insert	Start	End
* L CRNR(2X4) Up	@ Start	5"
* L premium(2X6) Down	6-1/4"	1' 1-1/4"

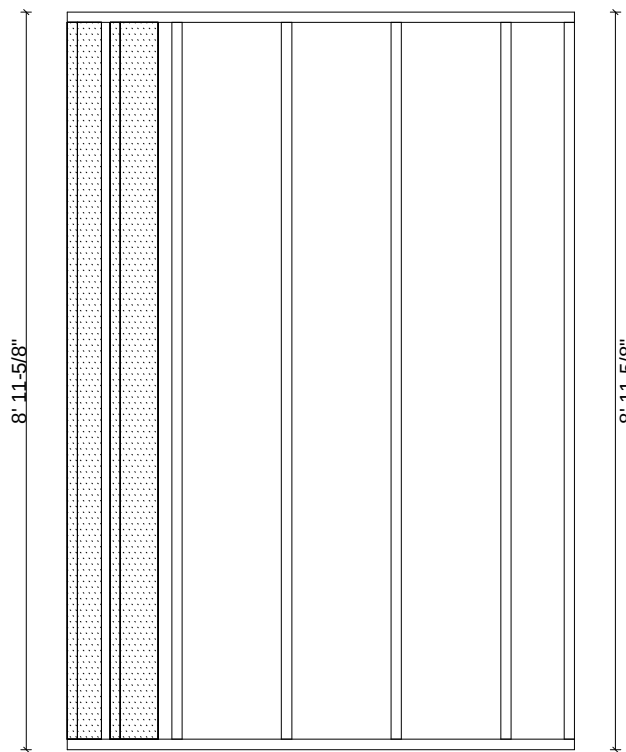

Panel Production Sheets

Job #Philis
Standard

Philis
Level 1

Date: 02/20/19
Page: 26
Bundle 1

Panel #51 (43.2 Bf)

Start Of Panel: 0"



Studs: 2X4 x 8' 8-5/8" (#2 SPF & BTR) [1] 1' 4" o.c.

(1) Top and (1) Bottom Plates: 2X4 x 5' 6-1/2" (#2 SPF & BTR)

The stud located at 3/4" is omitted.

*** Panel Diagonal 10' 6-1/2" ***

Insert	Start	End
2668/NB	2' 7-1/2"	5' 3-1/2"

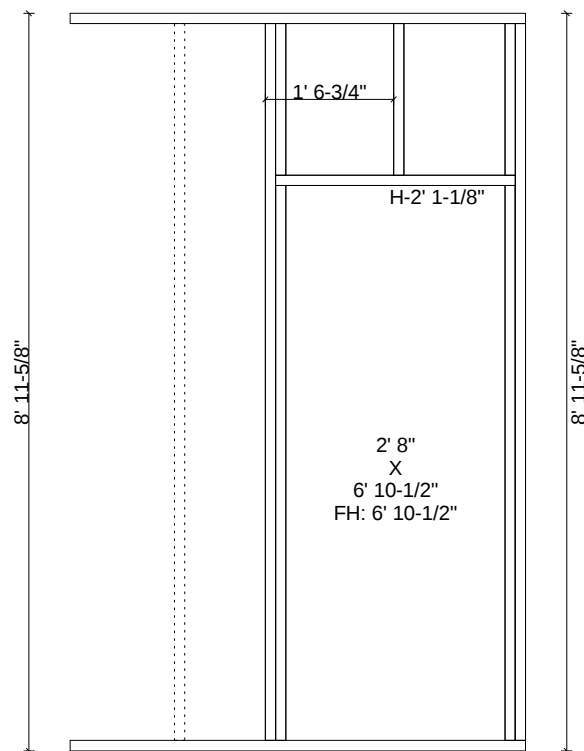

Panel Production Sheets

Job #Philis
Standard

Philis
Level 1

Date: 02/20/19
Page: 27
Bundle 1


Panel #38 (54.0 Bf)

Start Of Panel: 0"

Studs: 2X4 x 8' 8-5/8" (#2 SPF & BTR) [7] 1' 4" o.c.

(1) Top and (1) Bottom Plates: 2X4 x 8' 0" (#2 SPF & BTR)

*** Panel Diagonal 12' 0-3/16" ***

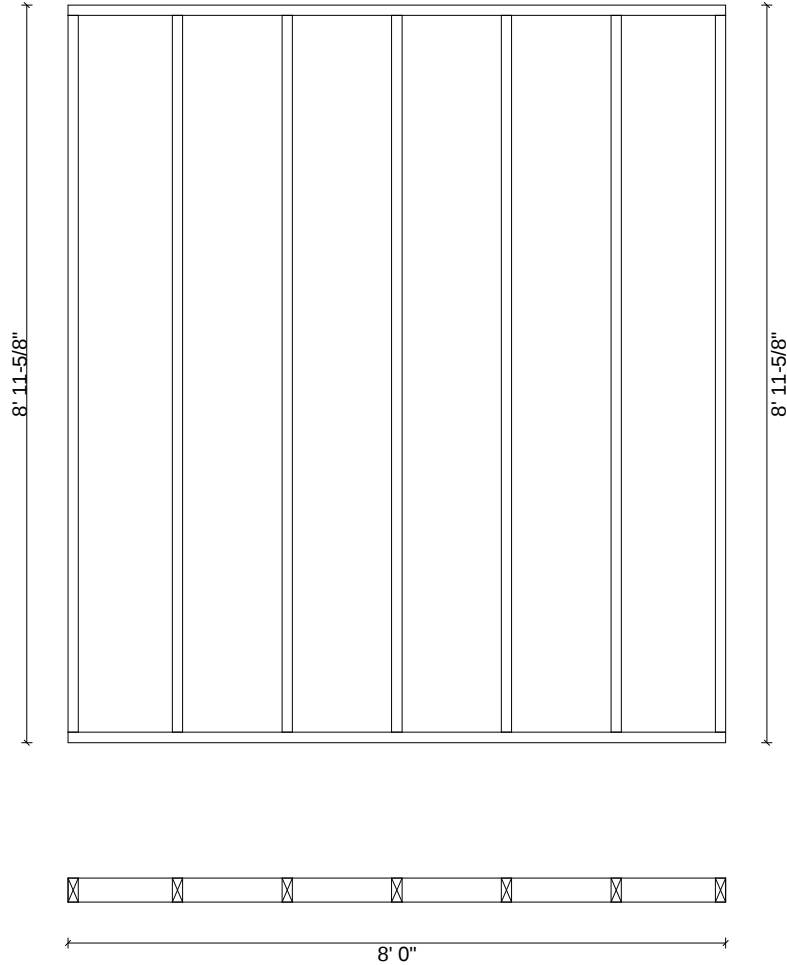

Panel Production Sheets

Job #Philis
Standard

Philis
Level 1

Date: 02/20/19
Page: 28
Bundle 1

Panel #34 (40.8 Bf)



Start Of Panel: 0"

Studs: 2X4 x 8' 8-5/8" (#2 SPF & BTR) [1] 1' 4" o.c.

(1) Top and (1) Bottom Plates: 2X4 x 3' 6" (#2 SPF & BTR)

*** Panel Diagonal 9' 7-1/2" ***

Insert	Start	End
2868/NB	5"	3' 3"

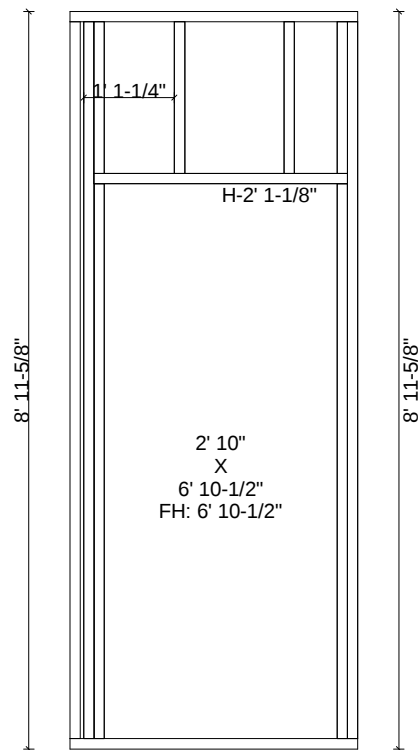

Panel Production Sheets

Job #Philis
Standard

Philis
Level 1

Date: 02/20/19
Page: 29
Bundle 1

Panel #39 (70.0 Bf)



Start Of Panel: 0"

Studs: 2X4 x 8' 8-5/8" (#2 SPF & BTR) [7] 1' 4" o.c.

(1) Top and (1) Bottom Plates: 2X4 x 9' 0" (#2 SPF & BTR)

*** Panel Diagonal 12' 8-7/16" ***

Insert	Start	End
* L premium(2X6) Up	4' 10-1/4"	5' 5-1/4"

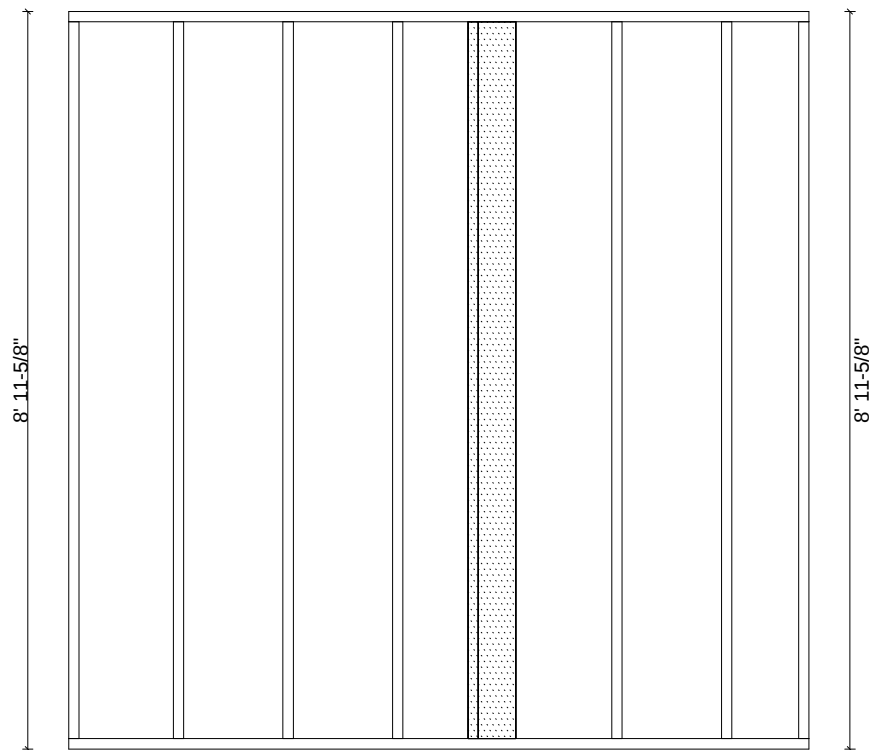

Date: 02/20/19
Page: 30
Bundle 1

Panel Production Sheets

Job #Philis
Standard

Philis
Level 1

Date: 02/20/19
Page: 31
Bundle 1

Panel #67 (35.2 Bf)

Start Of Panel: 0"


Studs: 2X4 x 8' 8-5/8" (#2 SPF & BTR) [3] 1' 4" o.c.

(1) Top and (1) Bottom Plates: 2X4 x 3' 0-1/2" (#2 SPF & BTR)


*** Panel Diagonal 9' 5-5/8" ***

Insert	Start	End

* L CRNR(2X4) Down	@ Start	5"

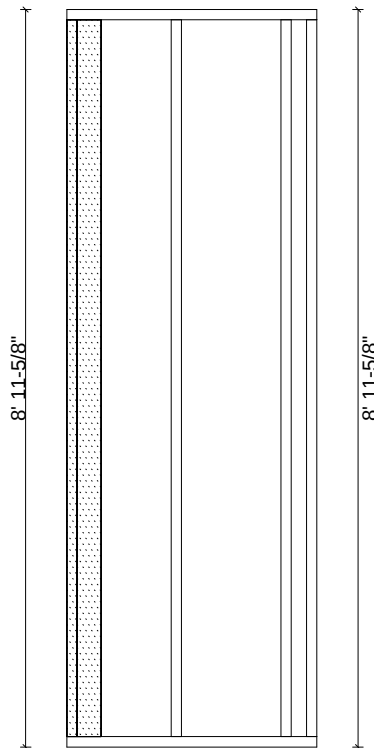

L CRNR



Panel Production Sheets

Job #Philis
Standard

Philis
Level 1

Date: 02/20/19
Page: 32
Bundle 1

Panel #36 (75.2 Bf)



Start Of Panel: 0"

Studs: 2X4 x 8' 8-5/8" (#2 SPF & BTR) [8] 1' 4" o.c.

(1) Top and (1) Bottom Plates: 2X4 x 8' 3-1/2" (#2 SPF & BTR)

*** Panel Diagonal 12' 2-9/16" ***

Insert	Start	End
* L CRNR(2X4) Down	3' 0"	3' 5"

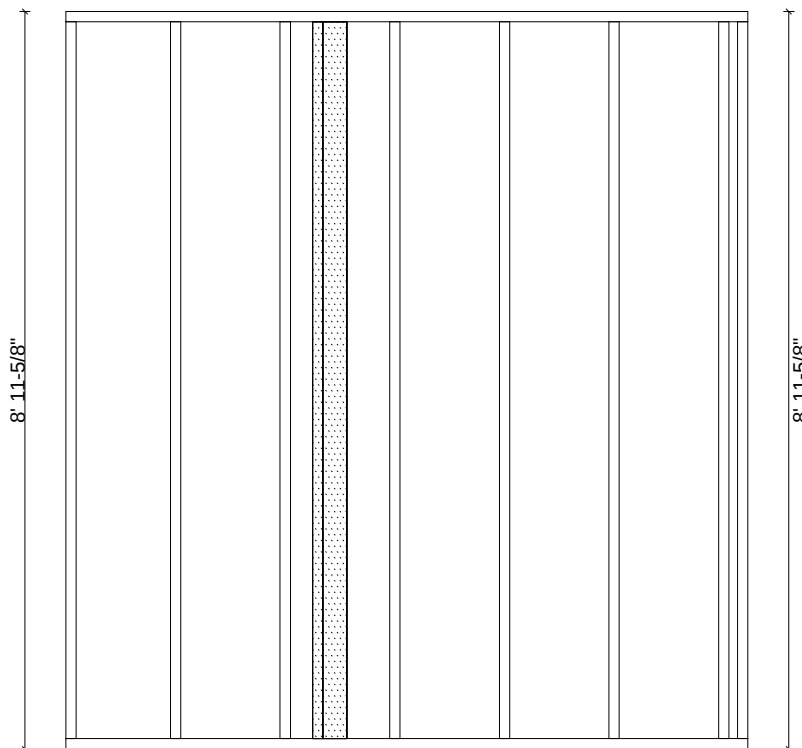

Panel Production Sheets

Job #Philis
Standard

Philis
Level 1

Date: 02/20/19
Page: 33
Bundle 1


Panel #35 (55.2 Bf)

Start Of Panel: 0"

Studs: 2X4 x 8' 8-5/8" (#2 SPF & BTR) [7] 1' 4" o.c.

(1) Top and (1) Bottom Plates: 2X4 x 7' 1" (#2 SPF & BTR)

*** Panel Diagonal 11' 5-1/8" ***

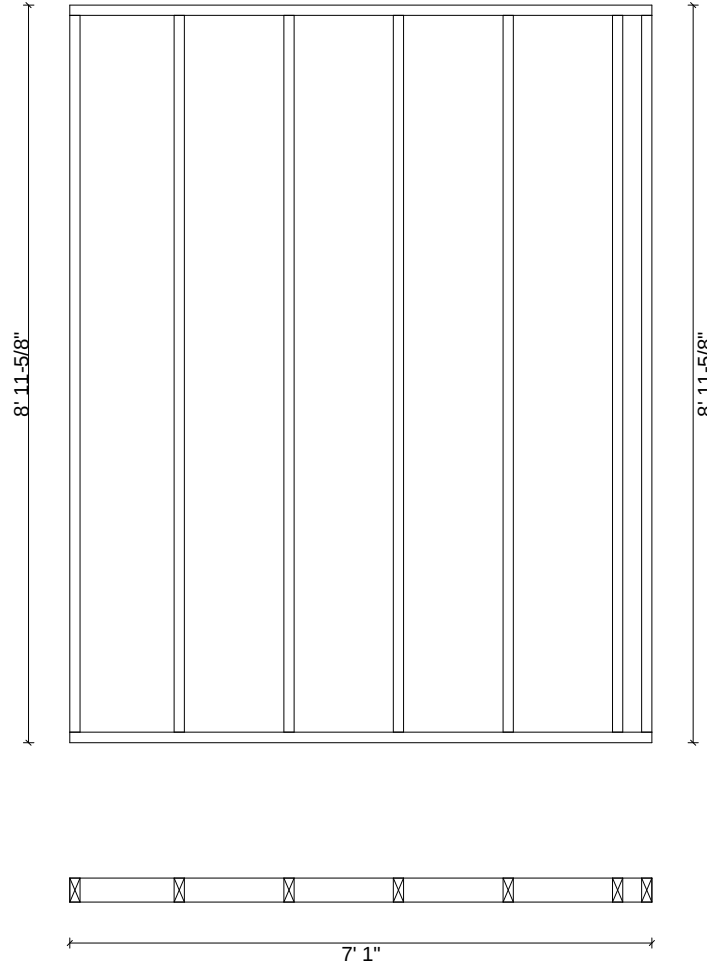

Panel Production Sheets

Job #Philis
Standard

Philis
Level 1

Date: 02/20/19
Page: 34
Bundle 1

Panel #33 (78.1 Bf)



Start Of Panel: 0"

Studs: 2X4 x 8' 8-5/8" (#2 SPF & BTR) [6] 1' 4" o.c.

(1) Top and (1) Bottom Plates: 2X4 x 8' 7" (#2 SPF & BTR)

*** Panel Diagonal 12' 4-15/16" ***

Insert	Start	End
* L CRNR(2X4) Down	@ Start	5"
* L premium(2X6) Down	5' 1-3/4"	5' 8-3/4"

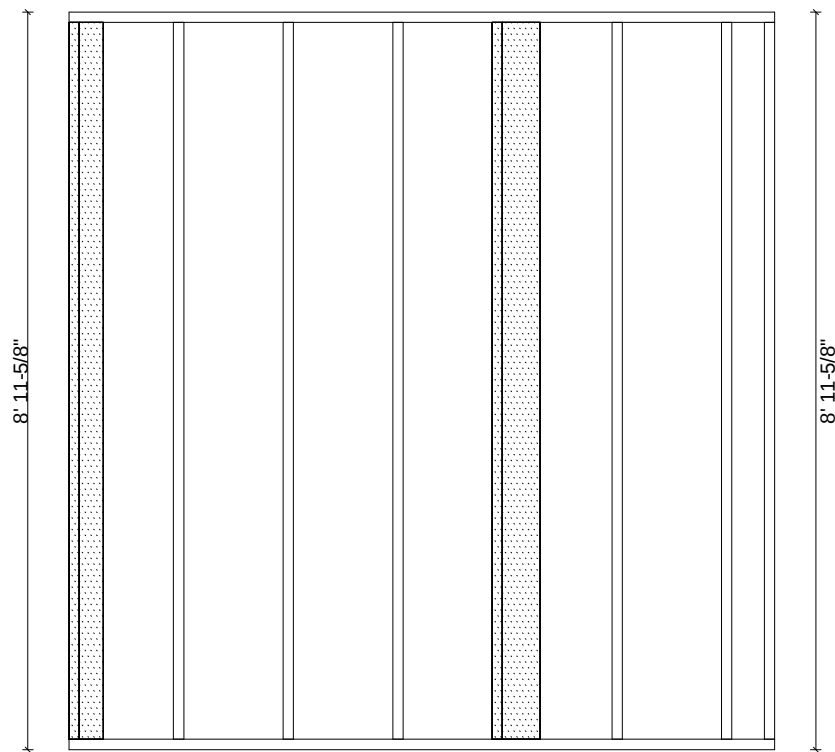

Panel Production Sheets

Job #Philis
Standard

Philis
Level 1

Date: 02/20/19
Page: 35
Bundle 1

Panel #41 (169.3 Bf)



Start Of Panel: 0"

Studs: 2X6 x 8' 8-5/8" (#2 SPF & BTR) [4] 1' 4" o.c.

(1) Top and (1) Bottom Plates: 2X6 x 11' 1" (#2 SPF & BTR)

*** Panel Diagonal 14' 3-1/16" ***

Insert	Start	End
2868/NB	3"	3' 1"
* L premium(2X6) Up	3' 6-3/4"	4' 1-3/4"
*2-2068/NB	4' 4-3/4"	7' 7-1/4"

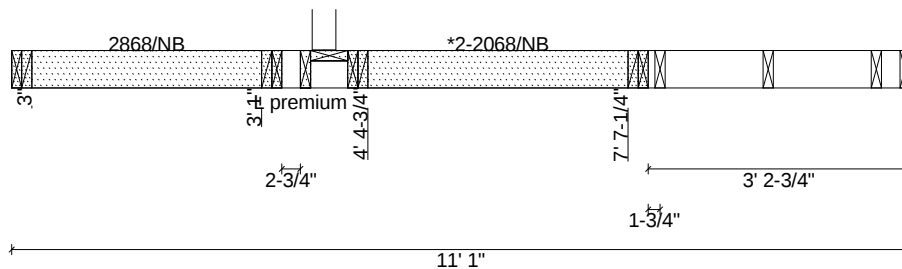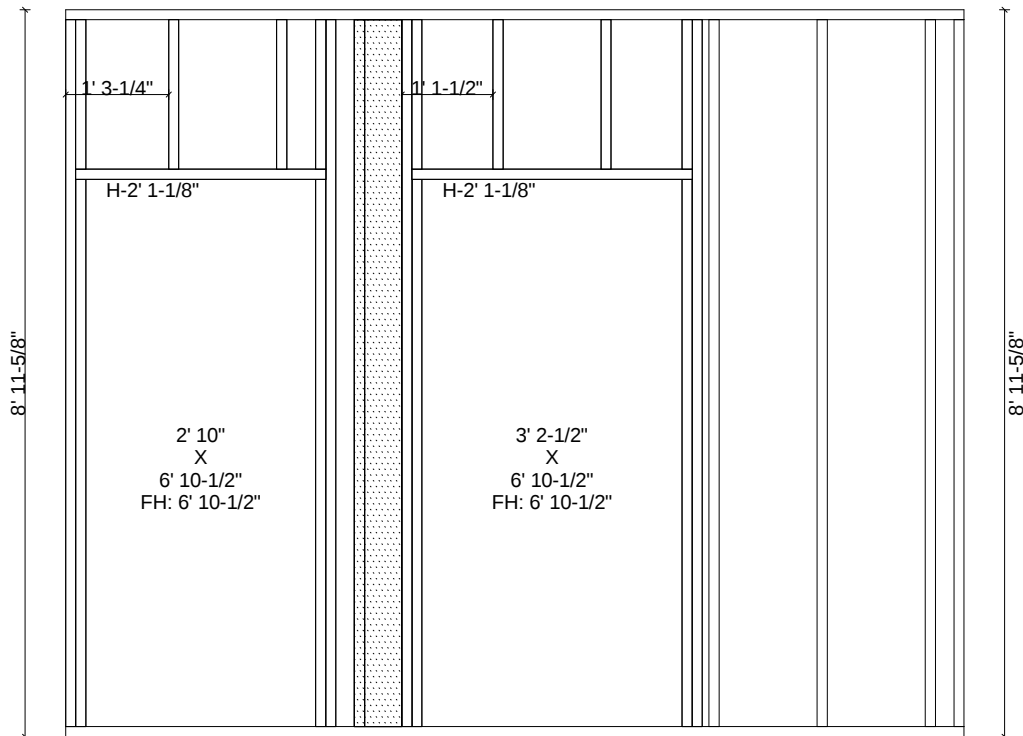

Panel Production Sheets

Job #Philis
Standard

Philis
Level 1

Date: 02/20/19
Page: 36
Bundle 1

Panel #86 (33.4 Bf)



Start Of Panel: 0"

Studs: 2X4 x 3' 1-1/2" (#2 SPF & BTR) [6] 1' 4" o.c.

(1) Top and (1) Bottom Plates: 2X4 x 7' 3-5/8" (#2 SPF & BTR)

*** Panel Diagonal 8' 0-1/2" ***

Insert	Start	End
C2x4(2X4) *	6' 10-9/16"	7' 3-9/16"

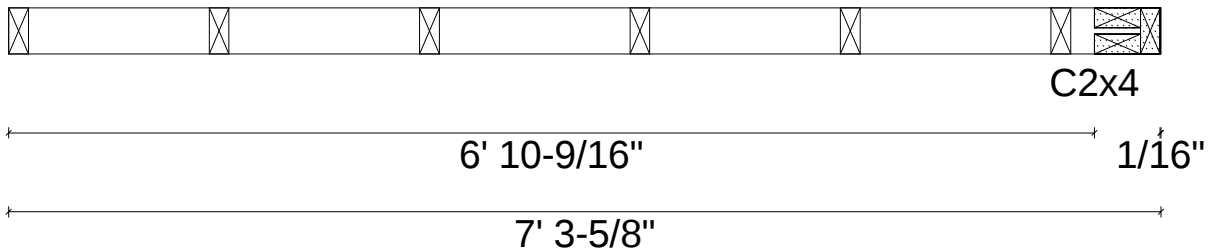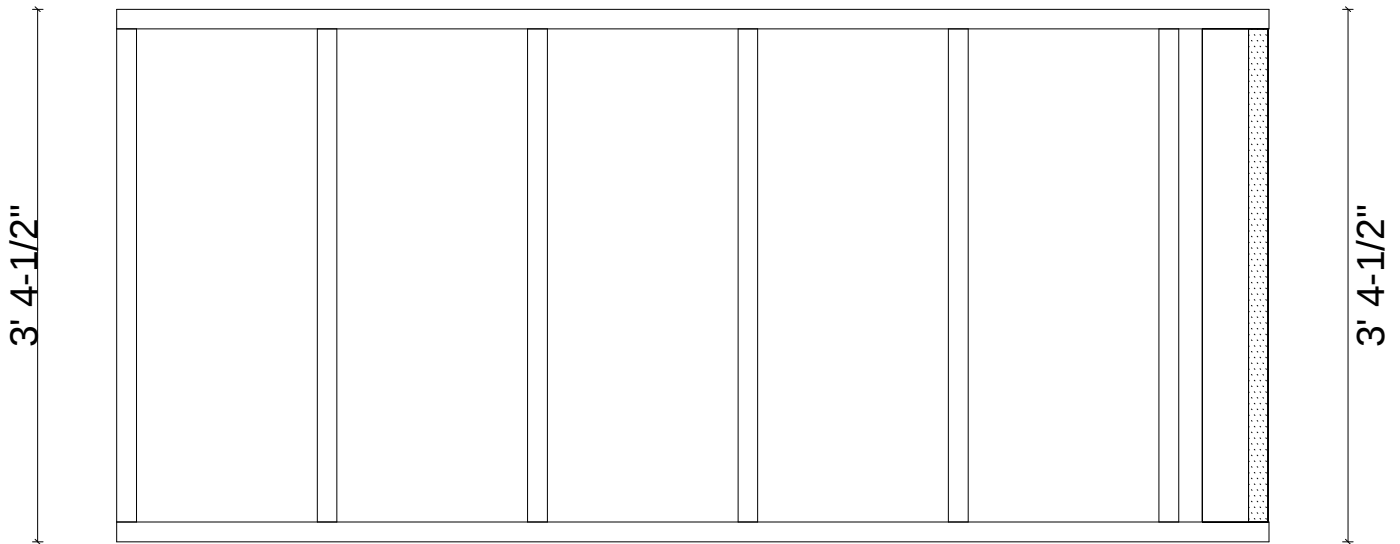

Panel Production Sheets

Job #Philis
Standard

Philis
Level 1

Date: 02/20/19
Page: 1
Bundle 2

Panel #32 (153.0 Bf)

Start Of Panel: 5-15/16"

Studs: 2X6 Sloped (#2 SPF & BTR) [4] 1' 4" o.c.

Top Plates: 2X6 (#2 SPF & BTR)

(1) 6' 0-11/16"
Start Rake Cut: 22.6 Deg /
End Rake Cut: 22.6 Deg /
TS: 6' 0-1/16"

(1) 6' 0-11/16"
Start Rake Cut: 112.6 Deg \
End Rake Cut: 112.6 Deg \
TS: 6' 0-1/16"

Bottom: (1) 2X6 x 11' 1" (#2 SPF & BTR)

Insert	Start	End
72x96-LB	3' 0-7/16"	9' 0-7/16"

Bottom Plate Lap: Flush

Start	Type	End
Extend 5-15/16"	3' 0-7/16" x 8' 0"	7/16" OSB

7/16" OSB	A: * 9"	B: 1' 3-3/16"
	C: * 2' 0-3/16"	D: N.A.
	E: 3' 0-7/16"	F: N.A.
	G: 3' 0-7/16"	H: N.A.

7/16" OSB	A: * 2' 0-3/16"	B: 1' 3"
	C: * 3' 3-3/16"	D: N.A.
	E: 3' 0"	F: N.A.
	G: 3' 0"	H: N.A.

7/16" OSB	A: * 3' 3-3/16"	B: N.A.
	C: * 2' 0-3/16"	D: 1' 3"
	E: 3' 0"	F: N.A.
	G: 3' 0"	H: N.A.

3' 0-7/16" x 8' 0" 7/16" OSB

7/16" OSB	A: * 2' 0-3/16"	B: N.A.
	C: * 9"	D: 1' 3-3/16"
	E: 3' 0-7/16"	F: N.A.
	G: 3' 0-7/16"	H: N.A.

Extend 5-15/16"

Panel Production Sheets

Job #Philis
Standard



Philis
Level 1

Date: 02/20/19

Page: 2

Bundle 2

Quan.	Left Edge	Right Edge	Pitch (/12)	Angle	Top Plate Location	Bot. Plate Location
(1)	8' 8-3/8"	* 8' 9"	5.00	22.6	0"	0"
(1)	9' 0-1/4"	* 9' 0-7/8"	5.00	22.6	10-1/16"	9-5/16"
(1)	* 9' 1-1/4"	9' 0-5/8"	-5.00	-22.6	4' 11-3/8"	10' 1-5/16"
(1)	* 8' 9"	8' 8-3/8"	-5.00	-22.6	5' 10-7/16"	10' 11-1/2"

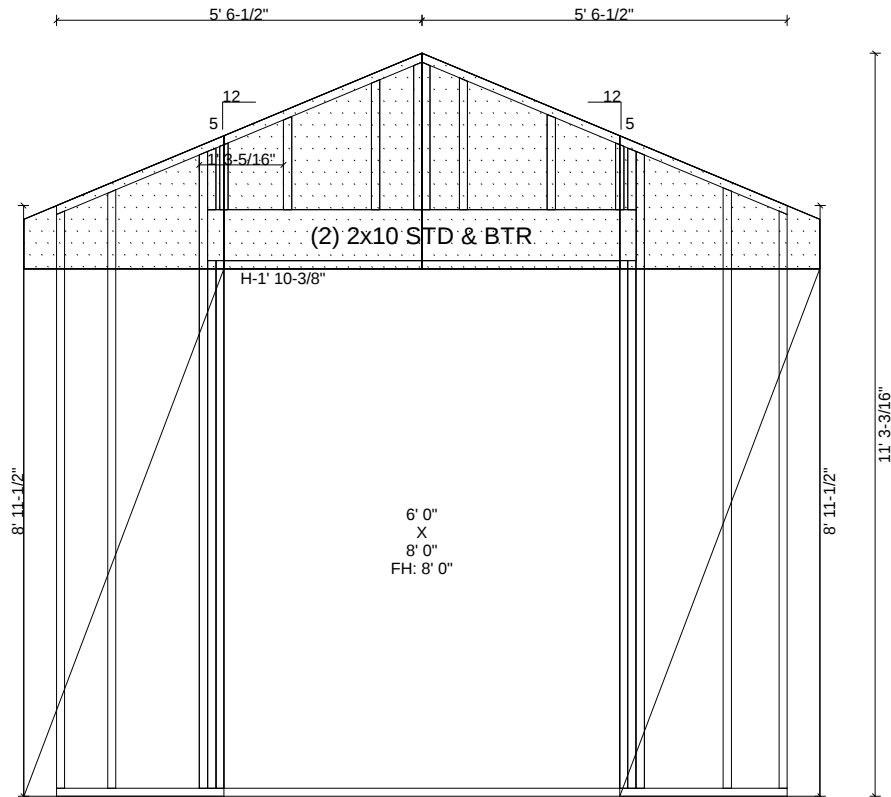

Panel Production Sheets

Job #Philis
Standard

Philis
Level 1

Date: 02/20/19
Page: 3
Bundle 2

Panel #1 (218.6 Bf)

Start Of Panel: 0"

Studs: 2X6 x 8' 8-5/8" (#2 SPF & BTR) [5] 1' 4" o.c.



(1) Top and (1) Bottom Plates: 2X6 x 13' 6" (#2 SPF & BTR)

*** Panel Diagonal 16' 2-1/2" ***

Insert	Start	End
* L CRNR(2X6) Down	@ Start	7"
*72x96-LB	4' 7"	10' 7"

Bottom Plate Lap: Flush

Start	Type	End
Flush	2' 8" x 8' 0" / 11-5/8" 7/16" OSB	
	1' 11" x 8' 0" / 11-5/8" 7/16" OSB	
	6' 0" x 1' 11-5/8" 7/16" OSB	
	6' 0" x 4' 0" / 1' 0" 7/16" OSB	
	2' 11" x 8' 0" / 11-5/8" 7/16" OSB	Flush

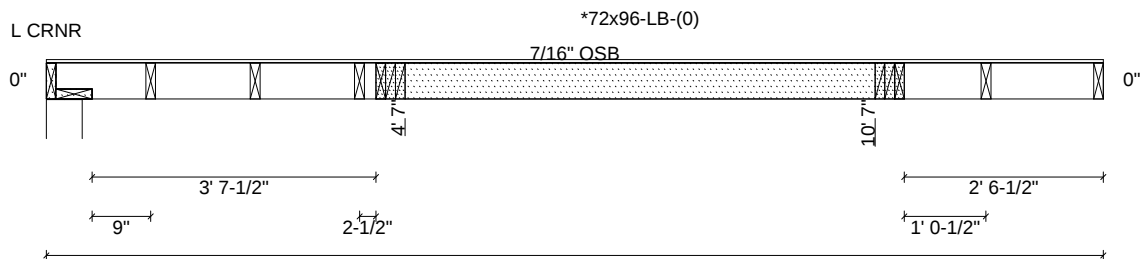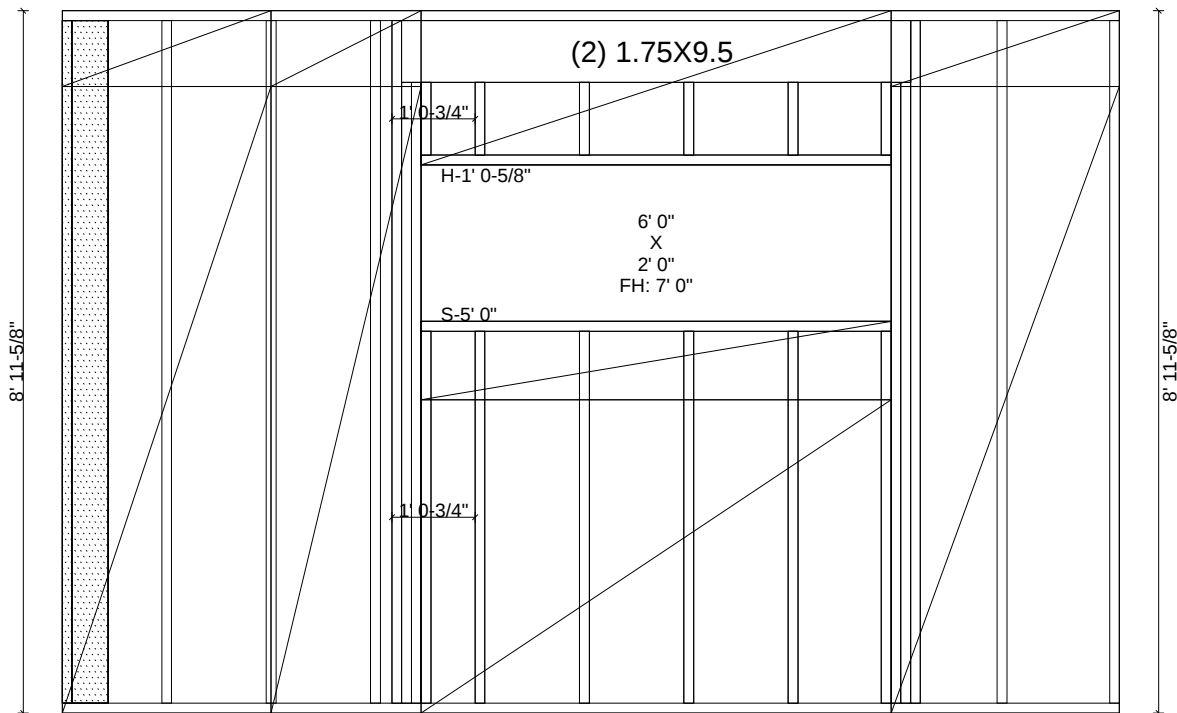

Panel Production Sheets

Job #Philis
Standard

Philis
Level 1

Date: 02/20/19
Page: 4
Bundle 2

Panel #31 (65.7 Bf)

Start Of Panel: 0"

Studs: 2X6 x 8' 8-5/8" (#2 SPF & BTR) [2] 1' 4" o.c.

(1) Top and (1) Bottom Plates: 2X6 x 4' 5-1/2" (#2 SPF & BTR)

*** Panel Diagonal 10' 0-3/16" ***



Insert	Start	End
* L CRNR(2X6) Up	@ Start	7"
L CRNR(2X6) Down *	3' 10-1/2"	@ End

Bottom Plate Lap: Flush

Start	Type	End
-------	------	-----

6-3/16" Open

3' 11-5/16" x 8' 0" / 11-5/8" 7/16" OSB Flush

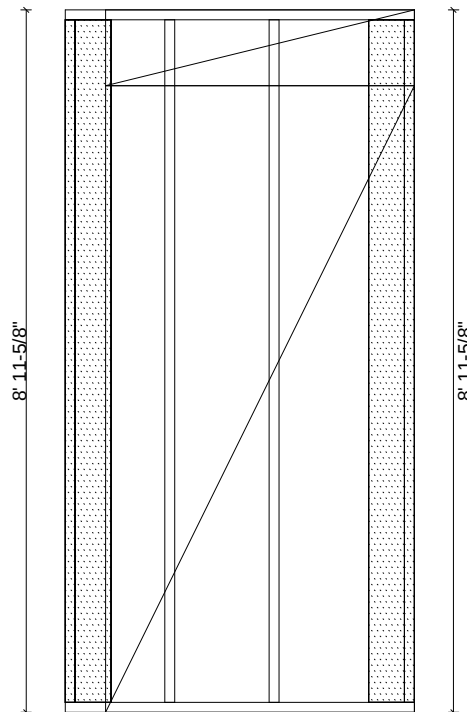

Panel Production Sheets

Job #Philis
Standard

Philis
Level 1

Date: 02/20/19
Page: 5
Bundle 2

Panel #2 (156.8 Bf)

Start Of Panel: 0"

Studs: 2X6 x 8' 8-5/8" (#2 SPF & BTR) [6] 1' 4" o.c.

(1) Top and (1) Bottom Plates: 2X6 x 10' 0" (#2 SPF & BTR)

*** Panel Diagonal 13' 5-3/16" ***

Insert	Start	End
* L CRNR(2X6) Up	1-9/16"	8-9/16"
30x54-LB	1' 5-1/2"	3' 11-1/2"

Bottom Plate Lap: Flush

Start	Type	End
-------	------	-----

6-3/16" Open



11-5/16" x 8' 0" / 11-5/8" 7/16" OSB

2' 6" x 1' 11-5/8" 7/16" OSB

2' 6" x 2' 6" 7/16" OSB

2' 8-1/2" x 8' 0" / 11-5/8" 7/16" OSB

3' 9-15/16" x 8' 0" / 11-5/8" 7/16" OSB Extend 5-15/16"

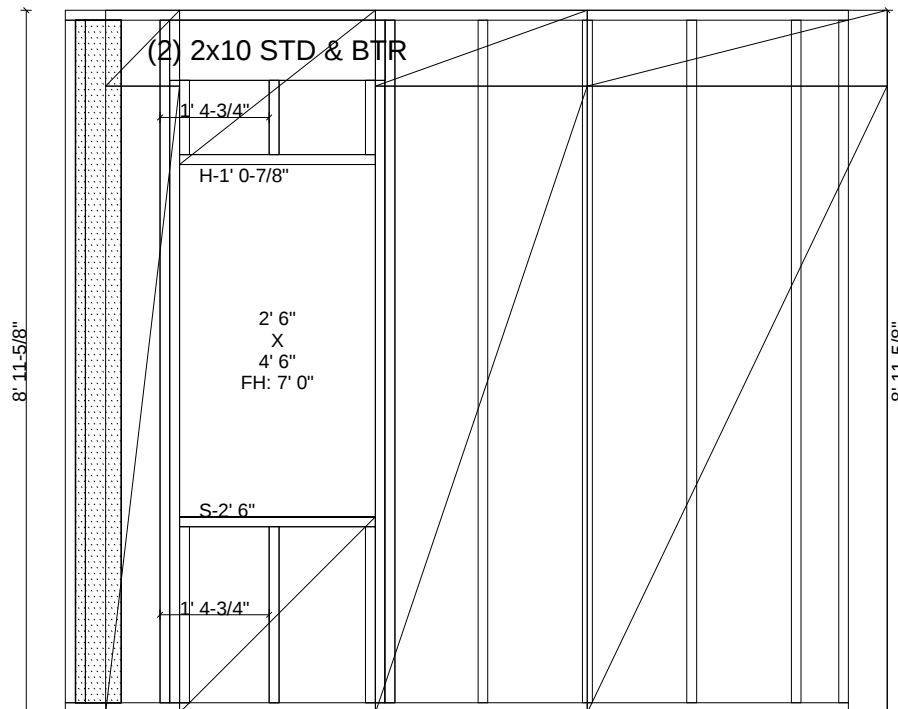

Panel Production Sheets

Job #Philis
Standard

Philis
Level 1

Date: 02/20/19
Page: 6
Bundle 2

Panel #3 (142.2 Bf)

Start Of Panel: 0"



Studs: 2X6 x 8' 8-5/8" (#2 SPF & BTR) [10] 1' 4" o.c.

(1) Top and (1) Bottom Plates: 2X6 x 12' 6-1/2" (#2 SPF & BTR)

*** Panel Diagonal 15' 5" ***

Insert	Start	End
* L CRNR(2X6) Down	@ Start	7"

Bottom Plate Lap: Flush	Start	Type	End
Flush	4' 0" x 8' 0"	/ 11-5/8"	7/16" OSB
	4' 0" x 8' 0"	/ 11-5/8"	7/16" OSB
	2' 8" x 8' 0"	/ 11-5/8"	7/16" OSB
	2' 4-7/16" x 8' 0"	/ 11-5/8"	7/16" OSB Extend 5-15/16"

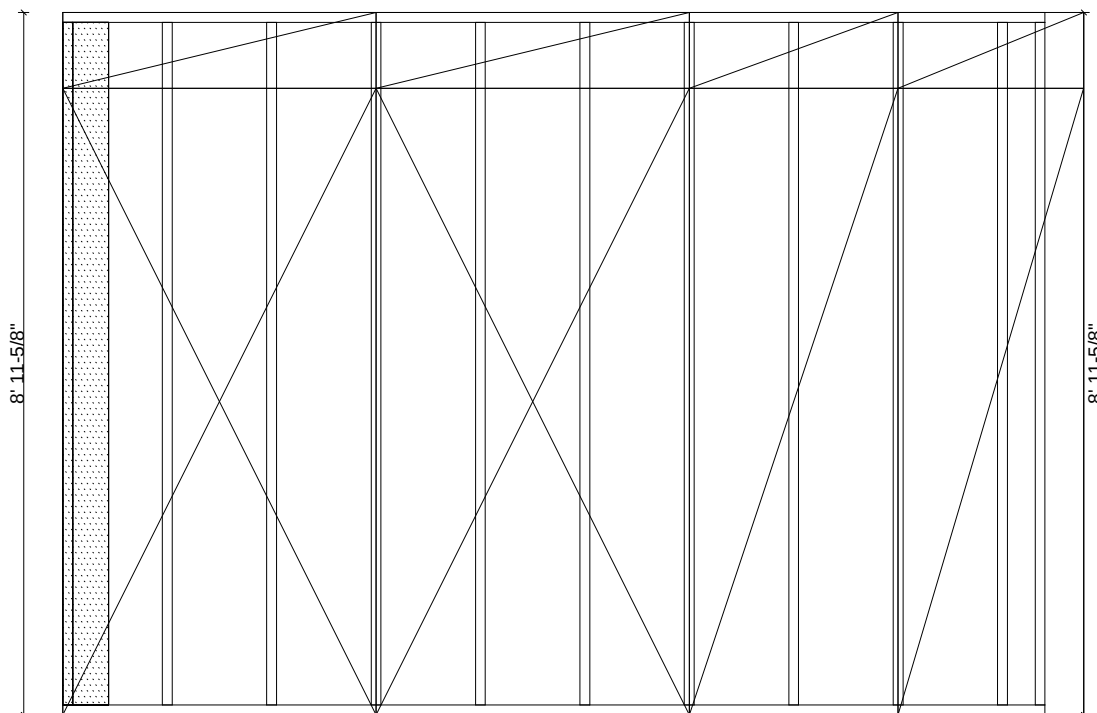

Panel Production Sheets

Job #Philis
Standard

Philis
Level 1

Date: 02/20/19
Page: 7
Bundle 2

Panel #4 (183.4 Bf)

Start Of Panel: 0"

Studs: 2X6 x 8' 8-5/8" (#2 SPF & BTR) [6] 1' 4" o.c.

(1) Top and (1) Bottom Plates: 2X6 x 10' 5-1/2" (#2 SPF & BTR)

*** Panel Diagonal 13' 9-5/16" ***



Insert	Start	End
* L CRNR(2X6) Down	@ Start	7"
30x54-LB	3' 0"	5' 6"
C premium(2X6) *	9' 8-15/16"	10' 3-15/16"

Bottom Plate Lap: Flush

Start	Type	End
Flush	3' 0" x 8' 0" / 11-5/8"	7/16" OSB
	2' 6" x 1' 11-5/8"	7/16" OSB
	2' 6" x 2' 6"	7/16" OSB
	2' 6" x 8' 0" / 11-5/8"	7/16" OSB
	1' 11-5/16" x 8' 0" / 11-5/8"	7/16" OSB
	6-3/16" Open	

Panel #4 Continued Next Page

Panel #4 (Continued)

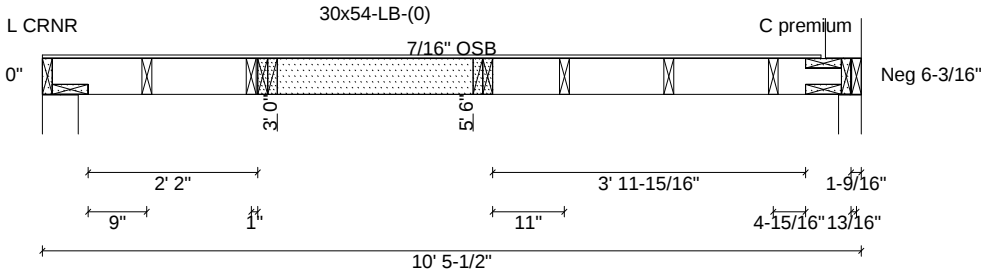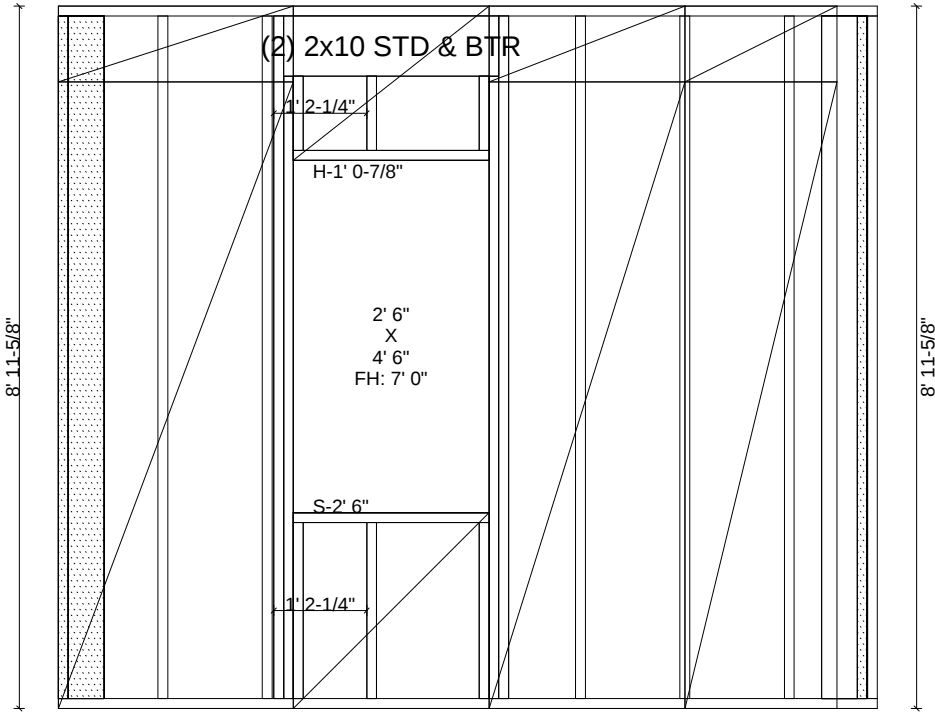

Panel Production Sheets

Job #Philis
Standard

Philis
Level 1

Date: 02/20/19
Page: 9
Bundle 2

Panel #5 (197.7 Bf)

Start Of Panel: 0"

Studs: 2X6 x 8' 8-5/8" (#2 SPF & BTR) [3] 1' 4" o.c.



(1) Top and (1) Bottom Plates: 2X6 x 12' 4" (#2 SPF & BTR)

*** Panel Diagonal 15' 3" ***

Insert	Start	End
72x24-LB	2' 11-1/4"	8' 11-1/4"
L CRNR(2X6) Down *	11' 9"	@ End

Bottom Plate Lap: Flush

Start	Type	End
Flush	2' 11-1/4" x 8' 0" / 11-5/8" 7/16" OSB	
	6' 0" x 1' 11-5/8" 7/16" OSB	
	6' 0" x 4' 0" / 1' 0" 7/16" OSB	
	3' 4-3/4" x 8' 0" / 11-5/8" 7/16" OSB	Flush

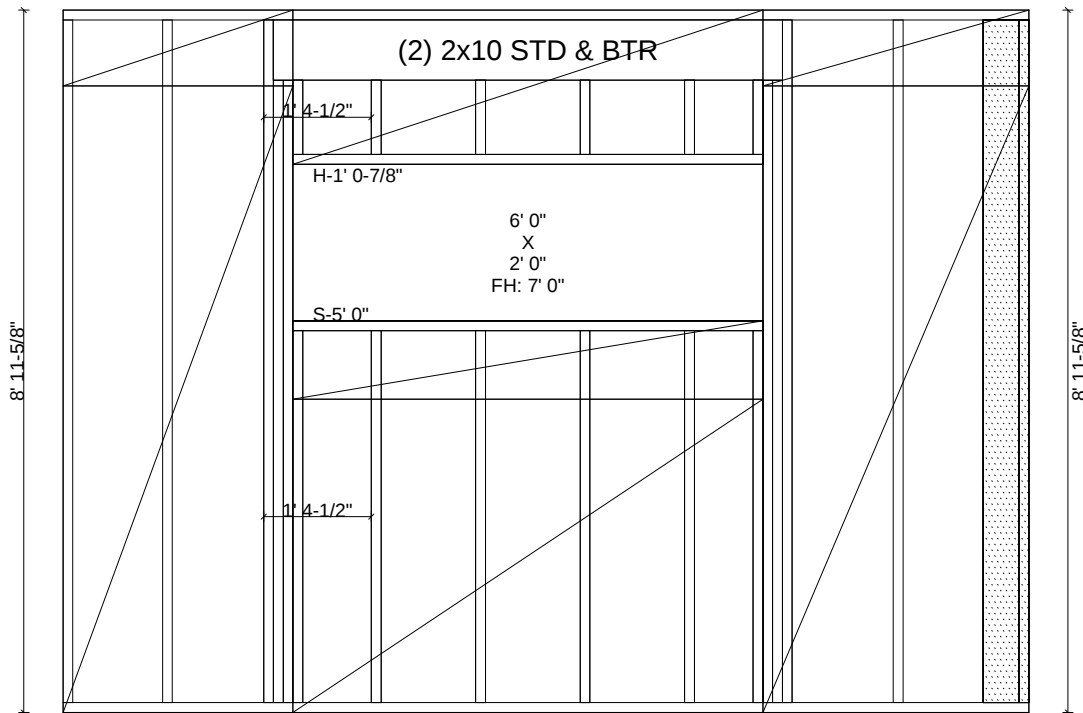

Panel Production Sheets

Job #Philis
Standard

Philis
Level 1

Date: 02/20/19
Page: 10
Bundle 2

Panel #6 (41.1 Bf)

Start Of Panel: 5-15/16"

Studs: 2X6 Sloped (#2 SPF & BTR) [2] 1' 4" o.c.

Top Plates: 2X6 (#2 SPF & BTR)

(1) 2' 2-5/8"

Start Rake Cut: 22.6 Deg /

End Rake Cut: 22.6 Deg /

TS: 2' 2"

Bottom: (1) 2X6 x 2' 0" (#2 SPF & BTR)

Insert	Start	End
L CRNR(2X6) Up *	1' 10-15/16"	@ End

Bottom Plate Lap: Flush

Start	Type	End
Extend 5-15/16"	1' 11-3/4" x 8' 0"	7/16" OSB


7/16" OSB	A: * 9"	B: 9-7/8"
	C: * 1' 6-15/16"	D: N.A.
	E: 1' 11-3/4"	F: N.A.
	G: 1' 11-3/4"	H: N.A.

6-3/16" Open

Quan.	Left Edge	Right Edge	Pitch (/12)	Angle	Top Plate Location	Bot. Plate Location
(1)	8' 8-3/8"	* 8' 9"	5.00	22.6	0"	0"
(1)	9' 0-1/4"	* 9' 0-7/8"	5.00	22.6	10-1/16"	9-5/16"

Panel #6 Continued Next Page

Panel #6 (Continued)

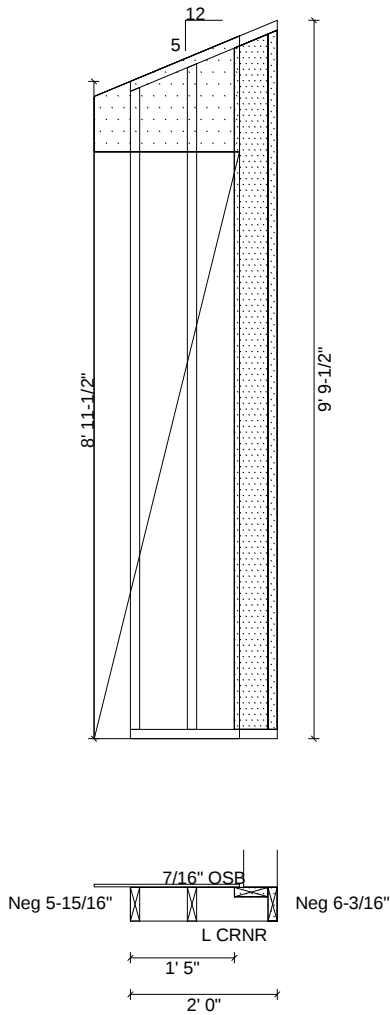

Panel Production Sheets

Job #Philis
Standard

Philis
Level 1

Date: 02/20/19
Page: 12
Bundle 2

Panel #7 (29.3 Bf)

Start Of Panel: 0"

Studs: 2X6 x 8' 8-5/8" (#2 SPF & BTR) [1] 1' 4" o.c.

(1) Top and (1) Bottom Plates: 2X6 x 2' 0" (#2 SPF & BTR)

The stud located at 1' 4" is omitted.



*** Panel Diagonal 9' 2-1/4" ***

Insert	Start	End

L2x4 Down *	1' 6-1/2"	1' 11-1/2"

Bottom Plate Lap: Flush		
Start	Type	End

Flush	2' 0" x 8' 0" / 11-5/8"	7/16" OSB Flush

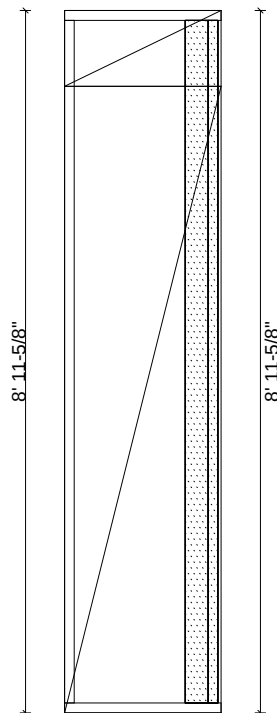

Panel Production Sheets

Job #Philis
Standard

Philis
Level 1

Date: 02/20/19
Page: 13
Bundle 2

Panel #9 (38.0 Bf)

Start Of Panel: 0"

Studs: 2X6 x 8' 8-5/8" (#2 SPF & BTR) [2] 1' 4" o.c.



(1) Top and (1) Bottom Plates: 2X6 x 2' 0" (#2 SPF & BTR)

*** Panel Diagonal 9' 2-1/4" ***

Insert	Start	End
* L2x4 Down	7/16"	5-7/16"

Bottom Plate Lap: Flush

Start	Type	End
Flush	2' 0" x 8' 0" / 11-5/8"	7/16" OSB
		Flush

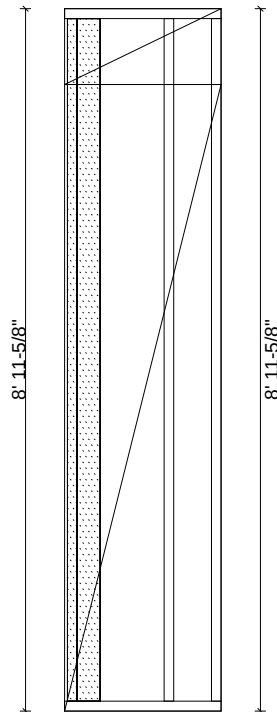

Panel Production Sheets

Job #Philis
Standard

Philis
Level 1

Date: 02/20/19
Page: 14
Bundle 2

Panel #10 (41.0 Bf)

Start Of Panel: 0"

Studs: 2X6 Sloped (#2 SPF & BTR) [2] 1' 4" o.c.

Top Plates: 2X6 (#2 SPF & BTR)

(1) 2' 2-5/8"

Start Rake Cut: 112.6 Deg \

End Rake Cut: 112.6 Deg \

TS: 2' 2"

Bottom: (1) 2X6 x 2' 0" (#2 SPF & BTR)

Insert	Start	End
* L CRNR(2X6) Up	@ Start	7"

Bottom Plate Lap: Flush

Start	Type	End
-------	------	-----

6-3/16" Open

1' 11-3/4" x 8' 0" 7/16" OSB

7/16" OSB

A: * 1' 6-15/16"

B: N.A.

C: * 9"

D: 9-7/8"

E: 1' 11-3/4"

F: N.A.

G: 1' 11-3/4"



H: N.A.

Extend 5-15/16"

Quan.	Left Edge	Right Edge	Pitch (/12)	Angle	Top Plate Location	Bot. Plate Location
(1)	* 9' 0"	8' 11-3/8"	-5.00	-22.6	1' 4-1/2"	1' 3-1/4"
(1)	* 8' 9"	8' 8-3/8"	-5.00	-22.6	2' 0-3/8"	1' 10-1/2"

Panel #10 Continued Next Page

Panel #10 (Continued)

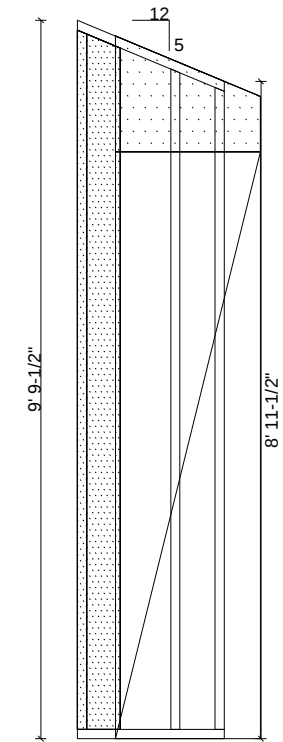

Panel Production Sheets

Job #Philis
Standard

Philis
Level 1

Date: 02/20/19
Page: 16
Bundle 2

Panel #8 (152.2 Bf)

Start Of Panel: 5-15/16"

Studs 2X6 x Neg 0" (#2 SPF & BTR) [0] 1' 4" o.c.

Top Plates: 2X6 (#2 SPF & BTR)

(1) 3' 10-11/16"

Start Rake Cut: 22.6 Deg /

End Rake Cut: 22.6 Deg /

TS: 3' 10-1/16"

(1) 3' 10-11/16"

Start Rake Cut: 112.6 Deg \

End Rake Cut: 112.6 Deg \

TS: 3' 10-1/16"

Bottom: (1) 2X6 x 7' 1" (#2 SPF & BTR)

Insert	Start	End
-LB	9-7/16"	7' 3-7/16"

Bottom Plate Lap: Flush

Start	Type	End
Extend 5-15/16"	9-7/16" x 8' 0" 7/16" OSB	

7/16" OSB	A: * 1' 7"	B: 3-15/16"
	C: * 1' 10-15/16"	D: N.A.
	E: 9-7/16"	F: N.A.
	G: 9-7/16"	H: N.A.

2' 0" Open

3" x 4' 0" 7/16" OSB

2' 0" Open

3" x 4' 0" 7/16" OSB

7/16" OSB	A: * 2' 2-15/16"	B: 1' 4-1/4"
	C: * 3' 7-3/16"	D: N.A.
	E: 3' 3"	F: N.A.
	G: 3' 3"	H: N.A.

7/16" OSB	A: * 3' 7-3/16"	B: N.A.
	C: * 2' 2-15/16"	D: 1' 4-1/4"
	E: 3' 3"	F: N.A.
	G: 3' 3"	H: N.A.

3' 3" x 3' 8" 7/16" OSB

Date: 02/20/19
Page: 17
Bundle 2

Panel Production Sheets

Job #Philis
Standard

Philis
Level 1

Date: 02/20/19
Page: 18
Bundle 2

Panel #11 (172.5 Bf)

Start Of Panel: 0"



Studs: 2X6 x 8' 8-5/8" (#2 SPF & BTR) [7] 1' 4" o.c.

(1) Top and (1) Bottom Plates: 2X6 x 12' 4" (#2 SPF & BTR)

*** Panel Diagonal 15' 3" ***

Insert	Start	End
* L CRNR(2X6) Down	@ Start	7"
30x54-LB	6' 7"	9' 1"

Bottom Plate Lap: Flush	Start	Type	End
Flush	4' 0" x 8' 0"	/ 11-5/8"	7/16" OSB
	2' 7" x 8' 0"	/ 11-5/8"	7/16" OSB
	2' 6" x 1' 11-5/8"	7/16" OSB	
	2' 6" x 2' 6"	7/16" OSB	
	3' 3" x 8' 0"	/ 11-5/8"	7/16" OSB
			Flush

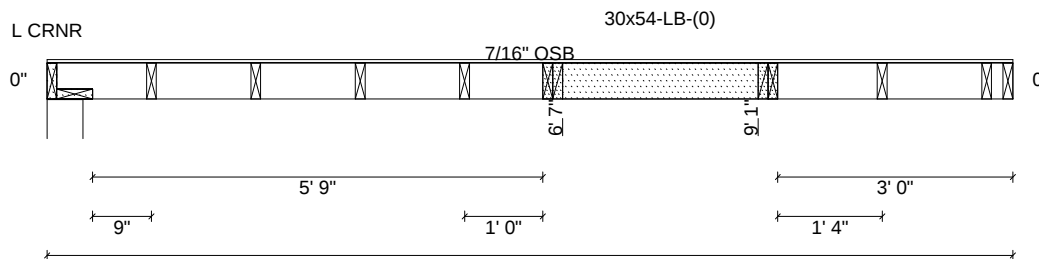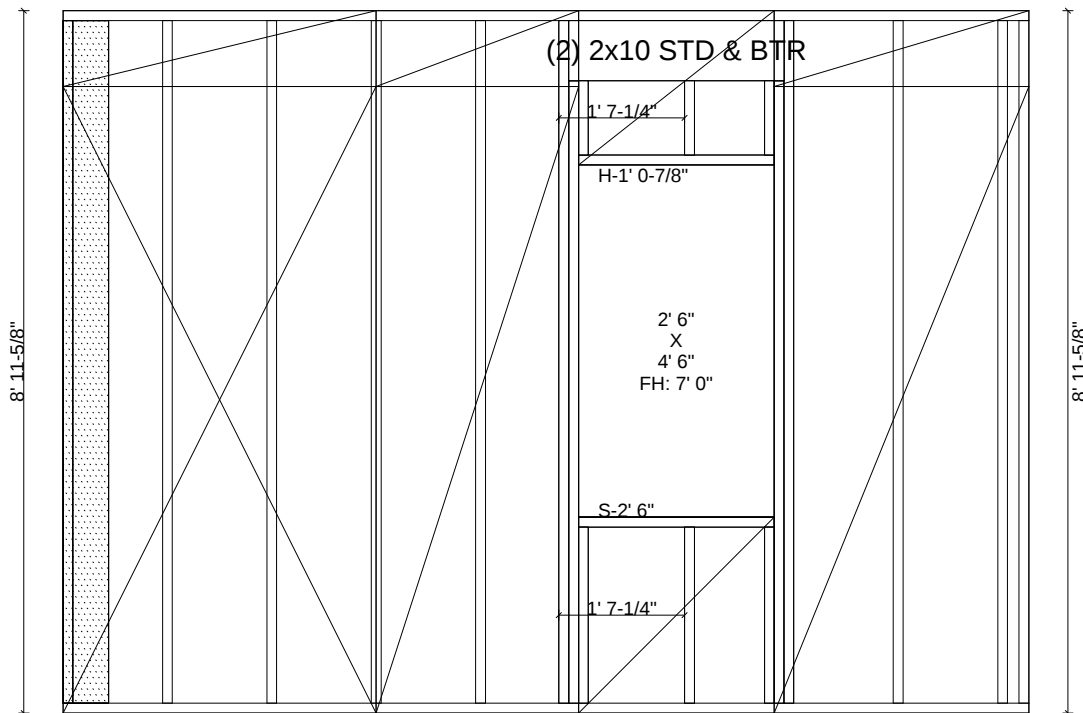

Panel Production Sheets

Job #Philis
Standard

Philis
Level 1

Date: 02/20/19
Page: 19
Bundle 2

Panel #12 (146.3 Bf)

Start Of Panel: 0"

Studs: 2X6 x 8' 8-5/8" (#2 SPF & BTR) [3] 1' 4" o.c.



(1) Top and (1) Bottom Plates: 2X6 x 7' 5-1/2" (#2 SPF & BTR)

*** Panel Diagonal 11' 8" ***

Insert	Start	End
* L CRNR(2X6) Up	1-9/16"	8-9/16"
36x54-LB	2' 5-1/2"	5' 5-1/2"
SS	7' 2-7/16"	7' 5-7/16"

Bottom Plate Lap: Flush

Start	Type	End
6-3/16" Open		
1' 11-5/16" x 8' 0" / 11-5/8"	7/16" OSB	
3' 0" x 1' 11-5/8"	7/16" OSB	
3' 0" x 2' 6"	7/16" OSB	
2' 0" x 8' 0" / 11-5/8"	7/16" OSB	Flush

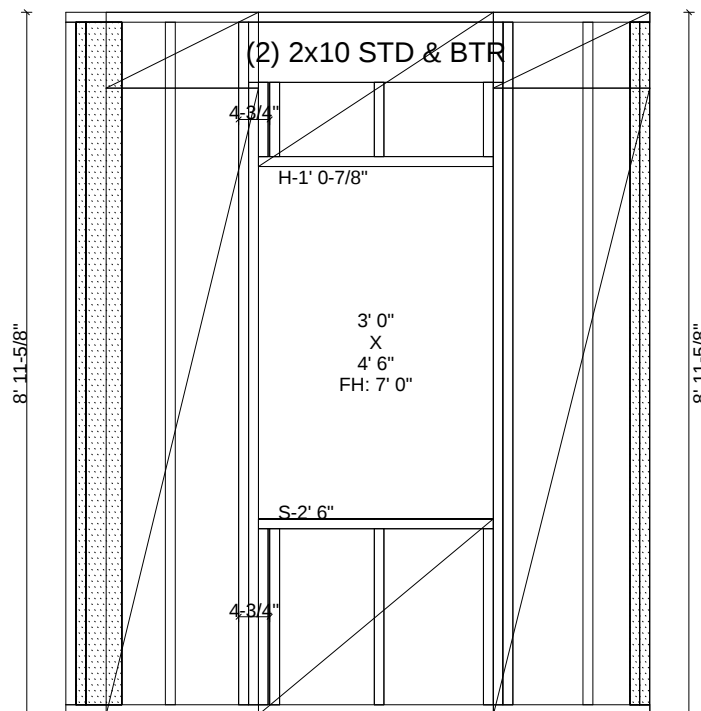

Panel Production Sheets

Job #Philis
Standard

Philis
Level 1

Date: 02/20/19
Page: 20
Bundle 2

Panel #13 (65.2 Bf)

Start Of Panel: 0"

Studs: 2X6 x 8' 8-5/8" (#2 SPF & BTR) [2] 1' 4" o.c.

(1) Top and (1) Bottom Plates: 2X6 x 4' 5-1/2" (#2 SPF & BTR)

*** Panel Diagonal 10' 0-3/16" ***



Insert	Start	End
* L CRNR(2X6) Up	@ Start	7"
L CRNR(2X6) Down *	3' 10-1/2"	@ End

Bottom Plate Lap: Flush

Start	Type	End
-------	------	-----

6-3/16" Open

3' 11-5/16" x 8' 0" / 11-5/8" 7/16" OSB Flush

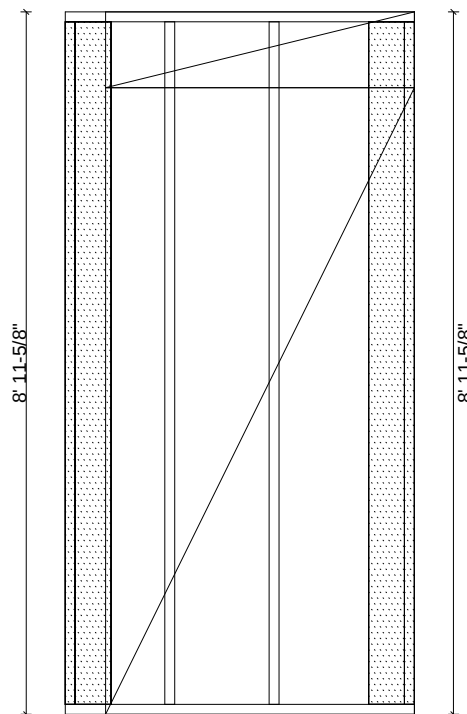

Panel Production Sheets

Job #Philis
Standard

Philis
Level 1

Date: 02/20/19
Page: 1
Bundle 3

Panel #17 (245.5 Bf)

Start Of Panel: 0"

Studs: 2X6 x 8' 8-5/8" (#2 SPF & BTR) [4] 1' 4" o.c.

(1) Top and (1) Bottom Plates: 2X6 x 12' 4" (#2 SPF & BTR)

*** Panel Diagonal 15' 3" ***

Insert	Start	End
*24x24-LB	2' 6-1/2"	4' 6-1/2"
* L premium(2X6) Down	4' 11"	5' 6"
30x54-LB	8' 10-1/2"	11' 4-1/2"
L CRNR(2X6) Down *	11' 9"	@ End

Bottom Plate Lap: Flush

Start	Type	End
Flush	2' 6-1/2" x 8' 0" / 11-5/8" 7/16" OSB	
	2' 0" x 1' 11-5/8" 7/16" OSB	
	2' 0" x 4' 0" / 1' 0" 7/16" OSB	
	2' 1-1/2" x 8' 0" / 11-5/8" 7/16" OSB	
	2' 2-1/2" x 8' 0" / 11-5/8" 7/16" OSB	
	2' 6" x 1' 11-5/8" 7/16" OSB	
	2' 6" x 2' 6" 7/16" OSB	
	11-1/2" x 8' 0" / 11-5/8" 7/16" OSB	Flush

Panel #17 Continued Next Page

Panel Production Sheets

Job #Philis
Standard



Philis
Level 1

Date: 02/20/19

Page: 2

Bundle 3

Panel #17 (Continued)

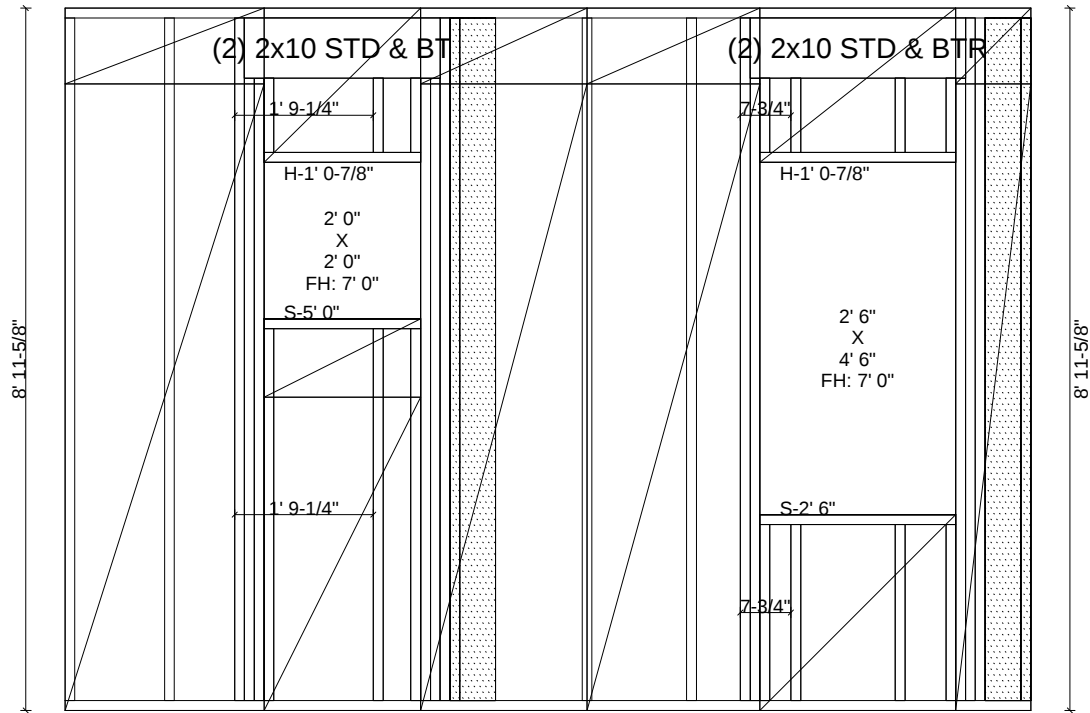

Panel Production Sheets

Job #Philis
Standard

Philis
Level 1

Date: 02/20/19
Page: 3
Bundle 3

Panel #16 (137.2 Bf)

Start Of Panel: 0"

Studs: 2X6 x 8' 8-5/8" (#2 SPF & BTR) [1] 1' 4" o.c.

(1) Top and (1) Bottom Plates: 2X6 x 7' 5-1/2" (#2 SPF & BTR)

The stud located at 5' 4" is omitted.

The stud located at 6' 8" is omitted.

*** Panel Diagonal 11' 8" ***

Insert	Start	End
SS	@ Start	3"
36x54-LB	2' 0"	5' 0"
Loose Stud	6' 1-1/4"	6' 2-3/4"
L CRNR(2X6) Up *	6' 10-1/2"	@ End

Bottom Plate Lap: Flush

Start	Type	End
Flush	2' 0" x 8' 0" / 11-5/8"	7/16" OSB
	3' 0" x 1' 11-5/8"	7/16" OSB
	3' 0" x 2' 6"	7/16" OSB
	1' 11-5/16" x 8' 0" / 11-5/8"	7/16" OSB
	6-3/16" Open	

Panel #16 Continued Next Page



Panel Production Sheets

Job #Philis
Standard

Philis
Level 1

Date: 02/20/19
Page: 4
Bundle 3

Panel #16 (Continued)

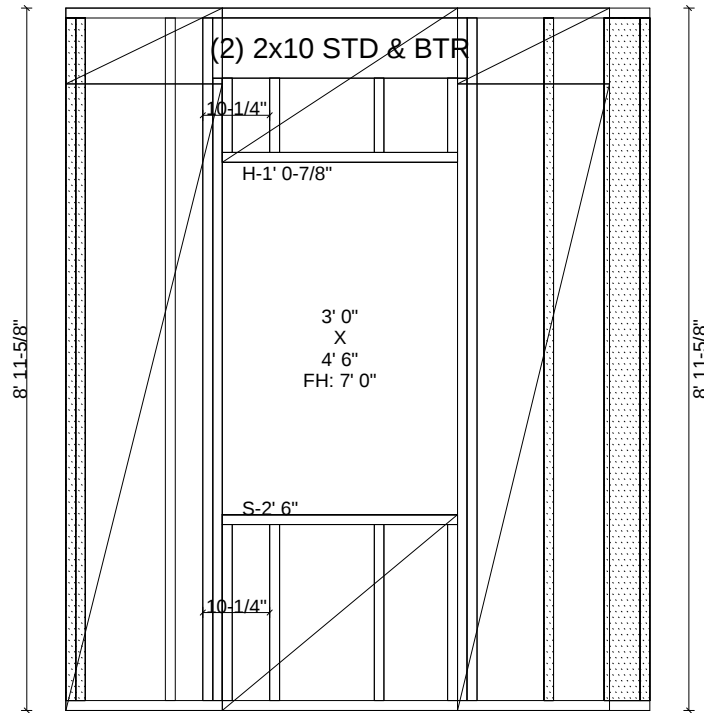

Panel Production Sheets

Job #Philis
Standard

Philis
Level 1

Date: 02/20/19
Page: 5
Bundle 3

Panel #15 (65.7 Bf)

Start Of Panel: 0"

Studs: 2X6 x 8' 8-5/8" (#2 SPF & BTR) [2] 1' 4" o.c.



(1) Top and (1) Bottom Plates: 2X6 x 4' 5-1/2" (#2 SPF & BTR)

*** Panel Diagonal 10' 0-3/16" ***

Insert	Start	End
* L CRNR(2X6) Down	@ Start	7"
L CRNR(2X6) Up *	3' 10-1/2"	@ End

Bottom Plate Lap: Flush

Start	Type	End
Flush	3' 11-5/16" x 8' 0" / 11-5/8" 7/16" OSB 6-3/16" Open	

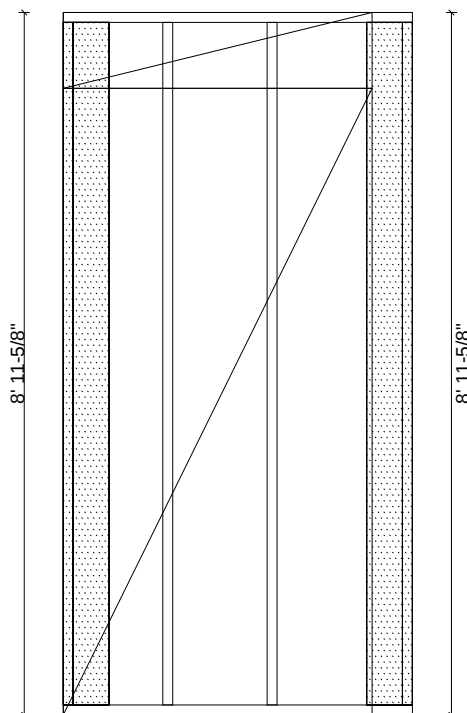

Panel Production Sheets

Job #Philis
Standard

Philis
Level 1

Date: 02/20/19
Page: 6
Bundle 3

Panel #14 (157.8 Bf)

Start Of Panel: 5-15/16"

Studs: 2X6 Sloped (#2 SPF & BTR) [2] 1' 4" o.c.

Top Plates: 2X6 (#2 SPF & BTR)

(1) 5' 6-1/2"

Start Rake Cut: 33.7 Deg /

End Rake Cut: 33.7 Deg /

TS: 5' 5-1/2"

(1) 5' 6-1/2"

Start Rake Cut: 123.7 Deg \

End Rake Cut: 123.7 Deg \

TS: 5' 5-1/2"

Bottom: (1) 2X6 x 9' 1" (#2 SPF & BTR)

The stud located at 8' 10-1/16" is omitted.

The stud located at 10-1/16" is omitted.

Insert	Start	End
front-LB	2' 3-15/16"	7' 8-15/16"

Bottom Plate Lap: Flush

Start	Type	End
Extend 5-15/16"	2' 3-15/16" x 8' 0"	7/16" OSB

7/16" OSB	A: * 1' 11-1/16"	B: 1' 6-5/8"
	C: * 3' 5-11/16"	D: N.A.
	E: 2' 3-15/16"	F: N.A.
	G: 2' 3-15/16"	H: N.A.

2' 8-1/2" x 4' 0" 7/16" OSB

7/16" OSB	A: * 7-3/16"	B: 1' 9-11/16"
	C: * 2' 4-13/16"	D: N.A.
	E: 2' 8-1/2"	F: N.A.
	G: 2' 8-1/2"	H: N.A.



2' 8-1/2" x 4' 0" 7/16" OSB

7/16" OSB	A: * 2' 4-13/16"	B: N.A.
	C: * 7-3/16"	D: 1' 9-11/16"
	E: 2' 8-1/2"	F: N.A.
	G: 2' 8-1/2"	H: N.A.

-Bundle 3

Extend 5-15/16"

Quan.	Left Edge		Right Edge	Pitch (/12)	Angle	Top Plate Location	Bot. Plate Location
(1)	9' 11-11/16"	*	10' 0-11/16"	8.00	33.7	0"	0"
(1)	* 10' 0-11/16"		9' 11-11/16"	-8.00	-33.7	5' 3-11/16"	8' 11-1/2"

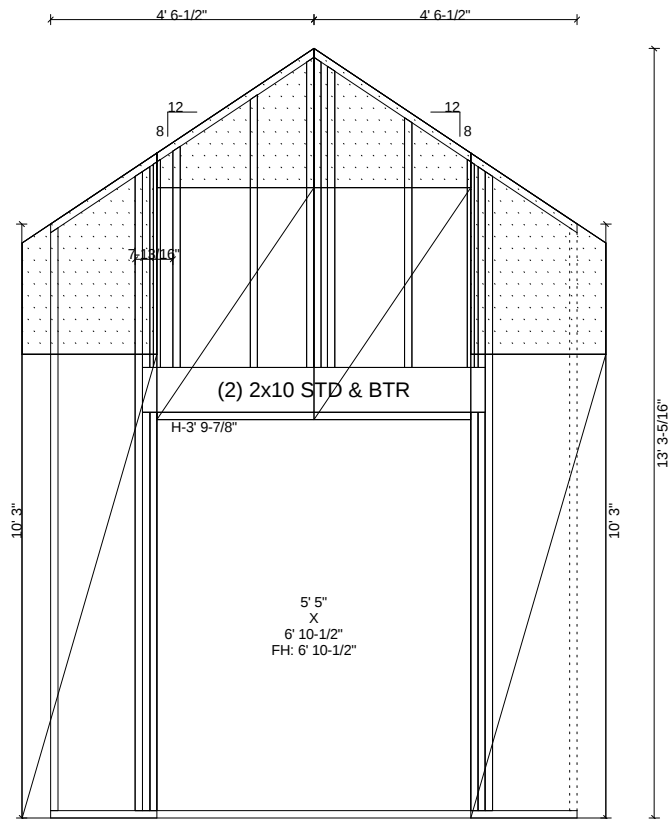

Panel Production Sheets

Job #Philis
Standard

Philis
Level 1

Date: 02/20/19
Page: 8
Bundle 3

Panel #18 (220.4 Bf)

Start Of Panel: 1' 9-15/16"

Studs: 2X6 x 8' 8-5/8" (#2 SPF & BTR) [9] 1' 4" o.c.



(1) Top and (1) Bottom Plates: 2X6 x 15' 6" (#2 SPF & BTR)

*** Panel Diagonal 17' 10-7/8" ***

Insert	Start	End
L premium(2X6) Down *	10' 3-3/16"	10' 10-3/16"
entry-LB	11' 3-7/16"	14' 1-7/16"
SSSS	14' 7-3/16"	15' 1-3/16"

Bottom Plate Lap: Flush

Start	Type	End
Extend 5-15/16"	4' 0" x 8' 0" / 11-5/8" 7/16" OSB	
	4' 0" x 8' 0" / 11-5/8" 7/16" OSB	
	1' 11-7/16" x 8' 0" / 11-5/8" 7/16" OSB	
	2' 10" x 9-3/8" 7/16" OSB	
	3' 8-7/16" x 8' 0" / 11-5/8" 7/16" OSB	Extend 5-15/16"

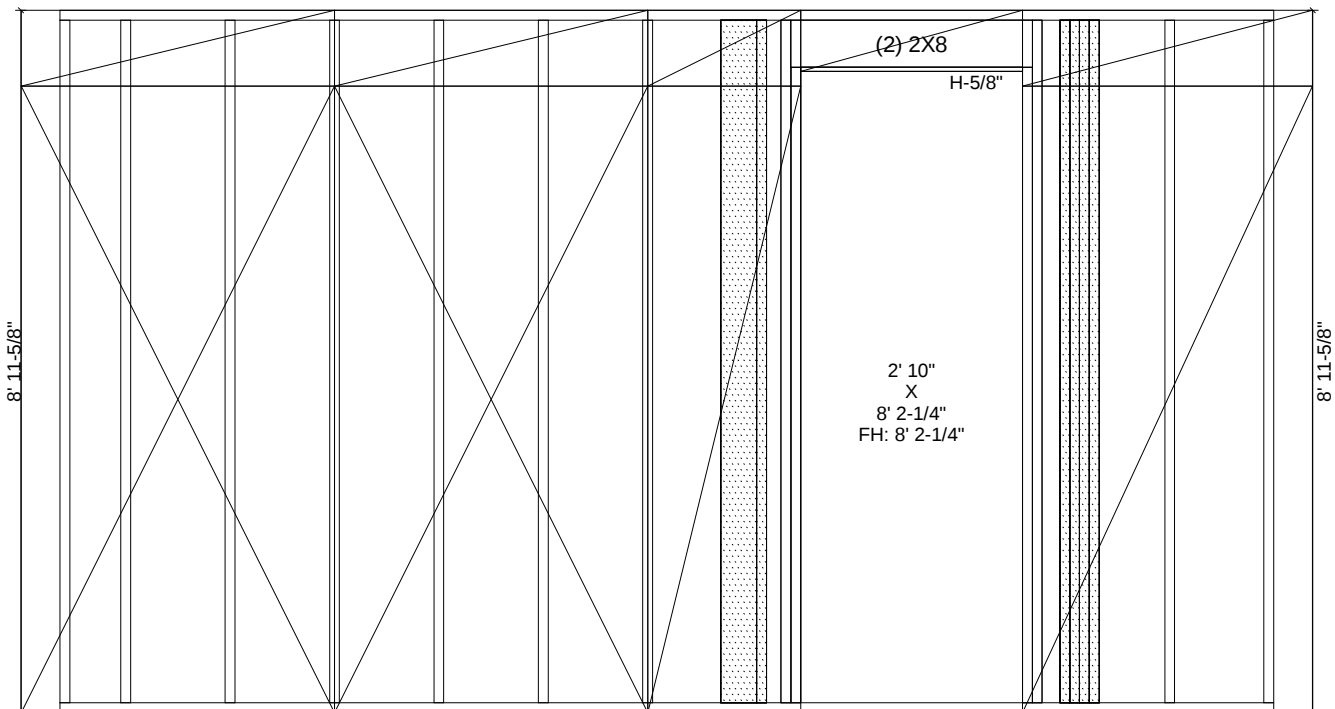

Panel Production Sheets

Job #Philis
Standard

Philis
Level 1

Date: 02/20/19
Page: 9
Bundle 3

Panel #19 (61.7 Bf)

Start Of Panel: 0"

Studs: 2X6 x 8' 8-5/8" (#2 SPF & BTR) [2] 1' 4" o.c.



(1) Top and (1) Bottom Plates: 2X6 x 3' 5-1/2" (#2 SPF & BTR)

*** Panel Diagonal 9' 7-3/8" ***

Insert	Start	End
* L CRNR(2X6) Down	@ Start	7"
L CRNR(2X6) Up *	2' 10-1/2"	@ End

Bottom Plate Lap: Flush

Start	Type	End
Flush	2' 11-5/16" x 8' 0" / 11-5/8" 7/16" OSB 6-3/16" Open	

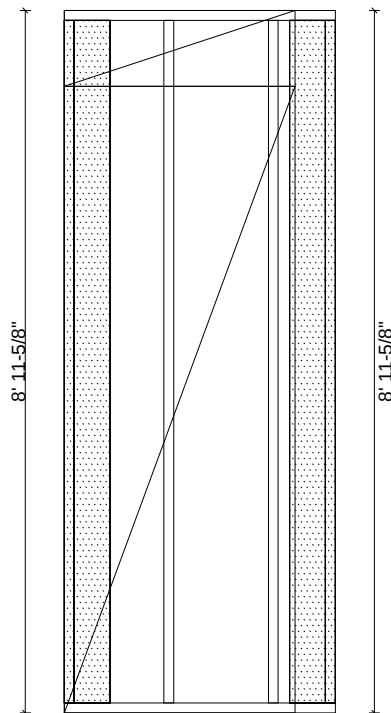

Panel Production Sheets

Job #Philis
Standard

Philis
Level 1

Date: 02/20/19
Page: 10
Bundle 3

Panel #20 (83.0 Bf)

Start Of Panel: 0"

Studs: 2X6 x 8' 8-5/8" (#2 SPF & BTR) [7] 1' 4" o.c.


(1) Top and (1) Bottom Plates: 2X6 x 7' 1-1/2" (#2 SPF & BTR)

*** Panel Diagonal 11' 5-7/16" ***

Bottom Plate Lap: Flush
Start Type

End

Flush 4' 0" x 8' 0" / 11-5/8" 7/16" OSB
3' 7-7/16" x 8' 0" / 11-5/8" 7/16" OSB Extend 5-15/16"

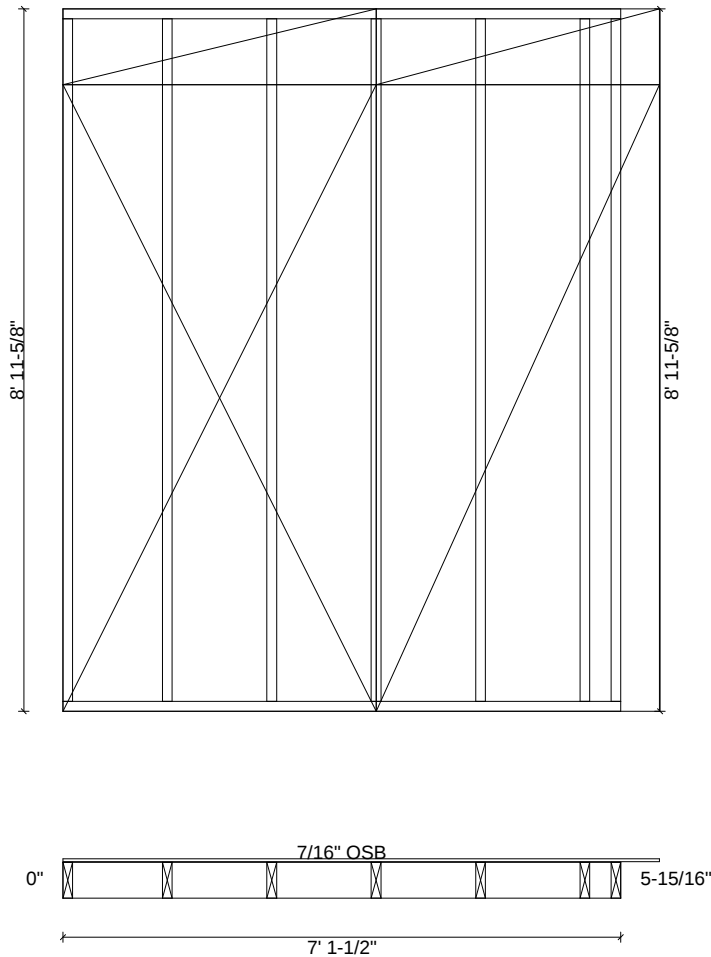

Panel Production Sheets

Job #Philis
Standard

Philis
Level 1

Date: 02/20/19
Page: 11
Bundle 3

Panel #21 (161.3 Bf)

Start Of Panel: 0"

Studs: 2X6 x 8' 8-5/8" (#2 SPF & BTR) [7] 1' 4" o.c.



(1) Top and (1) Bottom Plates: 2X6 x 10' 8" (#2 SPF & BTR)

*** Panel Diagonal 13' 11-1/4" ***

Insert	Start	End
* L CRNR(2X6) Down	@ Start	7"
SS	6' 7"	6' 10"
* L premium(2X6) Down	6' 10"	7' 5"
L premium(2X6) Down *	9' 10-1/4"	10' 5-1/4"

Bottom Plate Lap: Flush

Start	Type	End
Flush	2' 8" x 8' 0" / 11-5/8"	7/16" OSB
	4' 0" x 8' 0" / 11-5/8"	7/16" OSB
	4' 0" x 8' 0" / 11-5/8"	7/16" OSB
		Flush

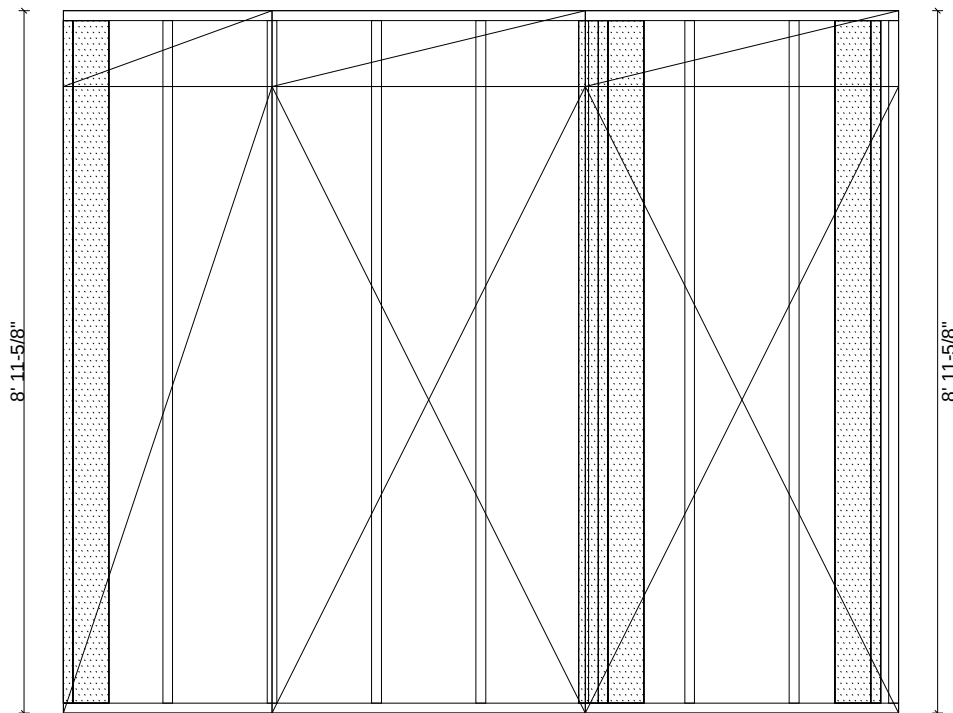

Panel Production Sheets

Job #Philis
Standard

Philis
Level 1

Date: 02/20/19
Page: 12
Bundle 3

Panel #22 (229.4 Bf)

Start Of Panel: 0"

Studs: 2X6 x 8' 8-5/8" (#2 SPF & BTR) [4] 1' 4" o.c.

(1) Top and (1) Bottom Plates: 2X6 x 12' 0" (#2 SPF & BTR)

The stud located at 9' 4" is omitted.

The stud located at 8' 0" is omitted.

*** Panel Diagonal 14' 11-3/4" ***

Insert	Start	End
24x24-LB	1' 0"	3' 0"
30x48-LB	4' 10"	7' 4"
Loose Stud	8' 5-1/4"	8' 6-3/4"
L premium(2X6) Down *	9' 5-1/2"	10' 0-1/2"
S	10' 0-1/2"	10' 2"

Bottom Plate Lap: Flush

Start	Type	End
1' 0" x 8' 0"	/ 11-5/8"	7/16" OSB
2' 0" x 1' 11-5/8"	7/16"	OSB
2' 0" x 4' 0"	/ 1' 0"	7/16" OSB
1' 10" x 8' 0"	/ 11-5/8"	7/16" OSB
2' 6" x 1' 11-5/8"	7/16"	OSB
2' 6" x 3' 0"	7/16"	OSB
8" x 8' 0"	/ 11-5/8"	7/16" OSB
4' 0" x 8' 0"	/ 11-5/8"	7/16" OSB
		Flush

Panel #22 Continued Next Page


Panel Production Sheets

Job #Philis
Standard

Philis
Level 1

Date: 02/20/19
Page: 13
Bundle 3

Panel #22 (Continued)

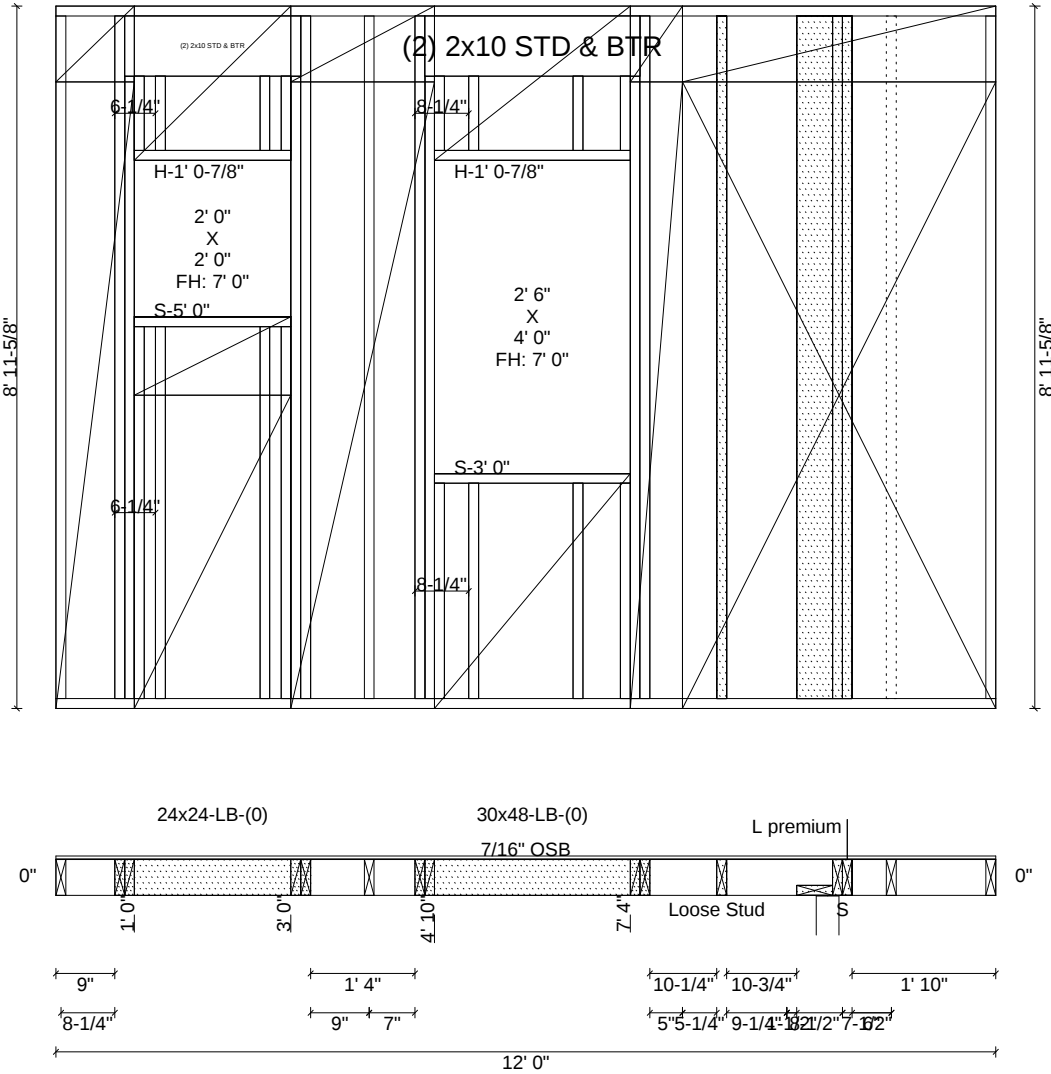

Panel Production Sheets

Job #Philis
Standard

Philis
Level 1

Date: 02/20/19
Page: 14
Bundle 3

Panel #23 (180.5 Bf)

Start Of Panel: 0"



Studs: 2X6 x 8' 8-5/8" (#2 SPF & BTR) [4] 1' 4" o.c.

(1) Top and (1) Bottom Plates: 2X6 x 10' 8-1/2" (#2 SPF & BTR)

*** Panel Diagonal 13' 11-5/8" ***

Insert	Start	End
72x24-LB	1' 4"	7' 4"

Bottom Plate Lap: Flush	Type	End
1' 4" x 8' 0" / 11-5/8"	7/16" OSB	
6' 0" x 1' 11-5/8"	7/16" OSB	
6' 0" x 4' 0" / 1' 0"	7/16" OSB	
3' 10-7/16" x 8' 0" / 11-5/8"	7/16" OSB	Extend 5-15/16"

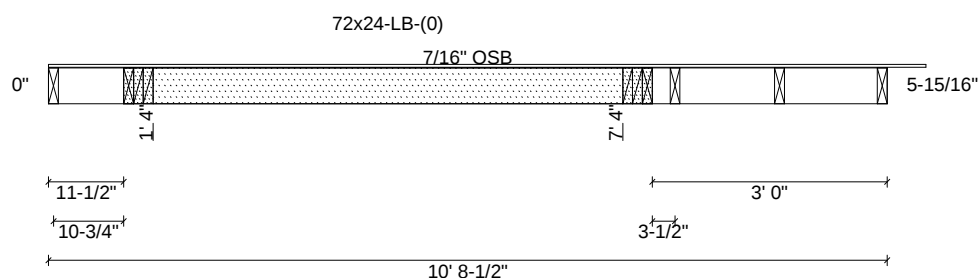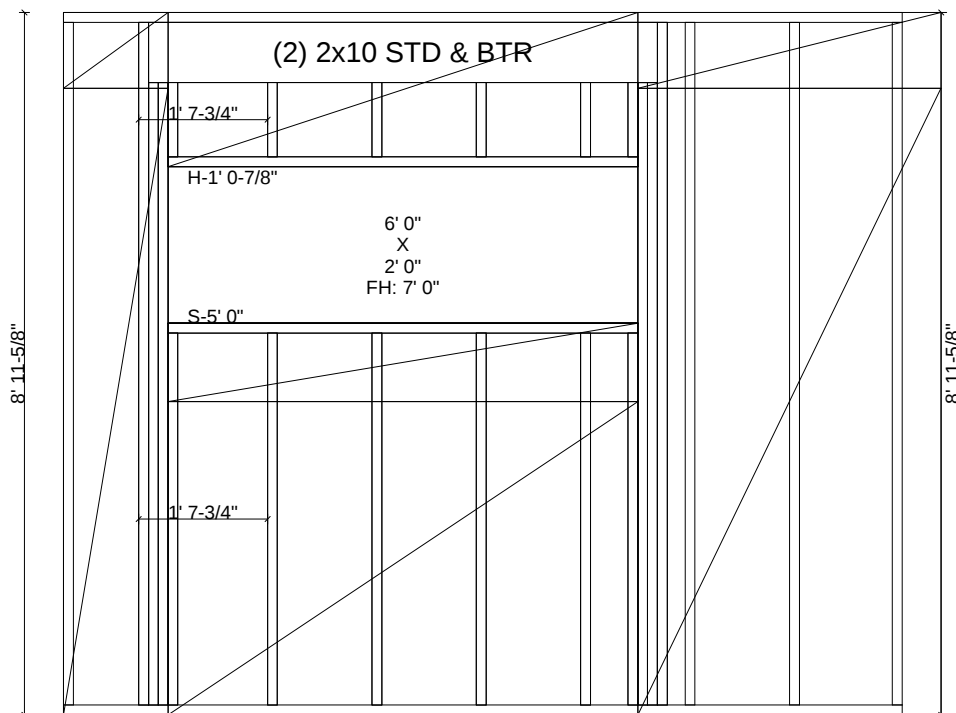

Panel Production Sheets

Job #Philis
Standard

Philis
Level 1

Date: 02/20/19
Page: 15
Bundle 3

Panel #24 (216.2 Bf)

Start Of Panel: 0"

Studs: 2X6 x 8' 8-5/8" (#2 SPF & BTR) [6] 1' 4" o.c.



(1) Top and (1) Bottom Plates: 2X6 x 16' 0" (#2 SPF & BTR)

*** Panel Diagonal 18' 4-1/8" ***

Insert	Start	End
* L CRNR(2X6) Down	@ Start	7"
SS	4' 0-3/4"	4' 3-3/4"
96x96-LB	6' 0"	14' 0"

Bottom Plate Lap: Flush

Start	Type	End
Flush	4' 0" x 8' 0" / 11-5/8"	7/16" OSB
	2' 0" x 8' 0" / 11-5/8"	7/16" OSB
	8' 0" x 11-3/4"	7/16" OSB
	2' 0" x 8' 0" / 11-5/8"	7/16" OSB
		Flush

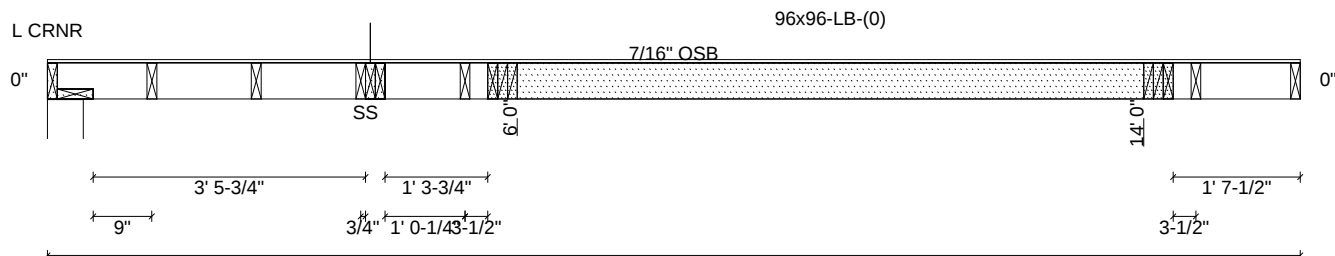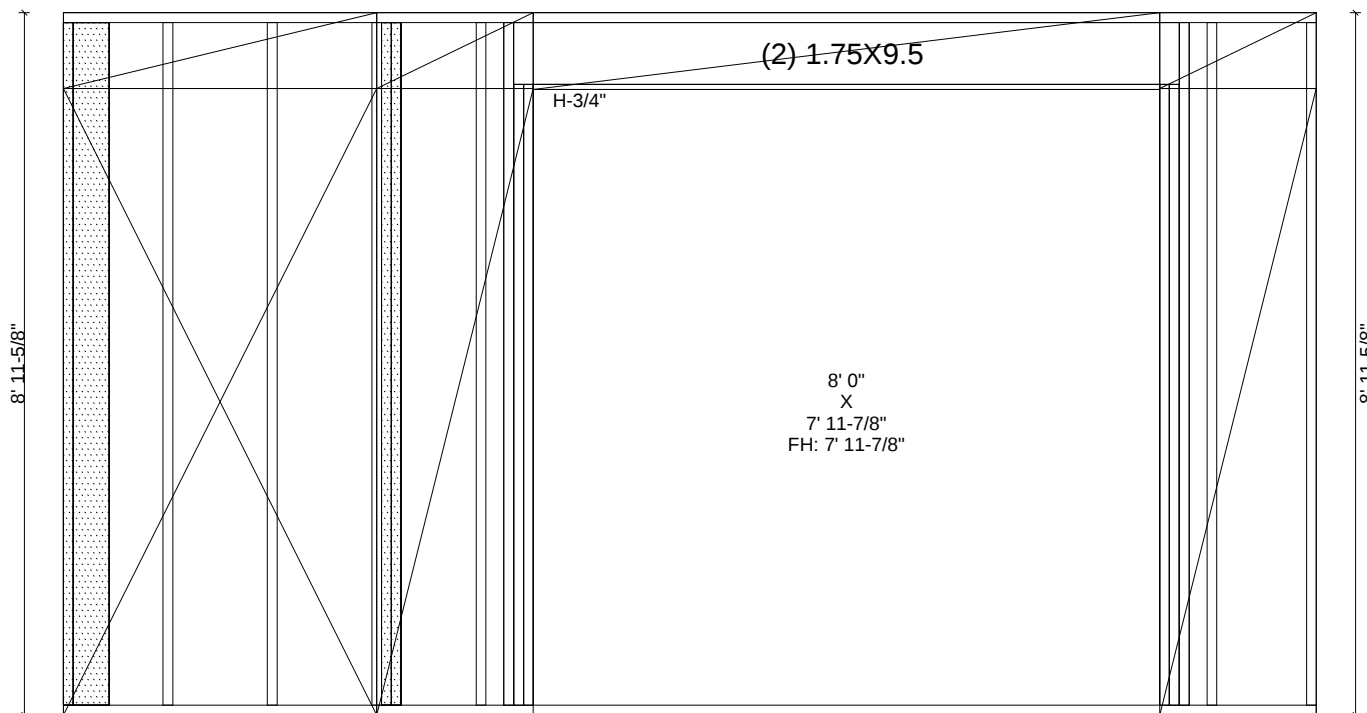

Panel Production Sheets

Job #Philis
Standard

Philis
Level 1

Date: 02/20/19
Page: 1
Bundle 4

Panel #84 (224.9 Bf)

Start Of Panel: 0"

Studs: 2X6 Sloped (#2 SPF & BTR) [2] 1' 4" o.c.

Top Plates: 2X6 (#2 SPF & BTR)

(1) 6' 4-1/8"

Start Rake Cut: 33.6 Deg /

End Rake Cut: 33.7 Deg /

TS: 6' 3-1/8"

(1) 5' 10-1/8"

Start Rake Cut: 123.7 Deg \

End Rake Cut: 123.7 Deg \

TS: 5' 9-1/8"

Bottom: (1) 2X6 x 10' 0" (#2 SPF & BTR)

Insert	Start	End
Dining-LB	1' 1"	9' 4"

Bottom Plate Lap: Flush

Start	Type	End
1' 1" x 8' 0"	7/16" OSB	

7/16" OSB	A: * 3' 1-11/16"	B: 8-11/16"
	C: * 3' 10-5/16"	D: N.A.
	E: 1' 1"	F: N.A.
	G: 1' 1"	H: N.A.

2' 6" Open

4-1/2" x 7' 0" 7/16" OSB

2' 6" Open

4-1/2" x 7' 0" 7/16" OSB

7/16" OSB	A: * 3' 10-5/16"	B: 1-11/16"
	C: * 4' 0"	D: N.A.
	E: 2-1/2"	F: 3' 11"
	G: 4' 1-1/2"	H: N.A.

7/16" OSB	A: N.A.	B: 2' 7-5/16"
	C: * 2' 7-5/16"	D: N.A.
	E: 3' 11"	F: N.A.
	G: 3' 11"	H: N.A.

7/16" OSB	A: * 4' 0"	B: N.A.
-----------	------------	---------

Panel Production Sheets

Job #Philis
Standard

Philis
Level 1

Date: 02/20/19
Page: 2
Bundle 4

C: * 3' 10-5/16"	D: 1-11/16"
E: 3' 11"	F: 2-1/2"
G: 4' 1-1/2"	H: N.A.

7/16" OSB

A: * 2' 7-5/16"	B: N.A.
C: N.A.	D: 2' 7-5/16"
E: 3' 11"	F: N.A.
G: N.A.	H: N.A.

4' 1-1/2" x 1' 0" 7/16" OSB
4' 1-1/2" x 1' 0" 7/16" OSB
8" x 8' 0" 7/16" OSB

7/16" OSB

A: * 3' 10-5/16"	B: N.A.
C: * 3' 5"	D: 5-5/16"
E: 8"	F: N.A.
G: 8"	H: N.A.

Flush

Quan.	Left Edge	Right Edge	Pitch (/12)	Angle	Top Plate Location	Bot. Plate Location
(1)	10' 10-3/8"	* 10' 11-3/8"	8.00	33.7	0"	0"
(1)	* 11' 2-11/16"	11' 1-11/16"	-8.00	-33.7	5' 7-5/16"	9' 10-1/2"

Panel #84 Continued Next Page


Panel Production Sheets

Job #Philis
Standard

Philis
Level 1

Date: 02/20/19
Page: 3
Bundle 4

Panel #84 (Continued)

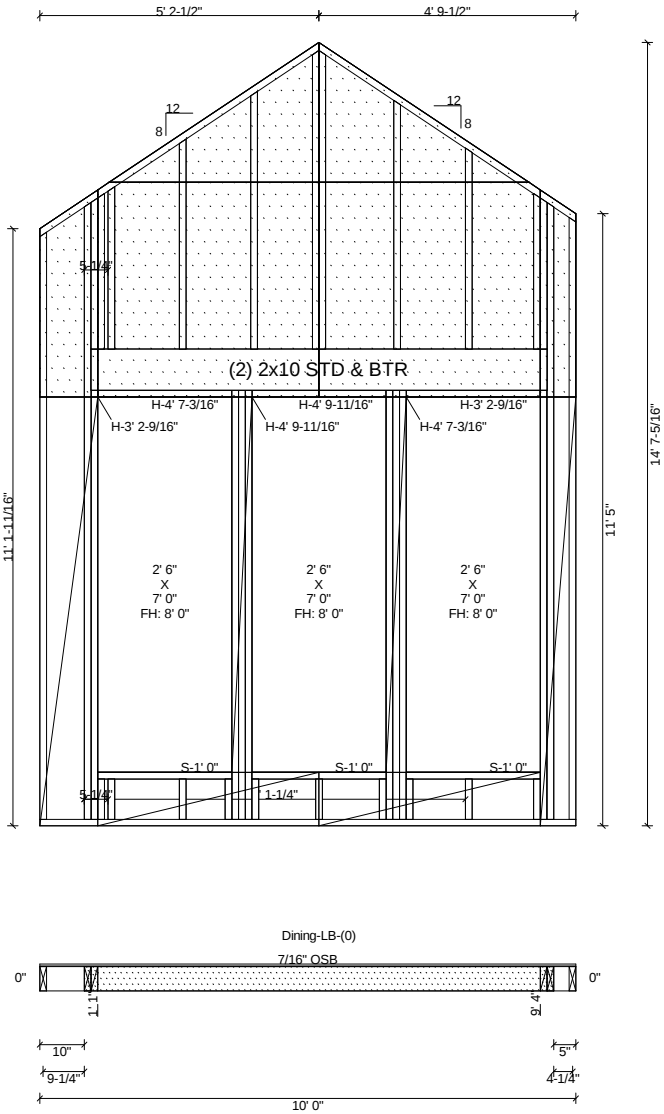

Panel Production Sheets

Job #Philis
Standard

Philis
Level 1

Date: 02/20/19
Page: 4
Bundle 4

Panel #83 (23.9 Bf)

Start Of Panel: 5-15/16"

Studs: 2X6 Sloped (#2 SPF & BTR) [2] 1' 4" o.c.

Top Plates: 2X6 (#2 SPF & BTR)

(1) 1' 8-1/4"

Start Rake Cut: 33.7 Deg /

End Rake Cut: 33.7 Deg /

TS: 1' 7-1/4"

Bottom: (1) 2X6 x 1' 4" (#2 SPF & BTR)

The stud located at 10-1/16" is omitted.

Bottom Plate Lap: Flush

Start Type End

Extend 5-15/16" 1' 9-15/16" x 8' 0" 7/16" OSB

7/16" OSB

A: * 1' 11-1/16"

B: 1' 2-5/8"

C: * 3' 1-11/16"

D: N.A.

E: 1' 9-15/16"

F: N.A.

G: 1' 9-15/16"



H: N.A.

Flush

Quan.	Left Edge	Right Edge	Pitch (/12)	Angle	Top Plate Location	Bot. Plate Location
(1)	9' 11-11/16"	* 10' 0-11/16"	8.00	33.7	0"	0"
(1)	10' 9-3/8"	* 10' 10-3/8"	8.00	33.7	1' 5-7/16"	1' 2-1/2"

Panel #83 Continued Next Page

Panel #83 (Continued)



Panel Production Sheets

Job #Philis
Standard

Philis
Level 1

Date: 02/20/19
Page: 6
Bundle 4

Panel #85 (35.4 Bf)

Start Of Panel: 0"

Studs: 2X6 Sloped (#2 SPF & BTR) [3] 1' 4" o.c.

Top Plates: 2X6 (#2 SPF & BTR)

(1) 2' 2-1/4"

Start Rake Cut: 123.7 Deg \

End Rake Cut: 123.7 Deg \

TS: 2' 1-1/4"

Bottom: (1) 2X6 x 1' 9" (#2 SPF & BTR)

Bottom Plate Lap: Flush

Start Type End

2' 2-15/16" x 8' 0" 7/16" OSB

7/16" OSB

A: * 3' 5"

B: N.A.

C: * 1' 11-1/16"

D: 1' 5-15/16"

E: 2' 2-15/16"

F: N.A.

G: 2' 2-15/16"



H: N.A.

Extend 5-15/16"

Quan.	Left Edge	Right Edge	Pitch (/12)	Angle	Top Plate Location	Bot. Plate Location
(1)	* 11' 1-11/16"	11' 0-11/16"	-8.00	-33.7	0"	0"
(1)	* 10' 3-1/2"	10' 2-1/2"	-8.00	-33.7	1' 6-5/16"	1' 3-1/4"
(1)	* 10' 0-11/16"	9' 11-11/16"	-8.00	-33.7	1' 11-7/16"	1' 7-1/2"

Panel #85 Continued Next Page

Panel #85 (Continued)



Panel Production Sheets

Job #Philis
Standard

Philis
Level 1

Date: 02/20/19
Page: 8
Bundle 4

Panel #25 (100.4 Bf)

Start Of Panel: 0"

Studs: 2X6 x 8' 8-5/8" (#2 SPF & BTR) [5] 1' 4" o.c.

(1) Top and (1) Bottom Plates: 2X6 x 7' 5-1/2" (#2 SPF & BTR)

*** Panel Diagonal 11' 8" ***

Insert	Start	End
* L CRNR(2X6) Up	@ Start	7"
L CRNR(2X6) Down *	6' 10-1/2"	@ End



Bottom Plate Lap: Flush

Start	Type	End
-------	------	-----

6-3/16" Open

3' 5-13/16" x 8' 0" / 11-5/8" 7/16" OSB

3' 5-1/2" x 8' 0" / 11-5/8" 7/16" OSB Flush

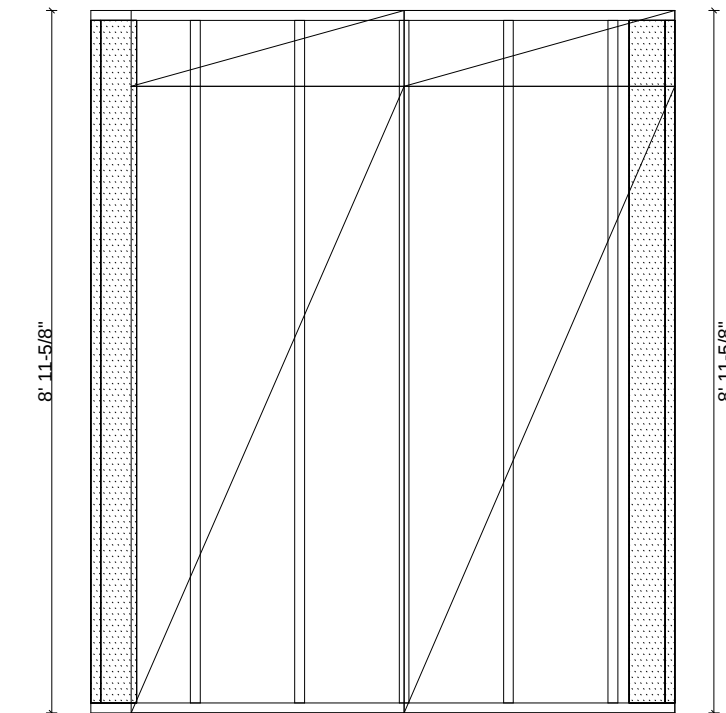

Panel Production Sheets

Job #Philis
Standard

Philis
Level 1

Date: 02/20/19
Page: 9
Bundle 4

Panel #27 (132.7 Bf)

Start Of Panel: 0"

Studs: 2X6 x 8' 8-5/8" (#2 SPF & BTR) [3] 1' 4" o.c.



(1) Top and (1) Bottom Plates: 2X6 x 9' 5-1/2" (#2 SPF & BTR)

*** Panel Diagonal 13' 0-7/16" ***

Insert	Start	End
* L CRNR(2X6) Down	@ Start	7"
entry-LB	11"	3' 9"
L CRNR(2X6) Up *	8' 10-1/2"	@ End

Bottom Plate Lap: Flush

Start	Type	End
Flush	11" x 8' 0" / 11-5/8" 7/16" OSB	
	2' 10" x 9-3/8" 7/16" OSB	
	2' 11" x 8' 0" / 11-5/8" 7/16" OSB	
	2' 3-5/16" x 8' 0" / 11-5/8" 7/16" OSB	
	6-3/16" Open	

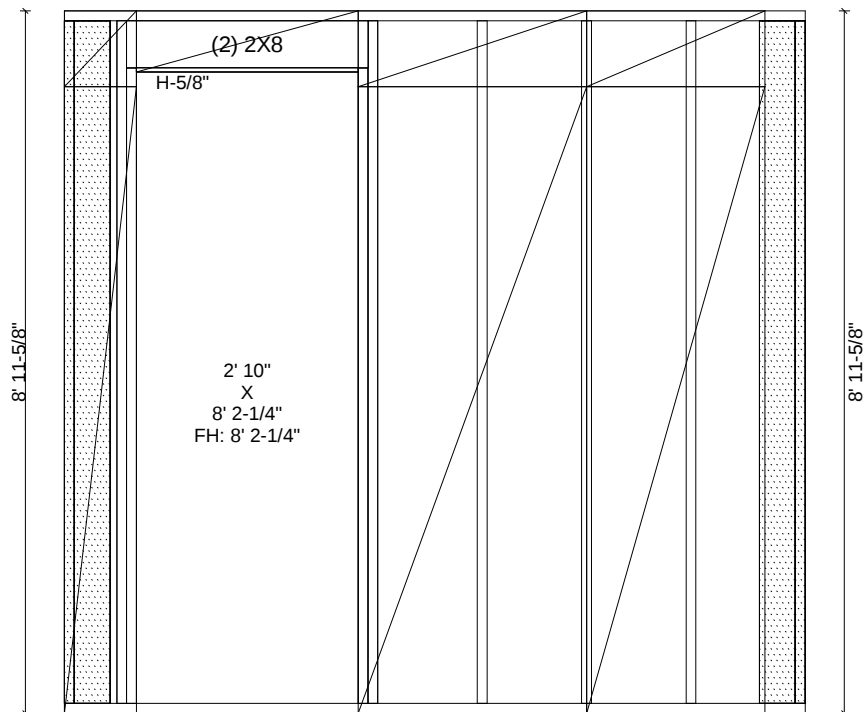

Panel Production Sheets

Job #Philis
Standard

Philis
Level 1

Date: 02/20/19
Page: 10
Bundle 4

Panel #28 (58.3 Bf)

Start Of Panel: 0"

Studs: 2X6 Sloped (#2 SPF & BTR) [4] 1' 4" o.c.

Top Plates: 2X6 (#2 SPF & BTR)

(1) 4' 3"

Start Rake Cut: 22.6 Deg /

End Rake Cut: 22.6 Deg /

TS: 4' 2-3/8"

Bottom: (1) 2X6 x 3' 10-1/2" (#2 SPF & BTR)

Bottom Plate Lap: Flush

Start Type End

Flush 3' 10-1/2" x 8' 0" 7/16" OSB

7/16" OSB

A: * 3' 11-1/2"

B: 1' 7-3/8"

C: * 5' 6-7/8"

D: N.A.

E: 3' 10-1/2"

F: N.A.

G: 3' 10-1/2"


H: N.A.

Flush

Quan.	Left Edge	Right Edge	Pitch (/12)	Angle	Top Plate Location	Bot. Plate Location
(1)	11' 8-3/8"	* 11' 9"	5.00	22.6	0"	0"
(1)	12' 2-3/4"	* 12' 3-3/8"	5.00	22.6	1' 4-1/2"	1' 3-1/4"
(1)	12' 9-3/8"	* 12' 10"	5.00	22.6	2' 9-7/8"	2' 7-1/4"
(1)	13' 3-1/8"	* 13' 3-3/4"	5.00	22.6	4' 0-3/4"	3' 9"

Panel #28 Continued Next Page

Panel #28 (Continued)

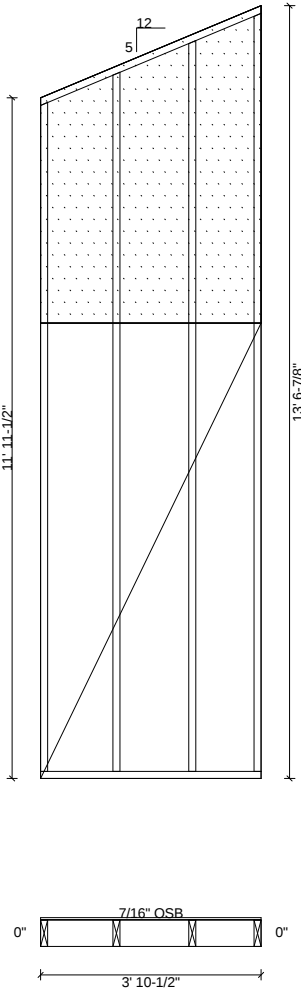

Panel Production Sheets

Job #Philis
Standard

Philis
Level 1

Date: 02/20/19
Page: 12
Bundle 4

Panel #30 (58.2 Bf)

Start Of Panel: 0"

Studs: 2X6 Sloped (#2 SPF & BTR) [4] 1' 4" o.c.

Top Plates: 2X6 (#2 SPF & BTR)

(1) 4' 3"

Start Rake Cut: 112.6 Deg \

End Rake Cut: 112.6 Deg \

TS: 4' 2-3/8"

Bottom: (1) 2X6 x 3' 10-1/2" (#2 SPF & BTR)

Bottom Plate Lap: Flush

Start Type End

3' 10-1/2" x 8' 0" 7/16" OSB

7/16" OSB

A: * 5' 6-7/8"

B: N.A.

C: * 3' 11-1/2"

D: 1' 7-3/8"

E: 3' 10-1/2"

F: N.A.

G: 3' 10-1/2"


H: N.A.

Flush

Quan.	Left Edge	Right Edge	Pitch (/12)	Angle	Top Plate Location	Bot. Plate Location
(1)	* 13' 3-3/4"	13' 3-1/8"	-5.00	-22.6	0"	0"
(1)	* 12' 9-3/8"	12' 8-3/4"	-5.00	-22.6	1' 4-1/2"	1' 3-1/4"
(1)	* 12' 2-3/4"	12' 2-1/8"	-5.00	-22.6	2' 9-7/8"	2' 7-1/4"
(1)	* 11' 9"	11' 8-3/8"	-5.00	-22.6	4' 0-3/4"	3' 9"

Panel #30 Continued Next Page

Panel #30 (Continued)

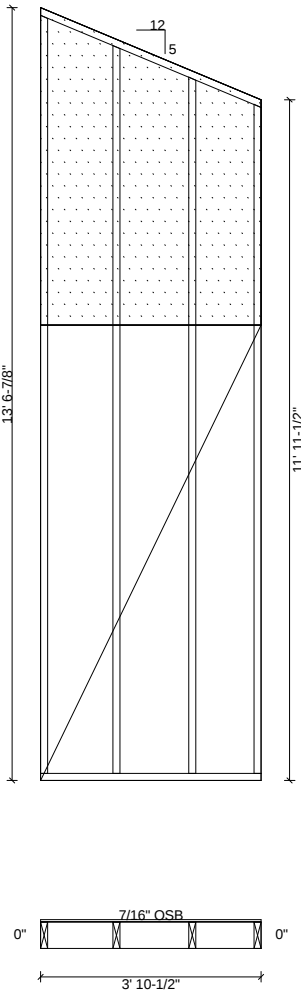

Panel Production Sheets

Job #Philis
Standard

Philis
Level 1

Date: 02/20/19
Page: 14
Bundle 4

Panel #29 (269.4 Bf)

Start Of Panel: 0"

Studs 2X6 x Neg 0" (#2 SPF & BTR) [0] 1' 4" o.c.

Top Plates: 2X6 (#2 SPF & BTR)

(1) 5' 7-1/4"

Start Rake Cut: 22.6 Deg /

End Rake Cut: 22.6 Deg /

TS: 5' 6-5/8"

(1) 5' 7-1/4"

Start Rake Cut: 112.6 Deg \

End Rake Cut: 112.6 Deg \

TS: 5' 6-5/8"

Bottom: (1) 2X6 x 10' 3" (#2 SPF & BTR)

Insert	Start	End
-----	-----	-----
36x84-LB	3"	10' 0"

Bottom Plate Lap: Flush

Start	Type	End
-----	-----	-----
3" x 8' 0"	7/16" OSB	

7/16" OSB	A: * 5' 6-7/8"	B: 1-1/4"
	C: * 5' 8-1/8"	D: N.A.
	E: 3"	F: N.A.
	G: 3"	H: N.A.

3' 0" Open

4-1/2" x 7' 0" 7/16" OSB

3' 0" Open

4-1/2" x 7' 0" 7/16" OSB

4' 10-1/2" x 4' 0" 7/16" OSB

7/16" OSB	A: * 1' 8-1/8"	B: 2' 0-3/8"
	C: * 3' 8-1/2"	D: N.A.
	E: 4' 10-1/2"	F: N.A.
	G: 4' 10-1/2"	H: N.A.

4' 10-1/2" x 4' 0" 7/16" OSB

7/16" OSB	A: * 3' 8-1/2"	B: N.A.
	C: * 1' 8-1/8"	D: 2' 0-3/8"
	E: 4' 10-1/2"	F: N.A.
	G: 4' 10-1/2"	H: N.A.

Date: 02/20/19
Page: 15
Bundle 4

Panel Production Sheets

Job #Philis
Standard

Philis
Level 1

Date: 02/20/19
Page: 1
Bundle 5

Panel #82 (159.5 Bf)

Start Of Panel: 0"

Studs: 2X6 x 9' 10-3/4" (#2 SPF & BTR) [5] 1' 4" o.c.

Top Plates: 2X6 (#2 SPF & BTR)

(1) 9' 11-5/8" TE \ 20.0 Deg

10' 1-5/8" LP

10' 1-5/8" BE

Bottom Plates: 2X6 (TREATED)

(1) 9' 11-5/8" TE \ 20.0 Deg

10' 1-5/8" LP

10' 1-5/8" BE

*** Panel Diagonal 14' 4-1/16" ***



Insert	Start	End
34x98-LB	3' 11-1/2"	6' 9-1/2"
SS	9' 8-5/8"	9' 11-5/8"
S	9' 10-13/16"	10' 0-5/16"

Bottom Plate Lap: Flush

Start	Type	End
3' 11-1/2" x 8' 0"	/ 2' 1-3/4"	7/16" OSB
2' 10" x 1' 11-1/2"	7/16" OSB	
3' 2-1/16" x 8' 0"	/ 2' 1-3/4"	7/16" OSB Hold 2-1/16"

Panel #82 Continued Next Page

Panel #82 (Continued)

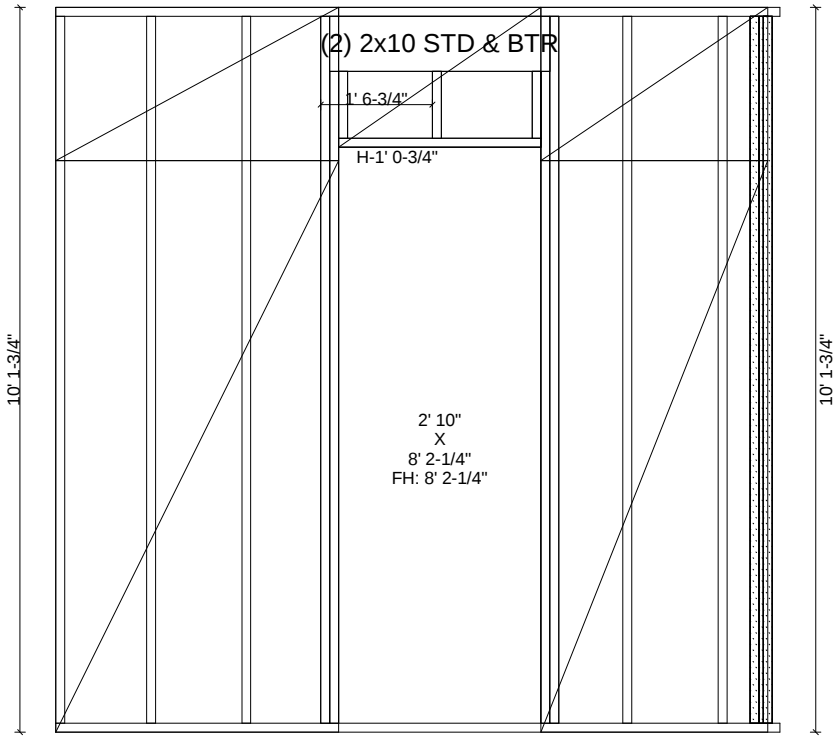

Panel Production Sheets

Job #Philis
Standard

Philis
Level 1

Date: 02/20/19
Page: 3
Bundle 5

Panel #81 (241.7 Bf)

Start Of Panel: 0"

Studs: 2X6 x 9' 10-3/4" (#2 SPF & BTR) [4] 1' 4" o.c.

Top Plates: (1) 2X6 x 12' 0" (#2 SPF & BTR)



Bottom: (1) 2X6 x 12' 0" (TREATED)

*** Panel Diagonal 15' 8-9/16" ***

Insert	Start	End
* L CRNR(2X6) Down	@ Start	7"
SS	2' 0-1/2"	2' 3-1/2"
72x24-LB	5' 2-3/4"	11' 2-3/4"

Bottom Plate Lap: Flush

Start	Type	End
Flush	2' 8" x 8' 0" / 2' 1-3/4" 7/16" OSB	
	2' 6-3/4" x 8' 0" / 2' 1-3/4" 7/16" OSB	
	6' 0" x 1' 11-5/8" 7/16" OSB	
	6' 0" x 4' 0" / 2' 2-1/8" 7/16" OSB	
	9-1/4" x 8' 0" / 2' 1-3/4" 7/16" OSB	Flush

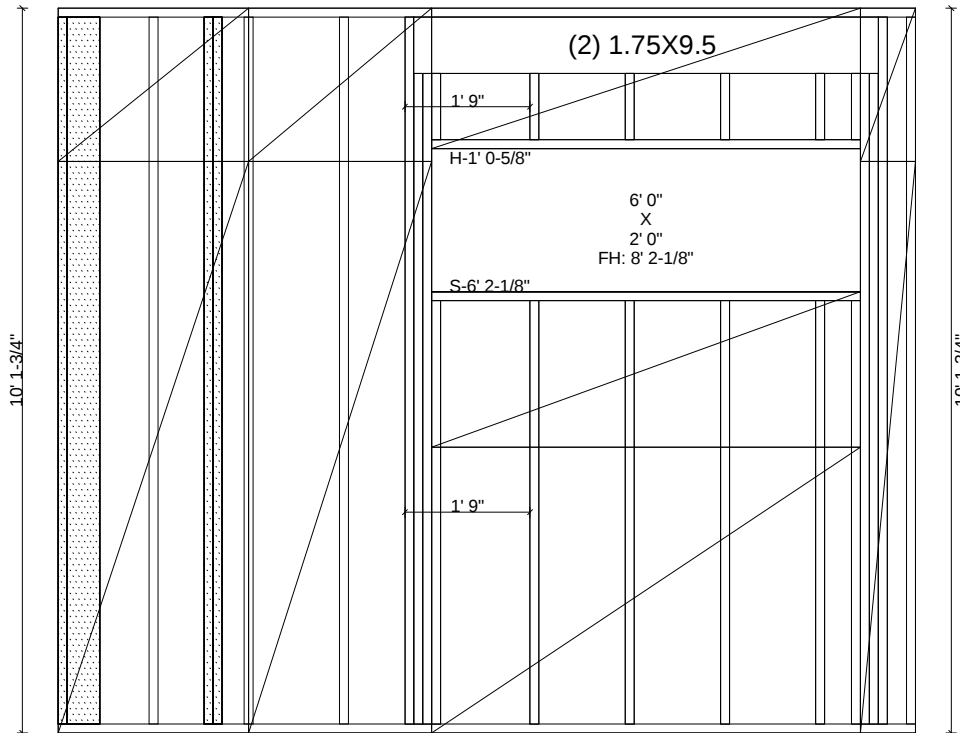

Panel Production Sheets

Job #Philis
Standard

Philis
Level 1

Date: 02/20/19
Page: 4
Bundle 5

Panel #79 (176.0 Bf)

Start Of Panel: 0"

Studs: 2X6 x 9' 10-3/4" (#2 SPF & BTR) [10] 1' 4" o.c.

Top Plates: (1) 2X6 x 12' 6" (#2 SPF & BTR)



Bottom: (1) 2X6 x 12' 6" (TREATED)

*** Panel Diagonal 16' 1-3/16" ***

Insert	Start	End
* L CRNR(2X6) Down SS	@ Start 4' 6-1/2"	7" 4' 9-1/2"

Bottom Plate Lap: Flush

Start	Type	End
Flush	4' 0" x 8' 0" / 2' 1-3/4" 7/16" OSB	
	4' 0" x 8' 0" / 2' 1-3/4" 7/16" OSB	
	2' 8" x 8' 0" / 2' 1-3/4" 7/16" OSB	
	1' 10" x 8' 0" / 2' 1-3/4" 7/16" OSB	Flush

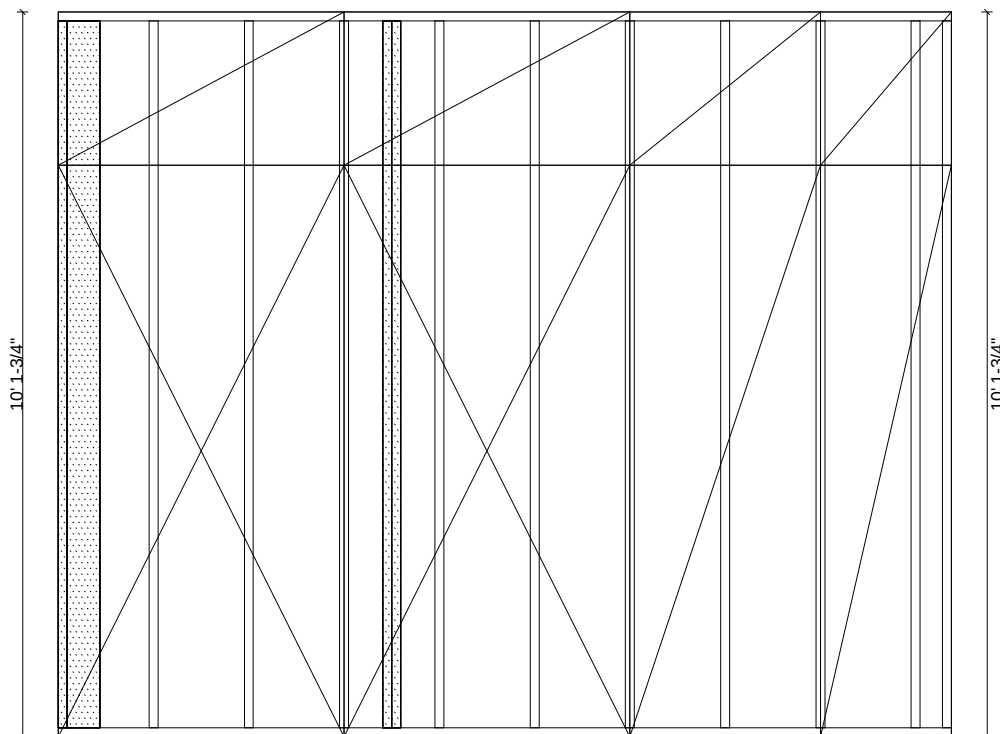

Panel Production Sheets

Job #Philis
Standard

Philis
Level 1

Date: 02/20/19
Page: 5
Bundle 5

Panel #80 (61.4 Bf)

Start Of Panel: 0"

Studs: 2X6 x 9' 10-3/4" (#2 SPF & BTR) [3] 1' 4" o.c.

Top Plates: (1) 2X6 x 4' 0" (#2 SPF & BTR)

Bottom: (1) 2X6 x 4' 0" (TREATED)



*** Panel Diagonal 10' 10-7/8" ***

Insert	Start	End
* L CRNR(2X6) Up	@ Start	7"

Bottom Plate Lap: Flush	Type	End
Start		

6-3/16" Open

3' 11-3/4" x 8' 0" / 2' 1-3/4" 7/16" OSB Extend 5-15/16"

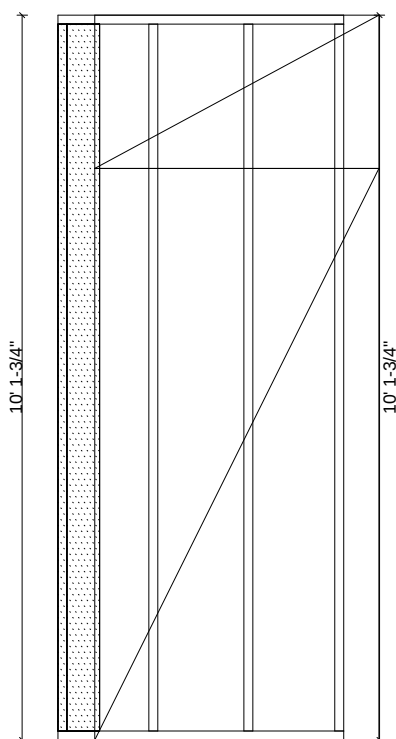

Panel Production Sheets

Job #Philis
Standard

Philis
Level 1

Date: 02/20/19
Page: 6
Bundle 5

Panel #78 (100.1 Bf)

Start Of Panel: 0"

Studs: 2X6 x 9' 10-3/4" (#2 SPF & BTR) [6] 1' 4" o.c.

Top Plates: (1) 2X6 x 7' 0" (#2 SPF & BTR)

Bottom: (1) 2X6 x 7' 0" (TREATED)

*** Panel Diagonal 12' 3-15/16" ***

Insert	Start	End
* L CRNR(2X6) Up	@ Start	7"



Bottom Plate Lap: Flush

Start	Type	End
-------	------	-----

6-3/16" Open

3' 5-13/16" x 8' 0" / 2' 1-3/4" 7/16" OSB

3' 5-15/16" x 8' 0" / 2' 1-3/4" 7/16" OSBExtend 5-15/16"

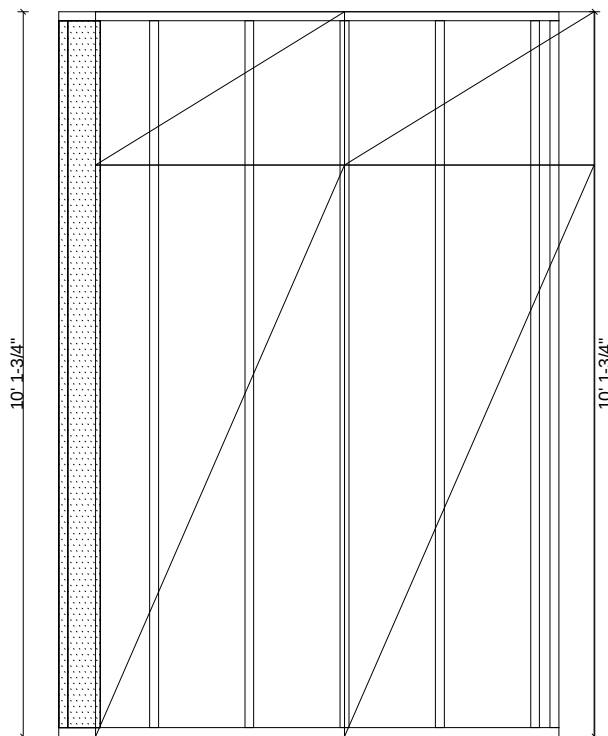

Panel Production Sheets

Job #Philis
Standard

Philis
Level 1

Date: 02/20/19
Page: 7
Bundle 5

Panel #76 (211.6 Bf)

Start Of Panel: 0"

Studs 2X6 x 9' 10-3/4" (#2 SPF & BTR) [0] 1' 4" o.c.

Top Plates: (1) 2X6 x 9' 0" (#2 SPF & BTR)

Bottom: (1) 2X6 x 9' 0" (TREATED)

*** Panel Diagonal 13' 6-3/4" ***

Insert	Start	End
* L CRNR(2X6) Down	0"	7"
garage-LB	1' 3"	7' 9"
L CRNR(2X6) Down *	8' 5"	9' 0"

Bottom Plate Lap: Flush

Start	Type	End
Flush	1' 3" x 8' 0" / 2' 1-3/4" 7/16" OSB	
	2' 0" Open	
	3" x 3' 6" 7/16" OSB	
	2' 0" Open	
	3" x 3' 6" 7/16" OSB	
	6' 6" x 3' 2-3/4" 7/16" OSB	
	6' 6" x 3' 5" 7/16" OSB	
	1' 3" x 8' 0" / 2' 1-3/4" 7/16" OSB	

Panel #76 Continued Next Page



Panel Production Sheets

Job #Philis
Standard

Philis
Level 1

Date: 02/20/19
Page: 8
Bundle 5

Panel #76 (Continued)

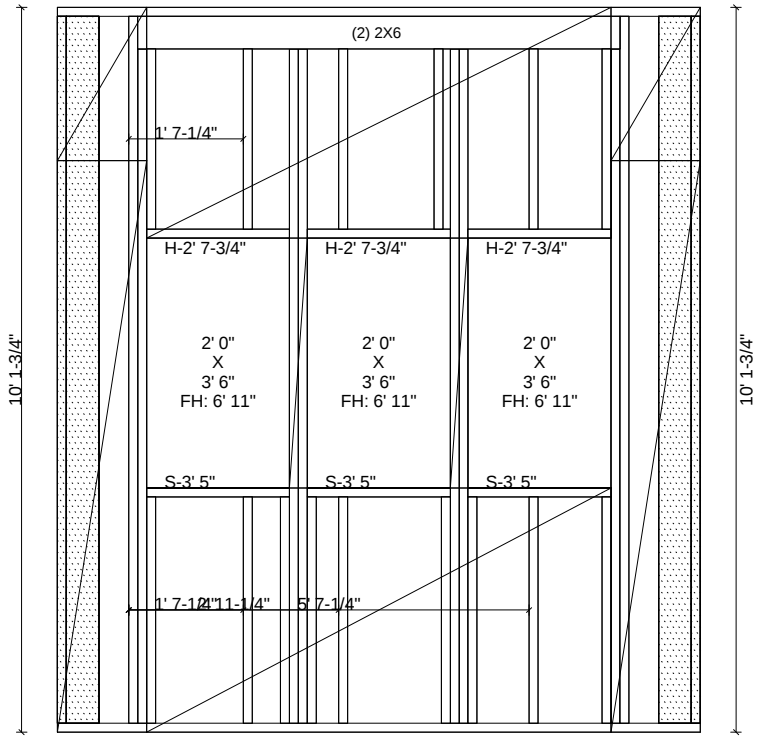

Panel Production Sheets

Job #Philis
Standard

Philis
Level 1

Date: 02/20/19
Page: 9
Bundle 5

Panel #77 (34.8 Bf)

Start Of Panel: 5-15/16"

Studs: 2X6 x 9' 10-3/4" (#2 SPF & BTR) [1] 1' 4" o.c.

Top Plates: (1) 2X6 x 1' 6-1/2" (#2 SPF & BTR)

Bottom: (1) 2X6 x 1' 6-1/2" (TREATED)



The stud located at 10-1/16" is omitted.

*** Panel Diagonal 10' 3-1/8" ***

Insert	Start	End
SS	1' 9-3/8"	2' 0-3/8"

Bottom Plate Lap: Flush

Start	Type	End
Extend 5-15/16"	2' 0-7/16" x 8' 0" / 2' 1-3/4"	7/16" OSB Flush



Panel Production Sheets

Job #Philis
Standard

Philis
Level 1

Date: 02/20/19
Page: 10
Bundle 5

Panel #75 (34.8 Bf)

Start Of Panel: 0"

Studs: 2X6 x 9' 10-3/4" (#2 SPF & BTR) [1] 1' 4" o.c.

Top Plates: (1) 2X6 x 1' 6-1/2" (#2 SPF & BTR)



Bottom: (1) 2X6 x 1' 6-1/2" (TREATED)

The stud located at 1' 4" is omitted.

*** Panel Diagonal 10' 3-1/8" ***

Insert	Start	End
SS	@ Start	3"

Bottom Plate Lap: Flush	Start	Type	End
Flush	2' 0-7/16" x 8' 0"	/ 2' 1-3/4"	7/16" OSB Extend 5-15/16"



Panel Production Sheets

Job #Philis
Standard

Philis
Level 1

Date: 02/20/19
Page: 11
Bundle 5

Panel #74 (130.7 Bf)

Start Of Panel: 0"

Studs: 2X6 x 9' 10-3/4" (#2 SPF & BTR) [5] 1' 4" o.c.

Top Plates: (1) 2X6 x 7' 5-1/2" (#2 SPF & BTR)



Bottom: (1) 2X6 x 7' 5-1/2" (TREATED)

*** Panel Diagonal 12' 7-1/8" ***

Insert	Start	End
* L CRNR(2X6) Down	@ Start	7"
SS	2' 9"	3' 0"
L CRNR(2X6) Up *	6' 10-1/2"	@ End

Bottom Plate Lap: Flush

Start	Type	End
Flush	4' 0" x 8' 0" / 2' 1-3/4" 7/16" OSB 2' 11-5/16" x 8' 0" / 2' 1-3/4" 7/16" OSB 6-3/16" Open	

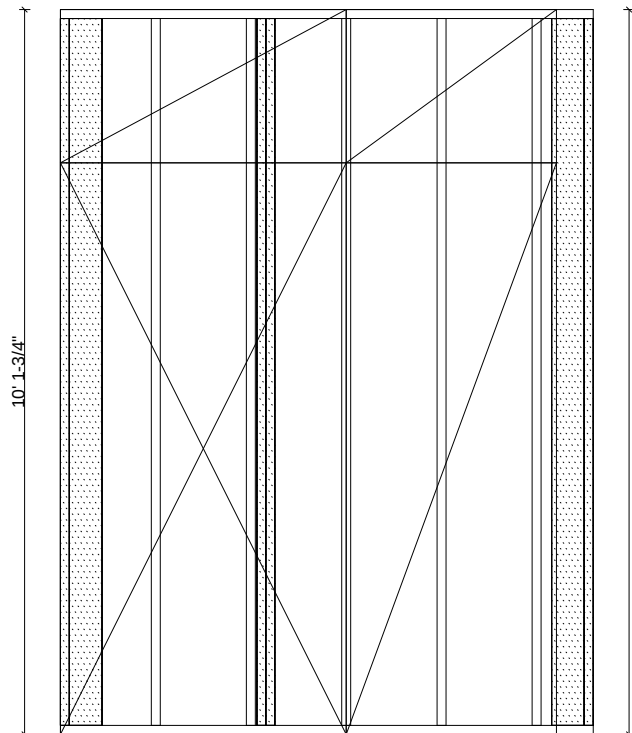

Panel Production Sheets

Job #Philis
Standard

Philis
Level 1

Date: 02/20/19
Page: 12
Bundle 5

Panel #72 (47.6 Bf)

Start Of Panel: 0"

Studs: 2X6 x 9' 10-3/4" (#2 SPF & BTR) [2] 1' 4" o.c.

Top Plates: (1) 2X6 x 2' 6-1/2" (#2 SPF & BTR)



Bottom: (1) 2X6 x 2' 6-1/2" (TREATED)

*** Panel Diagonal 10' 5-1/2" ***

Insert	Start	End
SS	@ Start	3"

Bottom Plate Lap: Flush

Start	Type	End
Flush	3' 0-7/16" x 8' 0" / 2' 1-3/4" 7/16" OSB Extend 5-15/16"	

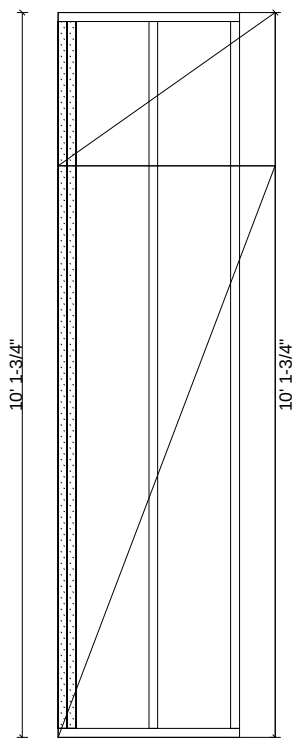

Panel Production Sheets

Job #Philis
Standard

Philis
Level 1

Date: 02/20/19
Page: 13
Bundle 5

Panel #73 (193.8 Bf)

Start Of Panel: 0"

Studs: 2X6 x 9' 10-3/4" (#2 SPF & BTR) [3] 1' 4" o.c.

Top Plates: (1) 2X6 x 12' 6-1/2" (#2 SPF & BTR)



Bottom: (1) 2X6 x 12' 6-1/2" (TREATED)

*** Panel Diagonal 16' 1-9/16" ***

Insert	Start	End
* L CRNR(2X6) Down 9x8-LB	@ Start 1' 10-1/2"	7" 11' 1-1/2"

Bottom Plate Lap: Flush

Start	Type	End
Flush	1' 10-1/2" x 8' 0" / 2' 1-3/4" 7/16" OSB 7' 5-1/2" x 2' 0-1/4" 7/16" OSB 1' 9-1/2" x 2' 0-1/4" 7/16" OSB 1' 10-15/16" x 8' 0" / 2' 1-3/4" 7/16" OSB	Extend 5-15/16"

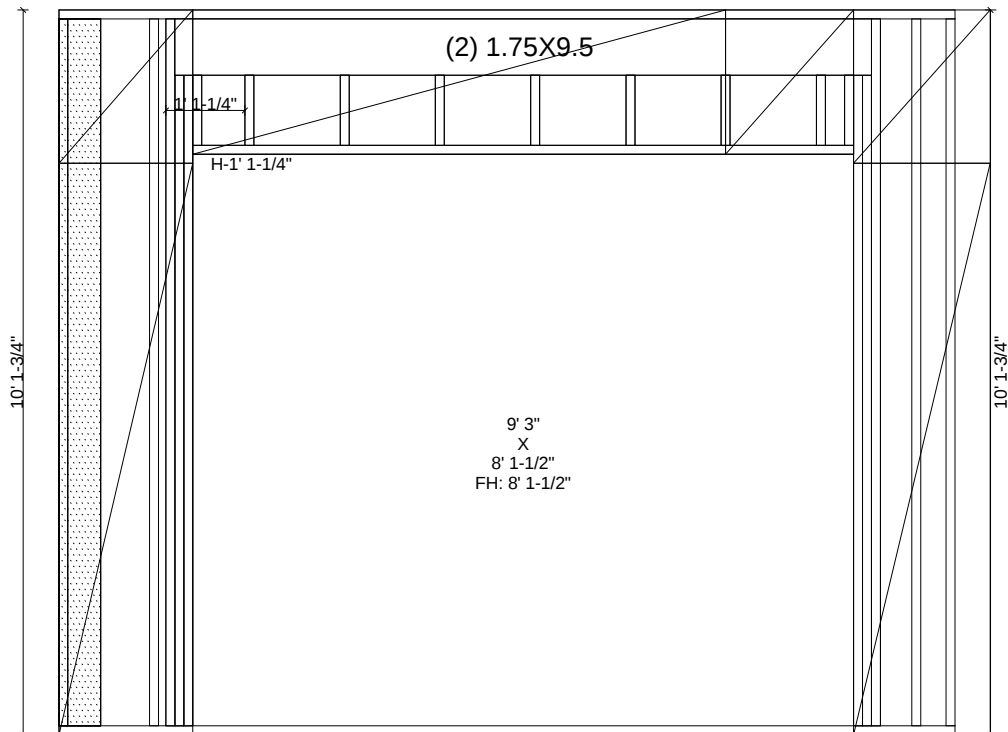

Panel Production Sheets

Job #Philis
Standard

Philis
Level 1

Date: 02/20/19
Page: 14
Bundle 5

Panel #71 (43.5 Bf)

Start Of Panel: 0"

Studs: 2X6 x 9' 10-3/4" (#2 SPF & BTR) [1] 1' 4" o.c.

Top Plates: (1) 2X6 x 1' 11-1/2" (#2 SPF & BTR)



Bottom: (1) 2X6 x 1' 11-1/2" (TREATED)

*** Panel Diagonal 10' 4" ***

Insert	Start	End
Loose Stud	7-11/16"	9-3/16"
L CRNR(2X6) Up *	1' 4-1/2"	@ End

Bottom Plate Lap: Flush

Start	Type	End
1' 5-5/16" x 8' 0"	/ 2' 1-3/4"	7/16" OSB Hold 6-3/16"

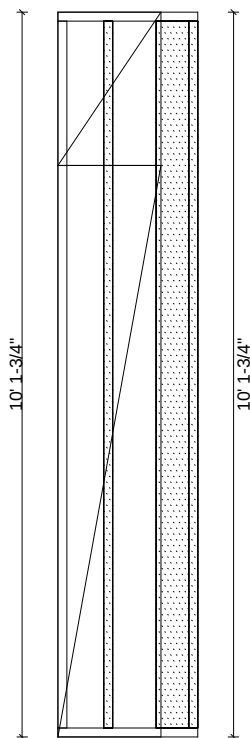

Panel Production Sheets

Job #Philis
Standard

Philis
Level 1

Date: 02/20/19
Page: 15
Bundle 5

Panel #70 (281.8 Bf)

Start Of Panel: 0"

Studs 2X6 x 9' 10-3/4" (#2 SPF & BTR) [0] 1' 4" o.c.

Top Plates: (1) 2X6 x 17' 3" (#2 SPF & BTR)



Bottom: (1) 2X6 x 17' 3" (TREATED)

*** Panel Diagonal 20' 0-1/8" ***

Insert	Start	End
16x8-LB	6"	16' 9"

Bottom Plate Lap: Flush

Start	Type	End
6" x 8' 0"	/ 2' 1-3/4"	7/16" OSB
7' 6" x 2' 0-1/4"		7/16" OSB
6' 8" x 2' 0-1/4"		7/16" OSB
2' 1" x 2' 0-1/4"		7/16" OSB
6" x 8' 0"	/ 2' 1-3/4"	7/16" OSB
		Flush

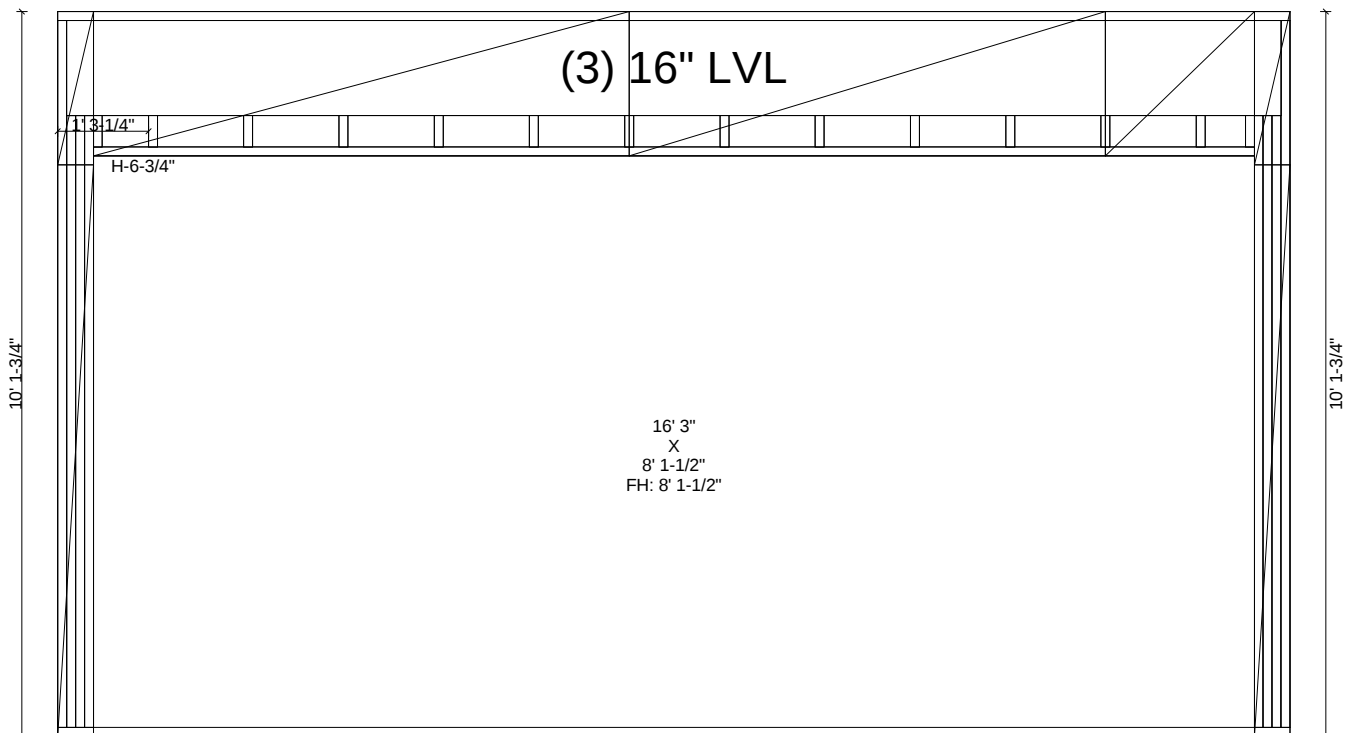

Panel Production Sheets

Job #Philis
Standard

Philis
Level 1

Date: 02/20/19
Page: 16
Bundle 5

Panel #69 (111.4 Bf)

Start Of Panel: 0"

Studs: 2X6 x 9' 10-3/4" (#2 SPF & BTR) [4] 1' 4" o.c.

10.0 Deg \ Top Plates: 2X6 (#2 SPF & BTR)
(1) 6' 11-13/16" TE
6' 11-13/16" LP
6' 10-13/16" BE
10.0 Deg \ Bottom Plates: 2X6 (TREATED)
(1) 6' 11-13/16" TE
6' 11-13/16" LP
6' 10-13/16" BE

The stud located at 6' 8" is omitted.

*** Panel Diagonal 12' 3-13/16" ***

Insert	Start	End
34x98-LB	3' 4-5/16"	6' 2-5/16"

Bottom Plate Lap: Flush

Start	Type	End
Flush	3' 4-5/16" x 8' 0" / 2' 1-3/4" 7/16" OSB 2' 10" x 1' 11-1/2" 7/16" OSB 9-1/2" x 8' 0" / 2' 1-3/4" 7/16" OSB	Flush

Panel #69 Continued Next Page



Panel Production Sheets

Job #Philis
Standard

Philis
Level 1

Date: 02/20/19
Page: 17
Bundle 5

Panel #69 (Continued)

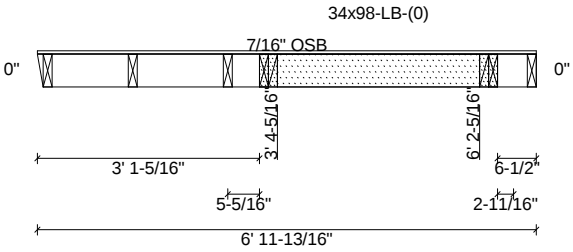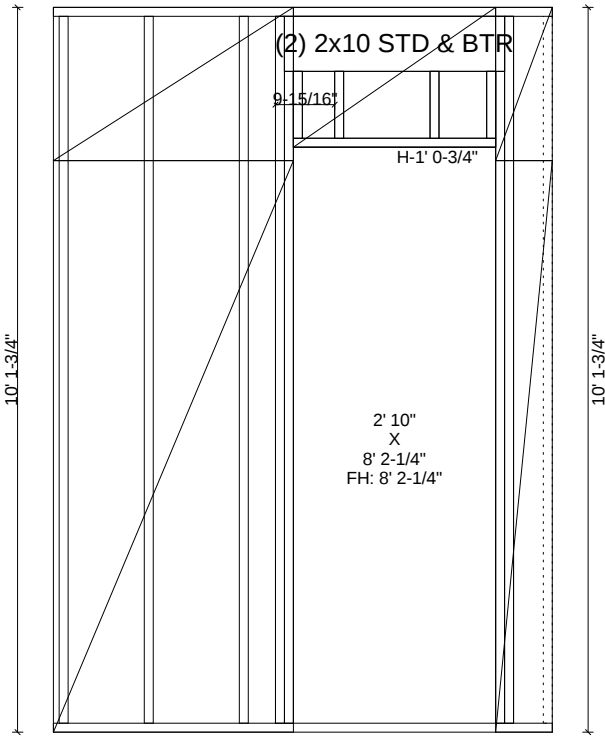

Panel Production Sheets

Job #Philis
Standard

Philis
Level 1

Date: 02/20/19
Page: 18
Bundle 5

Panel #68 (23.4 Bf)

Start Of Panel: 0"

Studs: 2X6 x 9' 10-3/4" (#2 SPF & BTR) [2] 1' 4" o.c.

Top Plates: 2X6 (#2 SPF & BTR)

(1) 1' 2-3/8" TE / 10.0 Deg

1' 2-3/8" LP

1' 1-3/8" BE

Bottom Plates: 2X6 (TREATED)

(1) 1' 2-3/8" TE / 10.0 Deg

1' 2-3/8" LP

1' 1-3/8" BE

*** Panel Diagonal 10' 2-9/16" ***

Bottom Plate Lap: Flush

Start Type End

Flush 1' 2-3/8" x 8' 0" / 2' 1-3/4" 7/16" OSB Flush

